




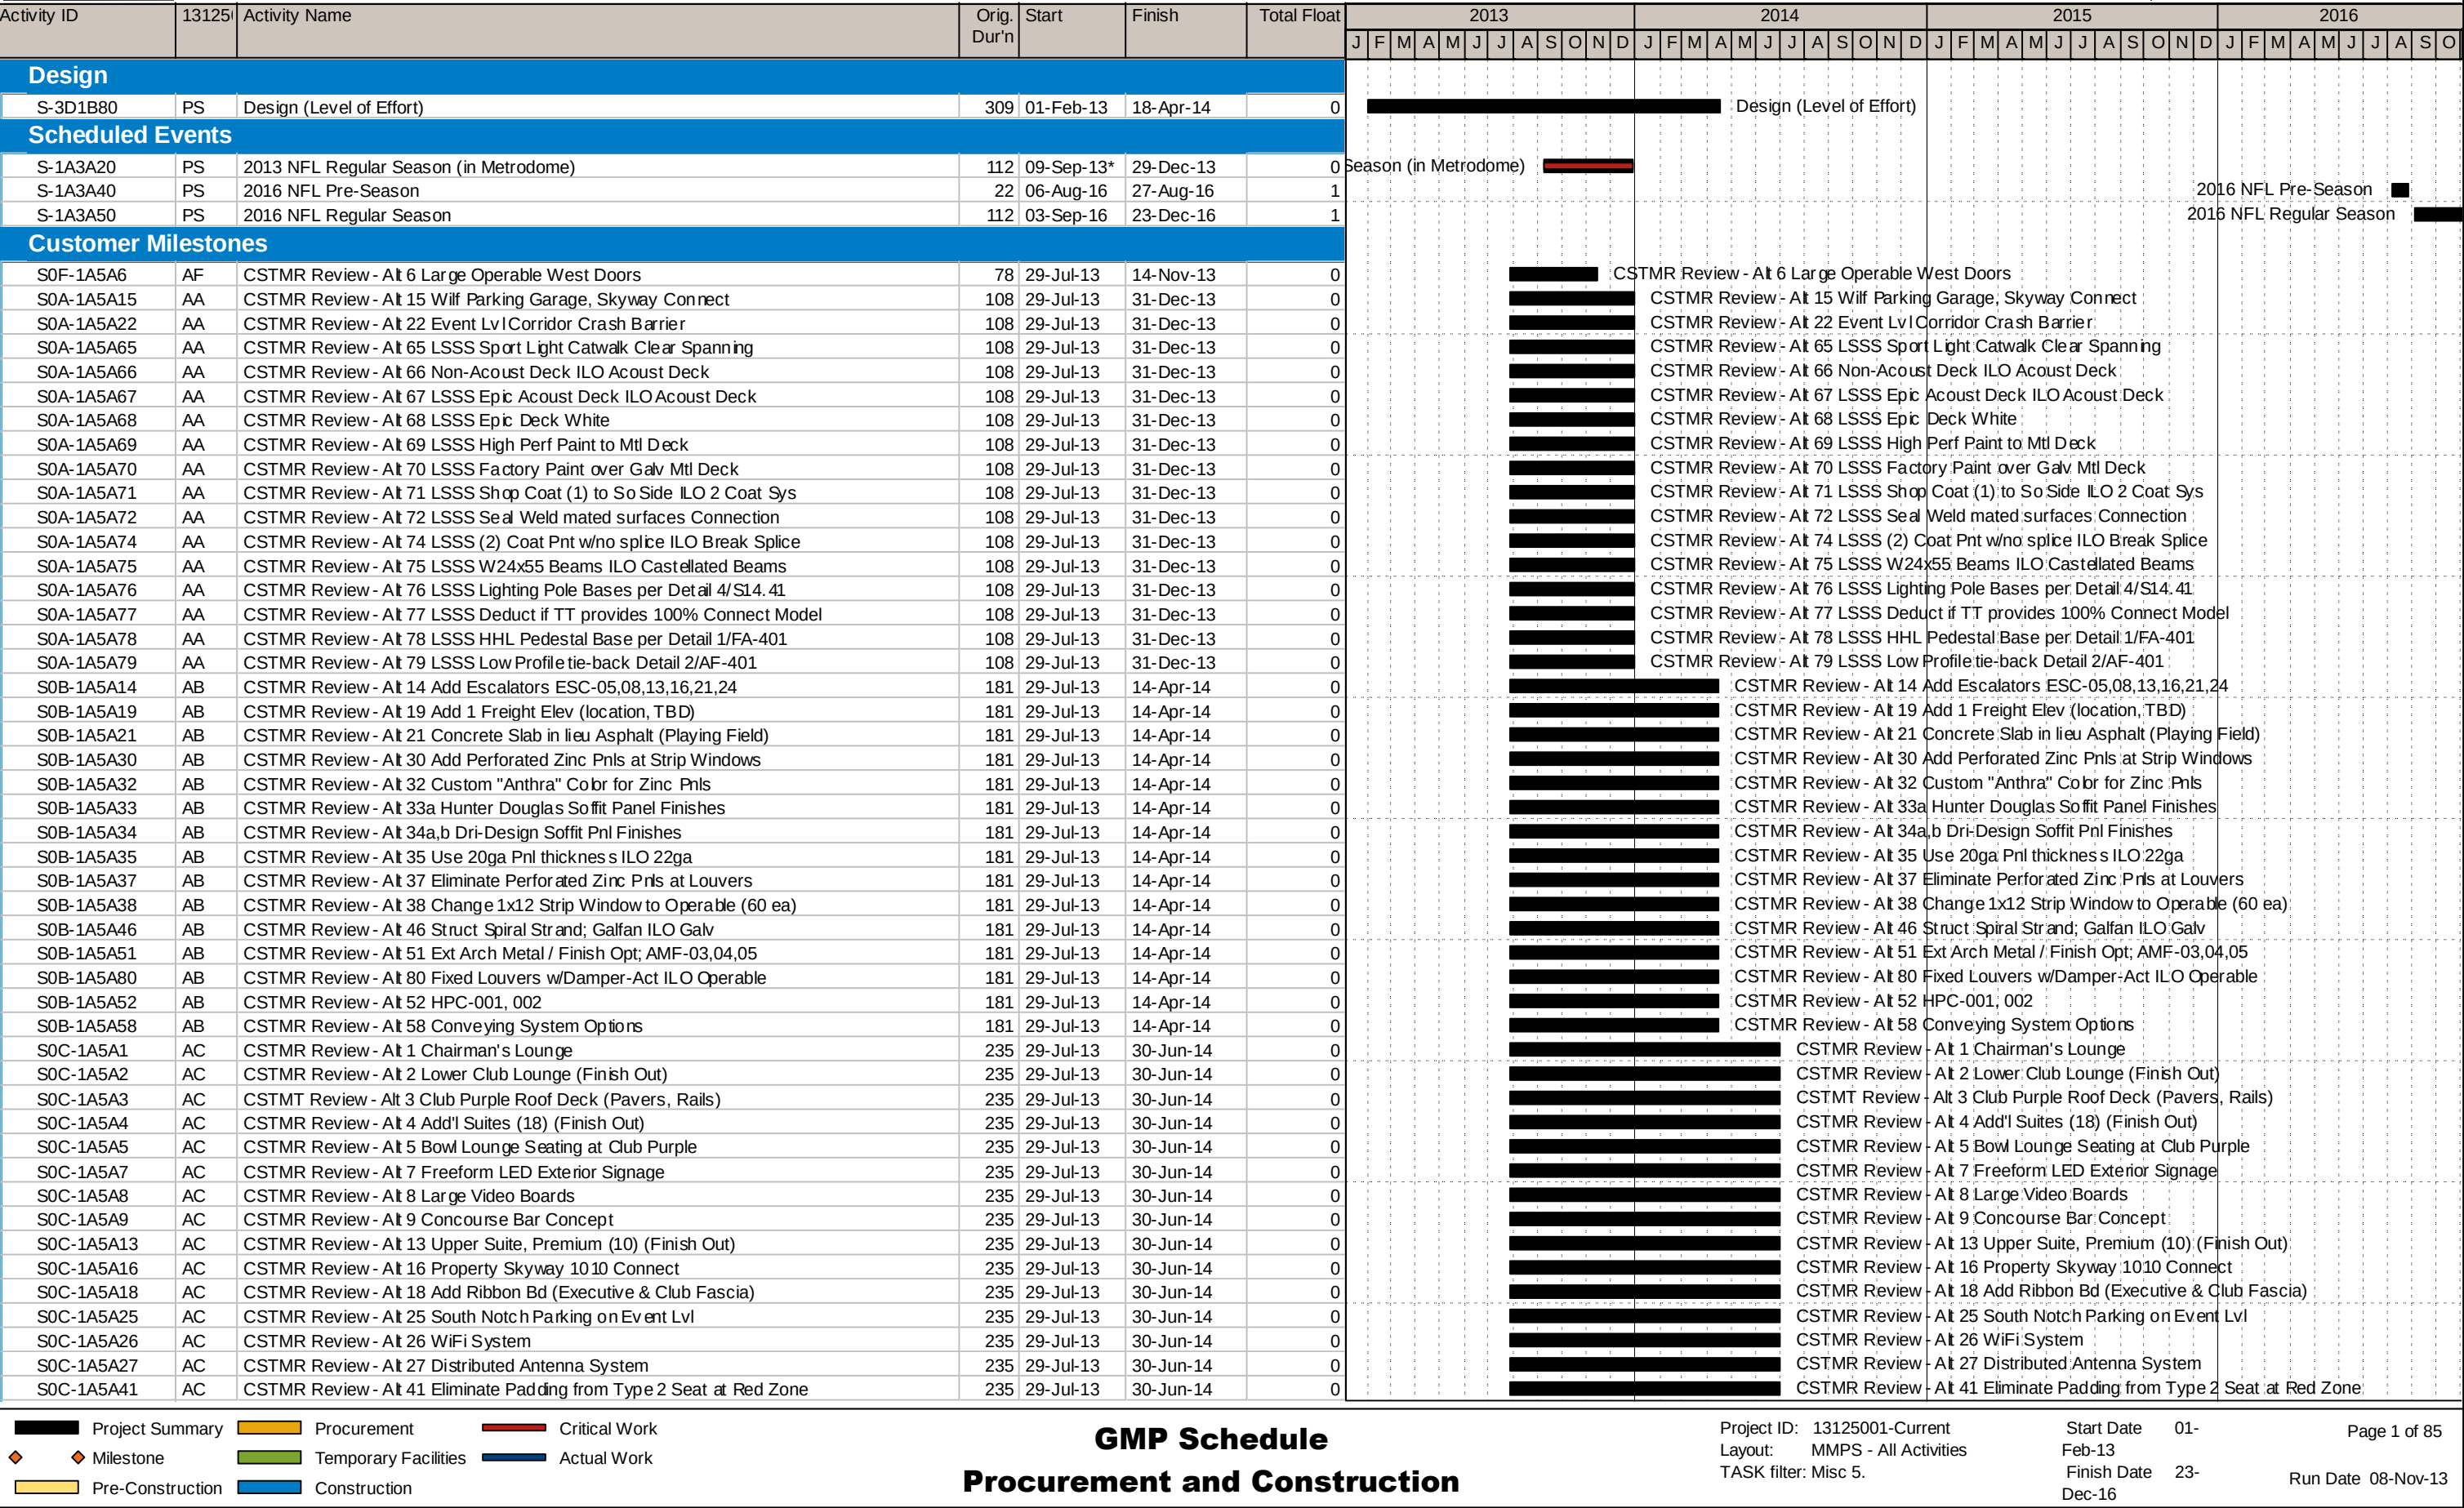

Minnesota Multi-Purpose Stadium

[illegible]

Project Summary
 Procurement
 Critical Work

Milestone
 Temporary Facilities
 Actual Work

Pre-Construction
 Construction

GMP Schedule

Procurement and Construction

Project ID: 13125001-Current
 Layout: MMPS - All Activities
 TASK filter: Misc 5.

Start Date 01-Feb-13
 Finish Date 23-Dec-16

Page 2 of 85
 Run Date 08-Nov-13



Minnesota Multi-Purpose Stadium



Activity ID	131251	Activity Name	Orig. Dur'n	Start	Finish	Total Float	2013												2014												2015												2016											
							J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D
S9D-1A5P1	D	Upper Ring Beam Complete - D-South West	0		21-Jul-15	0	21-Jul-15 ♦ Upper Ring Beam Complete - D-South West																																															
Mechanical/Electrical Milestones																																																						
S-1A5S1		Start Mech Room Rough-In	0	22-Sep-14		54	22-Sep-14, Start Mech Room Rough-In ♦																																															
S-1A5S7		Start M/E Systems Testing	0	13-Jan-16		6	13-Jan-16, Start M/E Systems Testing ♦																																															
Construction Complete																																																						
S-1A5X1	PM	Substantial Completion	0		15-Jul-16	1	15-Jul-16, Substantial Completion ♦																																															
Prepare Drawings																																																						
S0S-3D1B1	SD	Prepare 100% Schematic Design Documents	21	04-Feb-13	04-Mar-13	0	■ Prepare 100% Schematic Design Documents																																															
S0D-3D1B1	DD	Prepare 50% Design Development Documents	77	05-Mar-13	20-Jun-13	0	■ Prepare 50% Design Development Documents																																															
S0D-3D1B2	DD	Prepare 100% Design Development Documents	39	21-Jun-13	15-Aug-13	0	■ Prepare 100% Design Development Documents																																															
S0C-3D1C2	CD	Prepare Final CDs - Early Release Pkg -Area A Fnd/Deep Util	52	21-Jun-13	04-Sep-13	7	■ Prepare Final CDs - Early Release Pkg -Area A Fnd/Deep Util																																															
S0C-3D1C18	CD	Prepare Revised Final CDs - Early Release Pkg -Area A Fnd/Deep Util	25	05-Sep-13	09-Oct-13	7	■ Prepare Revised Final CDs - Early Release Pkg -Area A Fnd/Deep Util																																															
S0C-3D1C3	CD	Prepare Final CDs - Early Release Package -Area B,C,D,E,F Fnds	77	21-Jun-13	09-Oct-13	2	■ Prepare Final CDs - Early Release Package -Area B,C,D,E,F Fnds																																															
S0C-3D1C28	CD	Prepare Revised Final CDs - Early Release Pak -Area A,B,C,D,E,F Fnds	22	10-Oct-13	08-Nov-13	7	■ Prepare Revised Final CDs - Early Release Pak -Area A,B,C,D,E,F Fnds																																															
S0C-3D1C4	CD	Prepare Final CDs - Balance of Super Structure, Decks & Columns, Longspan Roof Perr	151	16-Aug-13	21-Mar-14	18	■ Prepare Final CDs - Balance of Super Structure, Decks & Columns, Longspan Roof Permit Issu																																															
S0C-3D1B2	CD	Prepare Final Construction Documents	53	05-Feb-14	18-Apr-14*	0	■ Prepare Final Construction Documents																																															
S0C-3D1C1	CD	Prepare Final CDs - Early Release Package - Mass Exc/Demo	39	21-Jun-13	15-Aug-13	0	■ Prepare Final CDs - Early Release Package - Mass Exc/Demo																																															
S0C1-3D1C4	CD	Prepare Final CDs - Executive Suite, Decks & Cols	80	16-Aug-13	10-Dec-13	0	■ Prepare Final CDs - Executive Suite, Decks & Cols																																															
S0C2-3D1C4	CD	Prepare Final CDs - Lower Club, Decks & Cols	80	16-Aug-13	10-Dec-13	0	■ Prepare Final CDs - Lower Club, Decks & Cols																																															
S0C3-3D1C4	CD	Prepare Final CDs - Main Concourse, Decks, Cols, Encl Steel ABs	95	16-Aug-13	02-Jan-14	0	■ Prepare Final CDs - Main Concourse, Decks, Cols, Encl Steel ABs																																															
S0C-3D1B1	CD	Prepare 50% Construction Documents	118	16-Aug-13	04-Feb-14	0	■ Prepare 50% Construction Documents																																															
S0C5-3D1C4	CD	Prepare Final CDs - Non Longspan Steel & Enclosure Grids 5.5 to 15.5	130	16-Aug-13	20-Feb-14	8	■ Prepare Final CDs - Non Longspan Steel & Enclosure Grids 5.5 to 15.5																																															
S0C6-3D1C4	CD	Prepare Documents- Skin Balance enough detail to bid	130	16-Aug-13	20-Feb-14	8	■ Prepare Documents- Skin Balance enough detail to bid																																															
S0C7-3D1C4	CD	Prepare Final CDs - Balance of Enclosure Documents	171	16-Aug-13	18-Apr-14	8	■ Prepare Final CDs - Balance of Enclosure Documents																																															
S0C-3D1C8	CD	Receive Signed CDs - Mass Exc/Demo	1	10-Oct-13	10-Oct-13	36	■ Receive Signed CDs - Mass Exc/Demo																																															
Prepare Structural Drawings																																																						
S0C-3D1C6	DD	Prepare Structural Steel Tekla Model for Mill Order - PH1 Gr 65	37	16-Aug-13	08-Oct-13	13	■ Prepare Structural Steel Tekla Model for Mill Order - PH1 Gr 65																																															
S0C-3D1C7	DD	Prepare Structural Steel Tekla Model for Mill Order - PH2 Gr 50	54	16-Aug-13	31-Oct-13	13	■ Prepare Structural Steel Tekla Model for Mill Order - PH2 Gr 50																																															
SR1-3D1C1	DD	Release TEKLA Model - Roof Steel Release 1	1	15-Nov-13	15-Nov-13	9	■ Release TEKLA Model - Roof Steel Release 1																																															
SR1-3D1C2	DD	Release TEKLA Model - Roof Steel Release 2	1	16-Dec-13	16-Dec-13	45	■ Release TEKLA Model - Roof Steel Release 2																																															
SR1-3D1C3	DD	Release TEKLA Model - Roof Steel Release 3	1	31-Jan-14	31-Jan-14	29	■ Release TEKLA Model - Roof Steel Release 3																																															
SR1-3D1C4	DD	Release TEKLA Model - Roof Steel Release 4	1	28-Feb-14	28-Feb-14	77	■ Release TEKLA Model - Roof Steel Release 4																																															
SR1-3D1C5	DD	Release TEKLA Model - Roof Steel Release 5	1	21-Apr-14	21-Apr-14	42	■ Release TEKLA Model - Roof Steel Release 5																																															
SR1-3D1C6	DD	Release TEKLA Model - Roof Steel Release 6	1	19-May-14	19-May-14	75	■ Release TEKLA Model - Roof Steel Release 6																																															
SR1-3D1C7	DD	Release TEKLA Model - Roof Steel Release 7	1	01-Jul-14	01-Jul-14	54	■ Release TEKLA Model - Roof Steel Release 7																																															
SR1-3D1C8	DD	Release TEKLA Model - Roof Steel Release 8	1	01-Aug-14	01-Aug-14	80	■ Release TEKLA Model - Roof Steel Release 8																																															
SR1-3D1C9	DD	Release TEKLA Model - Roof Steel Release 9	1	29-Aug-14	29-Aug-14	69	■ Release TEKLA Model - Roof Steel Release 9																																															
SX1-3D1C1	DD	Partial Cladding Steel TEKLA Model	1	20-Feb-14	20-Feb-14	8	■ Partial Cladding Steel TEKLA Model																																															
Budgeting and Estimating																																																						
S-3E1A1	CD	Prepare 50% DD Estimate	20	21-Jun-13	19-Jul-13	0	■ Prepare 50% DD Estimate																																															
S-3E1A2	CD	Review 50% DD Estimate	5	22-Jul-13	26-Jul-13	0	■ Review 50% DD Estimate																																															
Final GMP Estimate																																																						
S-3E1D	CD	Prepare GMP Pricing Package	63	17-May-13	15-Aug-13	0	■ Prepare GMP Pricing Package																																															
S-3E1D1	CD	Prepare GMP Estimate	49	16-Aug-13	24-Oct-13	0	■ Prepare																																															

Project Summary
 Procurement
 Critical Work

Milestone
 Temporary Facilities
 Actual Work

Pre-Construction
 Construction

GMP Schedule

Procurement and Construction

Project ID: 13125001-Current

Layout: MMPS - All Activities

TASK filter: Misc 5.

Start Date 01-Feb-13

Finish Date 23-Dec-16

Page 3 of 85

Run Date 08-Nov-13



Minnesota Multi-Purpose Stadium

[illegible]

Project Summary

Procurement

Critical Work

Pre-Construction

Temporary Facilities

Actual Work

Construction

GMP Schedule

Procurement and Construction

Project ID: 13125001-Current

Layout: MMPS - All Activities

TASK filter: Misc 5.

Start Date 01-Feb-13

Finish Date 23-Dec-16

Page 4 of 85

Run Date 08-Nov-13



Minnesota Multi-Purpose Stadium

[illegible]

Project Summary

Procurement

Critical Work

Milestone

Temporary Facilities

Actual Work

Pre-Construction

Construction

GMP Schedule

Procurement and Construction

Project ID: 13125001-Current
 Layout: MMPS - All Activities
 TASK filter: Misc 5.

Start Date 01-Feb-13
 Finish Date 23-Dec-16

Page 5 of 85
 Run Date 08-Nov-13



Minnesota Multi-Purpose Stadium



Activity ID	131251	Activity Name	Orig. Dur'n	Start	Finish	Total Float	2013												2014												2015												2016											
							J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O		
S1A-6L7C1	A	Backfill/Grade Temp Road into - Event A (NE)	5	03-Mar-14	07-Mar-14	2	█ Backfill/Grade Temp Road into - Event A (NE)																																															
Demolish Existing Facilities																																																						
S013E-4H2B2	AT.5	Evaluate Bids & Select Contractor - Demolition	18	18-Sep-13	11-Oct-13	9	█ Evaluate Bids & Select Contractor - Demolition																																															
S013E-4H2A2	AT.5	Solicit Pricing - Demolition	22	16-Aug-13	17-Sep-13	9	█ Solicit Pricing - Demolition																																															
S013E-4H2B3	AT.5	Confirm Pricing - Demolition	10	11-Oct-13	24-Oct-13	0	█ Confirm Pricing - Demolition																																															
S013E-4H2B4	AT.5	Award Contract - Demolition	1	18-Nov-13	18-Nov-13	35	Award Contract - Demolition																																															
S00-5M1DS	PR	Prepare Submittals - Demolition	20	14-Oct-13	08-Nov-13	16	█ Prepare Submittals - Demolition																																															
S00-5M1DR	PR	Submit - Demolition Submittal	1	11-Nov-13	11-Nov-13	16	Submit - Demolition Submittal																																															
S00-5M1DA	PR	Approve Submittals - Demolition	10	12-Nov-13	25-Nov-13	16	█ Approve Submittals - Demolition																																															
S00-5M1DB	PR	3rd Party Review Submtl - Demolition	10	12-Nov-13	25-Nov-13	16	█ 3rd Party Review Submtl - Demolition																																															
S00-5M1	Site	Mobilize - Demolition	5	13-Jan-14	17-Jan-14	0	█ Mobilize - Demolition																																															
Demolition																																																						
D00-8M1A1	Site	Vacate Building - Metro Dome	10	02-Jan-14	15-Jan-14	0	█ Vacate Building - Metro Dome																																															
D00-8M1D1	Site	Disconnect Util / Deflate Roof - Metro Dome	2	16-Jan-14	17-Jan-14	0	Disconnect Util / Deflate Roof - Metro Dome																																															
D00-8M1D	Site	Demolish Existing Facilities - Loading Dock	15	20-Jan-14	07-Feb-14	0	█ Demolish Existing Facilities - Loading Dock																																															
D00-8M1D10	Site	Demolish Existing Facilities - Roof	15	20-Jan-14	07-Feb-14	0	█ Demolish Existing Facilities - Roof																																															
D00-8M1D20	Site	Demolish Existing Facilities - Quad NE	21	03-Feb-14	03-Mar-14	0	█ Demolish Existing Facilities - Quad NE																																															
D00-8M1D30	Site	Demolish Existing Facilities - Quad SE	22	25-Feb-14	26-Mar-14	1	█ Demolish Existing Facilities - Quad SE																																															
D00-8M1D50	Site	Demolish Existing Facilities - Quad NW	22	21-Mar-14	21-Apr-14	4	█ Demolish Existing Facilities - Quad NW																																															
D00-8M1D40	Site	Demolish Existing Facilities - Quad SW	22	16-Apr-14	15-May-14	41	█ Demolish Existing Facilities - Quad SW																																															
Excavation																																																						
S023E-1A5L3	AT.6	CSTMR Issue limited NTP - Ret Wall Design	0	18-Nov-13		0	18-Nov-13, ◆																																															
S023E-4H2B2	AT.6	Evaluate Bids & Select Contractor - Earthwork / Retention	18	18-Sep-13	11-Oct-13	9	█ Evaluate Bids & Select Contractor - Earthwork / Retention																																															
S023E-4H2A2	AT.6	Solicit Pricing - Earthwork / Retention	22	16-Aug-13	17-Sep-13	9	█ Solicit Pricing - Earthwork / Retention																																															
S023E-4H2B3	AT.6	Confirm Pricing - Earthwork / Retention	10	11-Oct-13	24-Oct-13	0	█ Confirm Pricing - Earthwork / Retention																																															
S023E-4H2B4	AT.6	Award Contract - Earthwork / Retention	1	18-Nov-13	18-Nov-13	8	Award Contract - Earthwork / Retention																																															
Earth Retention Systems																																																						
D00-4H2A2		Solicit Pricing - Earthwork/Retention - XCEL Work	8	05-Jul-13*	16-Jul-13	0	█ Solicit Pricing - Earthwork/Retention - XCEL Work																																															
D00-4H2B2		Evaluate Bids & Select Contractor - Earth/Retention -XCEL	8	17-Jul-13	26-Jul-13	9	█ Evaluate Bids & Select Contractor - Earth/Retention -XCEL																																															
S1A-5M4A1	A	Design Earth Ret Wall - Temp "J" Area A (NE)	8	18-Nov-13	27-Nov-13	0	█ Design Earth Ret Wall - Temp "J" Area A (NE)																																															
S1A-5M4AF	A	Fab/Deliver Earth Ret Wall - Temp "J" Area A (NE)	8	02-Dec-13	11-Dec-13	0	█ Fab/Deliver Earth Ret Wall - Temp "J" Area A (NE)																																															
S1F1-5M4A1	F	Design Earth Ret Wall - Permanent "A1" Area F (SE)	8	18-Nov-13	27-Nov-13	0	█ Design Earth Ret Wall - Permanent "A1" Area F (SE)																																															
S1F1-5M4AS	F	Prepare Submtls Earth Ret Wall - Permanent "A1" Area F (SE)	5	02-Dec-13	06-Dec-13	5	Prepare Submtls Earth Ret Wall - Permanent "A1" Area F (SE)																																															
S1F1-5M4AR	F	Mort Rev/Submit Earth Ret Wall - Permanent "A1" Area F (SE)	1	09-Dec-13	09-Dec-13	5	Mort Rev/Submit Earth Ret Wall - Permanent "A1" Area F (SE)																																															
S1F1-5M4AA	F	Approve Earth Ret Wall - Permanent "A1" Area F1 (SE)	10	10-Dec-13	23-Dec-13	5	█ Approve Earth Ret Wall - Permanent "A1" Area F1 (SE)																																															
S1F1-5M4AB	F	3rd Party Rev Submtl - Permanent "A1" Area F (SE)	10	10-Dec-13	23-Dec-13	5	█ 3rd Party Rev Submtl - Permanent "A1" Area F (SE)																																															
S1F1-5M4AD	F	Distribute Submtl Earth Ret Wall - Permanent "A1" Area F (SE)	1	24-Dec-13	24-Dec-13	5	Distribute Submtl Earth Ret Wall - Permanent "A1" Area F (SE)																																															
S1F1-5M4AF	F	Fab/Deliver Earth Ret Wall - Permanent "A1" Area F (SE)	10	26-Dec-13	09-Jan-14	5	█ Fab/Deliver Earth Ret Wall - Permanent "A1" Area F (SE)																																															
S1F2-5M4A1	F	Design Earth Ret Wall - Permanent "A2" Area F (SE)	10	02-Dec-13	13-Dec-13	0	█ Design Earth Ret Wall - Permanent "A2" Area F (SE)																																															
S1F2-5M4AS	F	Prepare Submtls Earth Ret Wall - Permanent "A2" Area F (SE)	5	16-Dec-13	20-Dec-13	0	Prepare Submtls Earth Ret Wall - Permanent "A2" Area F (SE)																																															
S1F2-5M4AR	F	Mort Rev/Submit Earth Ret Wall - Permanent "A2" Area F (SE)	1	23-Dec-13	23-Dec-13	0	Mort Rev/Submit Earth Ret Wall - Permanent "A2" Area F (SE)																																															
S1F2-5M4AA	F	Approve Earth Ret Wall - Permanent "A2" Area F1 (SE)	10	24-Dec-13	08-Jan-14	0	█ Approve Earth Ret Wall - Permanent "A2" Area F1 (SE)																																															
S1F2-5M4AB	F	3rd Party Rev Submtl - Permanent "A2" Area F (SE)	10	24-Dec-13	08-Jan-14	0	█ 3rd Party Rev Submtl - Permanent "A2" Area F (SE)																																															
S1F2-5M4AD	F	Distribute Submtl Earth Ret Wall - Permanent "A2" Area F (SE)	1	09-Jan-14	09-Jan-14	0	Distribute Submtl Earth Ret Wall - Permanent "A2" Area F (SE)																																															
S1F2-5M4AF	F	Fab/Deliver Earth Ret Wall - Permanent "A2" Area F (SE)	10	10-Jan-14	23-Jan-14	0	█ Fab/Deliver Earth Ret Wall - Permanent "A2" Area F (SE)																																															
S1F-5M4A1	F	Design Earth Ret Wall - Temp "D" Area F (SE)	10	02-Dec-13	13-Dec-13	18	█ Design Earth Ret Wall - Temp "D" Area F (SE)																																															
S1F-5M4AF	F	Fab/Deliver Earth Ret Wall - Temp "D" Area F (SE)	5	16-Dec-13	20-Dec-13	18	█ Fab/Deliver Earth Ret Wall - Temp "D" Area F (SE)																																															
S1B-5M4A1	B	Design Earth Ret Wall - Temp "G" Area B (North)	10	16-Dec-13	30-Dec-13	36	█ Design Earth Ret Wall - Temp "G" Area B (North)																																															
S1B-5M4AF	B	Fab/Deliver Earth Ret Wall - Temp "G" Area B (North)	8	31-Dec-13	10-Jan-14	36	█ Fab/Deliver Earth Ret Wall - Temp "G" Area B (North)																																															
S1E1-5M4A1	E	Design Earth Ret Wall - Permanent "B" Area E (South)	10	16-Dec-13	30-Dec-13	20	█ Design Earth Ret Wall - Permanent "B" Area E (South)																																															
S1E1-5M4AS	E	Prepare Submtls Earth Ret Wall - Permanent "B" Area E (South)	5	31-Dec-13	07-Jan-14	20	█ Prepare Submtls Earth Ret Wall - Permanent "B" Area E (South)																																															
S1E1-5M4AR	E	Mort Rev/Submit Earth Ret Wall - Permanent "B" Area E (South)	1	08-Jan-14	08-Jan-14	20	Mort Rev/Submit Earth Ret Wall - Permanent "B" Area E (South)																																															
S1E1-5M4AA	E	Approve Earth Ret Wall - Permanent "B" Area E (South)	10	09-Jan-14	22-Jan-14	20	█ Approve Earth Ret Wall - Permanent "B" Area E (South)																																															

Project Summary

Procurement

Critical Work

Pre-Construction

Temporary Facilities

Actual Work

Milestone

Construction

GMP Schedule

Procurement and Construction

Project ID: 13125001-Current

Layout: MMPS - All Activities

TASK filter: Misc 5.

Start Date 01-Feb-13

Finish Date 23-Dec-16

Page 6 of 85

Run Date 08-Nov-13



Minnesota Multi-Purpose Stadium

[illegible]

Project Summary

Procurement

Critical Work

Temporary Facilities

Actual Work

Pre-Construction

Construction

GMP Schedule

Procurement and Construction

Project ID: 13125001-Current

Layout: MMPS - All Activities

TASK filter: Misc 5.


Start Date 01-Feb-13

Finish Date 23-Dec-16

Page 7 of 85

Run Date 08-Nov-13

[illegible]

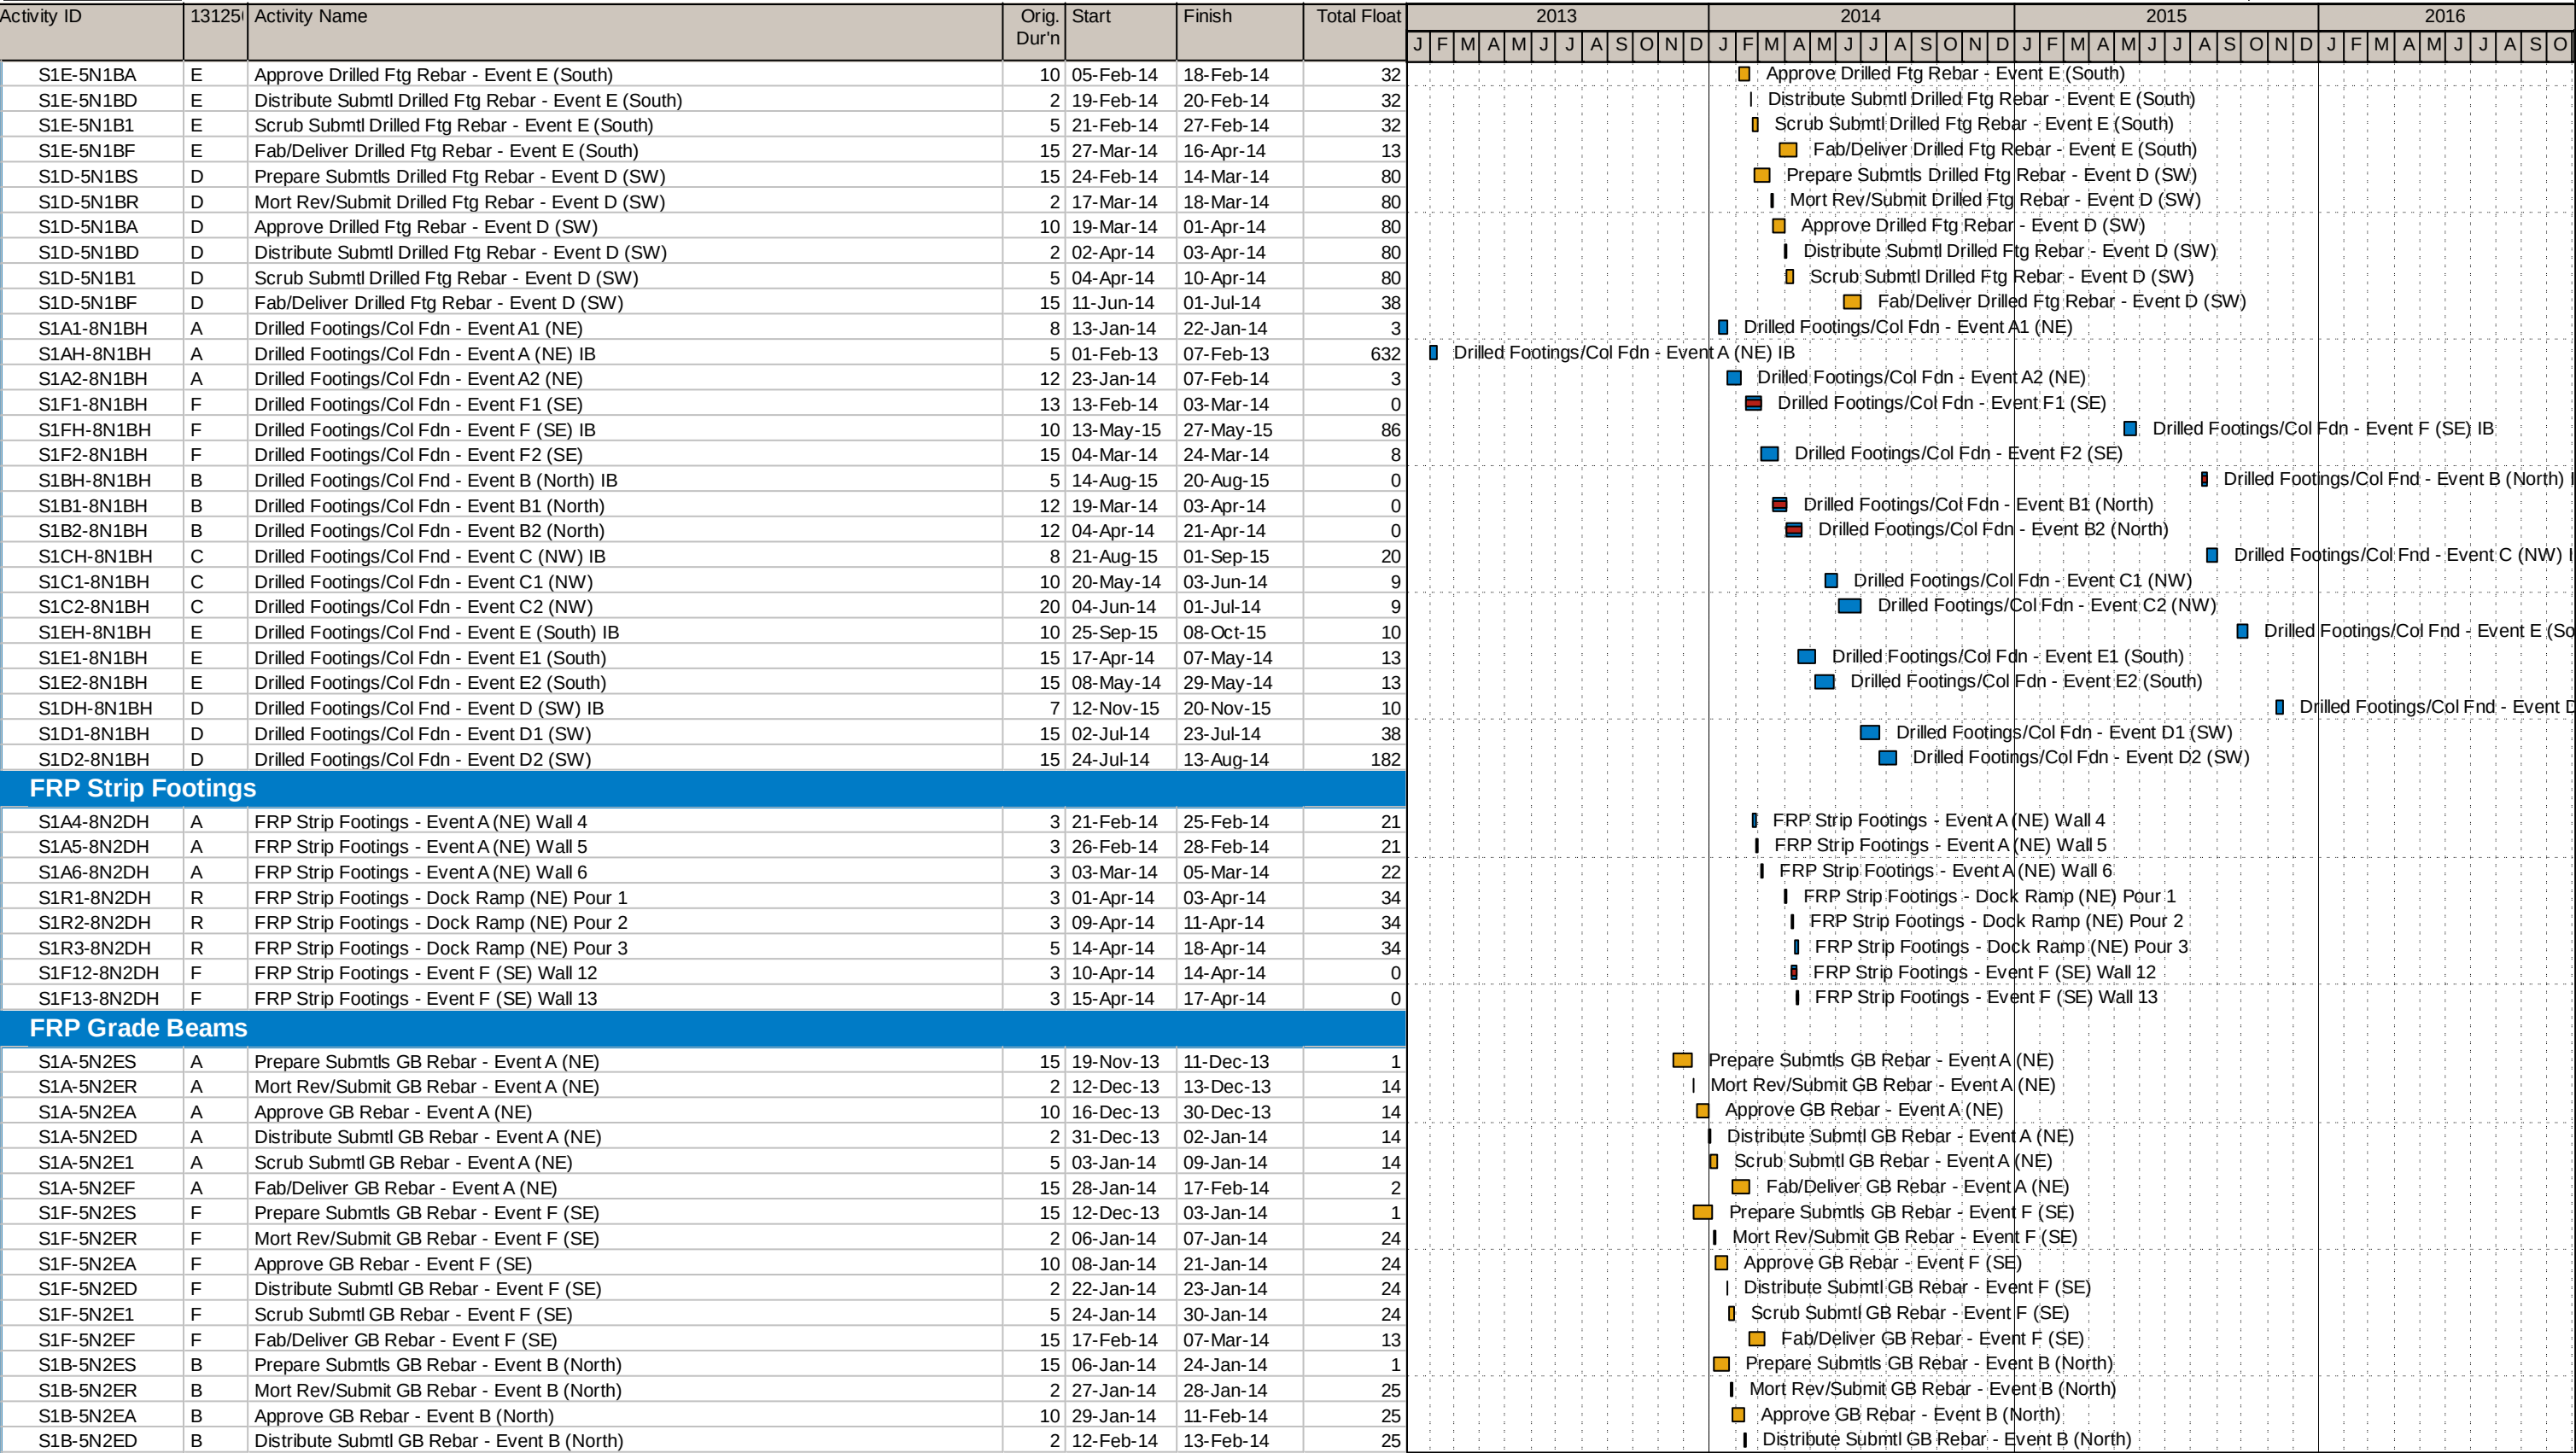



Minnesota Multi-Purpose Stadium

[illegible]

Project Summary
 Procurement
 Critical Work

Milestone
 Temporary Facilities
 Actual Work

Pre-Construction
 Construction

GMP Schedule

Procurement and Construction

Project ID: 13125001-Current

Layout: MMPS - All Activities

TASK filter: Misc 5.

Start Date 01-Feb-13

Finish Date 23-Dec-16

Page 10 of 85

Run Date 08-Nov-13

[illegible]

[illegible]



Minnesota Multi-Purpose Stadium

[illegible]

 Project Summary
  Procurement
  Critical Work

 Milestone
  Temporary Facilities
  Actual Work

 Pre-Construction
  Construction

GMP Schedule

Procurement and Construction

Project ID: 13125001-Current Start Date 01- Page 13 of 85
 Layout: MMPS - All Activities Feb-13
 TASK filter: Misc 5. Finish Date 23- Run Date 08-Nov-13
 Dec-16



Minnesota Multi-Purpose Stadium

[illegible]

 Project Summary
  Procurement
  Critical Work

 Milestone
  Temporary Facilities
  Actual Work

 Pre-Construction
  Construction

GMP Schedule

Procurement and Construction

Project ID: 13125001-Current Start Date 01- Page 14 of 85
 Layout: MMPS - All Activities Feb-13
 TASK filter: Misc 5. Finish Date 23- Run Date 08-Nov-13
 Dec-16

[illegible]



Minnesota Multi-Purpose Stadium

[illegible]

 Project Summary
  Procurement
  Critical Work

 Milestone
  Temporary Facilities
  Actual Work

 Pre-Construction
  Construction

GMP Schedule

Procurement and Construction

Project ID: 13125001-Current Start Date 01- Page 16 of 85
 Layout: MMPS - All Activities Feb-13
 TASK filter: Misc 5. Finish Date 23- Run Date 08-Nov-13
 Dec-16

[illegible]



Minnesota Multi-Purpose Stadium



Activity ID	13125	Activity Name	Orig. Dur'n	Start	Finish	Total Float	2013												2014												2015												2016											
							J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O		
S013-4H2A2	AT.9	Solicit Pricing - Structural Concrete, P&J Decks	17	16-Aug-13	10-Sep-13	12	Solicit Pricing - Structural Concrete, P&J Decks																																															
S013-4H2B2	AT.9	Evaluate Bids & Select Contractor - Structural Concrete, P&J Decks	10	11-Sep-13	24-Sep-13	12	Evaluate Bids & Select Contractor - Structural Concrete, P&J Decks																																															
S013-4H2B3	AT.9	Confirm Pricing - Structural Concrete, P&J Decks	10	11-Oct-13	24-Oct-13	0	Confirm Pricing - Structural Concrete, P&J Decks																																															
S013-4H2B4	AT.9	Award Contract - Structural Concrete, P&J Decks	1	18-Nov-13	18-Nov-13	1	Award Contract - Structural Concrete, P&J Decks																																															
S3A1-5P2GS1	A	Coord / Submit MEP Penetrations in P&J Deck - Lower Club A (NE) 1	5	02-Dec-13	06-Dec-13	2	Coord / Submit MEP Penetrations in P&J Deck - Lower Club A (NE) 1																																															
S3A1-5P2GA3	A	Approve MEP Penetrations in P&J Deck - Lower Club A (NE)	10	09-Dec-13	20-Dec-13	12	Approve MEP Penetrations in P&J Deck - Lower Club A (NE)																																															
S3A1-5P2GS	A	Prepare Submtl P&J Deck Rebar - Lower Club A (NE) 1	15	11-Dec-13	02-Jan-14	10	Prepare Submtl P&J Deck Rebar - Lower Club A (NE) 1																																															
S3A1-5P2GR	A	Mort Rev/Submit P&J Deck Rebar - Lower Club A (NE) Pour 1	2	03-Jan-14	06-Jan-14	28	Mort Rev/Submit P&J Deck Rebar - Lower Club A (NE) Pour 1																																															
S3A1-5P2GA	A	Approve P&J Deck Rebar - Lower Club Area A (NE) 1	10	07-Jan-14	20-Jan-14	28	Approve P&J Deck Rebar - Lower Club Area A (NE) 1																																															
S3A1-5P2GD	A	Distribute Submtl P&J Deck Rebar - Lower Club A (NE) Pour 1	2	21-Jan-14	22-Jan-14	28	Distribute Submtl P&J Deck Rebar - Lower Club A (NE) Pour 1																																															
S3A1-5P2GB	A	Scrub P&J Deck Rebar - Lower Club A (NE) 1	5	23-Jan-14	29-Jan-14	28	Scrub P&J Deck Rebar - Lower Club A (NE) 1																																															
S3A1-5P2GF	A	Fab/Del P&J Deck Rebar - Lower Club A (NE) 1	15	27-Feb-14	19-Mar-14	8	Fab/Del P&J Deck Rebar - Lower Club A (NE) 1																																															
S3A2-5P2GS	A	Prepare Submtls P&J Deck Rebar - Lower Club A (NE) Pour 2	10	03-Jan-14	16-Jan-14	10	Prepare Submtls P&J Deck Rebar - Lower Club A (NE) Pour 2																																															
S3A2-5P2GR	A	Mort Rev/Submit P&J Deck Rebar - Lower Club A (NE) Pour 2	2	17-Jan-14	20-Jan-14	32	Mort Rev/Submit P&J Deck Rebar - Lower Club A (NE) Pour 2																																															
S3A2-5P2GA	A	Approve P&J Deck Rebar - Lower Club A (NE) Pour 2	10	21-Jan-14	03-Feb-14	32	Approve P&J Deck Rebar - Lower Club A (NE) Pour 2																																															
S3A2-5P2GD	A	Distribute Submtl P&J Deck Rebar - Lower Club A (NE) Pour 2	2	04-Feb-14	05-Feb-14	32	Distribute Submtl P&J Deck Rebar - Lower Club A (NE) Pour 2																																															
S3A2-5P2G1	A	Scrub Submtl P&J Deck Rebar - Lower Club A (NE) Pour 2	5	06-Feb-14	12-Feb-14	32	Scrub Submtl P&J Deck Rebar - Lower Club A (NE) Pour 2																																															
S3A2-5P2GF	A	Fab/Deliver P&J Deck Rebar - Lower Club A (NE) Pour 2	15	28-Mar-14	17-Apr-14	1	Fab/Deliver P&J Deck Rebar - Lower Club A (NE) Pour 2																																															
S3A3-5P2GS	A	Prepare Submtls P&J Deck Rebar - Lower Club A (NE) Pour 3	15	17-Jan-14	06-Feb-14	10	Prepare Submtls P&J Deck Rebar - Lower Club A (NE) Pour 3																																															
S3A3-5P2GR	A	Mort Rev/Submit P&J Deck Rebar - Lower Club A (NE) Pour 3	2	07-Feb-14	10-Feb-14	86	Mort Rev/Submit P&J Deck Rebar - Lower Club A (NE) Pour 3																																															
S3A3-5P2GA	A	Approve P&J Deck Rebar - Lower Club A (NE) Pour 3	10	11-Feb-14	24-Feb-14	86	Approve P&J Deck Rebar - Lower Club A (NE) Pour 3																																															
S3A3-5P2GD	A	Distribute Submtl P&J Deck Rebar - Lower Club A (NE) Pour 3	2	25-Feb-14	26-Feb-14	86	Distribute Submtl P&J Deck Rebar - Lower Club A (NE) Pour 3																																															
S3A3-5P2G1	A	Scrub Submtl P&J Deck Rebar - Lower Club A (NE) Pour 3	5	27-Feb-14	05-Mar-14	86	Scrub Submtl P&J Deck Rebar - Lower Club A (NE) Pour 3																																															
S3A3-5P2GF	A	Fab/Deliver P&J Deck Rebar - Lower Club A (NE) Pour 3	15	19-May-14	09-Jun-14	34	Fab/Deliver P&J Deck Rebar - Lower Club A (NE) Pour 3																																															
S4A1-5P2GS1	A	Coord / Submit MEP Penetrations in P&J Deck - Main Concourse A (NE) Pour 1	5	02-Dec-13	06-Dec-13	17	Coord / Submit MEP Penetrations in P&J Deck - Main Concourse A (NE) Pour 1																																															
S4A1-5P2GA3	A	Approve MEP Penetrations in P&J Deck - Main Concourse A (NE)	10	09-Dec-13	20-Dec-13	37	Approve MEP Penetrations in P&J Deck - Main Concourse A (NE)																																															
S4A1-5P2GS	A	Prepare Submtls P&J Deck Rebar - Main Concourse A (NE) Pour 1	15	31-Jan-14	20-Feb-14	10	Prepare Submtls P&J Deck Rebar - Main Concourse A (NE) Pour 1																																															
S4A1-5P2GR	A	Mort Rev/Submit P&J Deck Rebar - Main Concourse A (NE) Pour 1	2	21-Feb-14	24-Feb-14	15	Mort Rev/Submit P&J Deck Rebar - Main Concourse A (NE) Pour 1																																															
S4A1-5P2GA	A	Approve P&J Deck Rebar - Main Concourse A (NE) Pour 1	10	25-Feb-14	10-Mar-14	15	Approve P&J Deck Rebar - Main Concourse A (NE) Pour 1																																															
S4A1-5P2GD	A	Distribute Submtl P&J Deck Rebar - Main Concourse A (NE) Pour 1	2	11-Mar-14	12-Mar-14	15	Distribute Submtl P&J Deck Rebar - Main Concourse A (NE) Pour 1																																															
S4A1-5P2G1	A	Sc																																																				

Project Summary

Procurement

Critical Work

Milestone

Temporary Facilities

Actual Work

Pre-Construction

Construction

GMP Schedule

Procurement and Construction

Project ID: 13125001-Current

Layout: MMPS - All Activities

TASK filter: Misc 5.

Start Date 01-Feb-13

Finish Date 23-Dec-16

Page 18 of 85

Run Date 08-Nov-13



Minnesota Multi-Purpose Stadium

[illegible]

Project Summary

Procurement

Critical Work

Pre-Construction

Temporary Facilities

Actual Work

Milestone

Construction

GMP Schedule

Procurement and Construction

Project ID: 13125001-Current

Layout: MMPS - All Activities


TASK filter: Misc 5.

Start Date 01-Feb-13

Finish Date 23-Dec-16

Page 19 of 85

Run Date 08-Nov-13

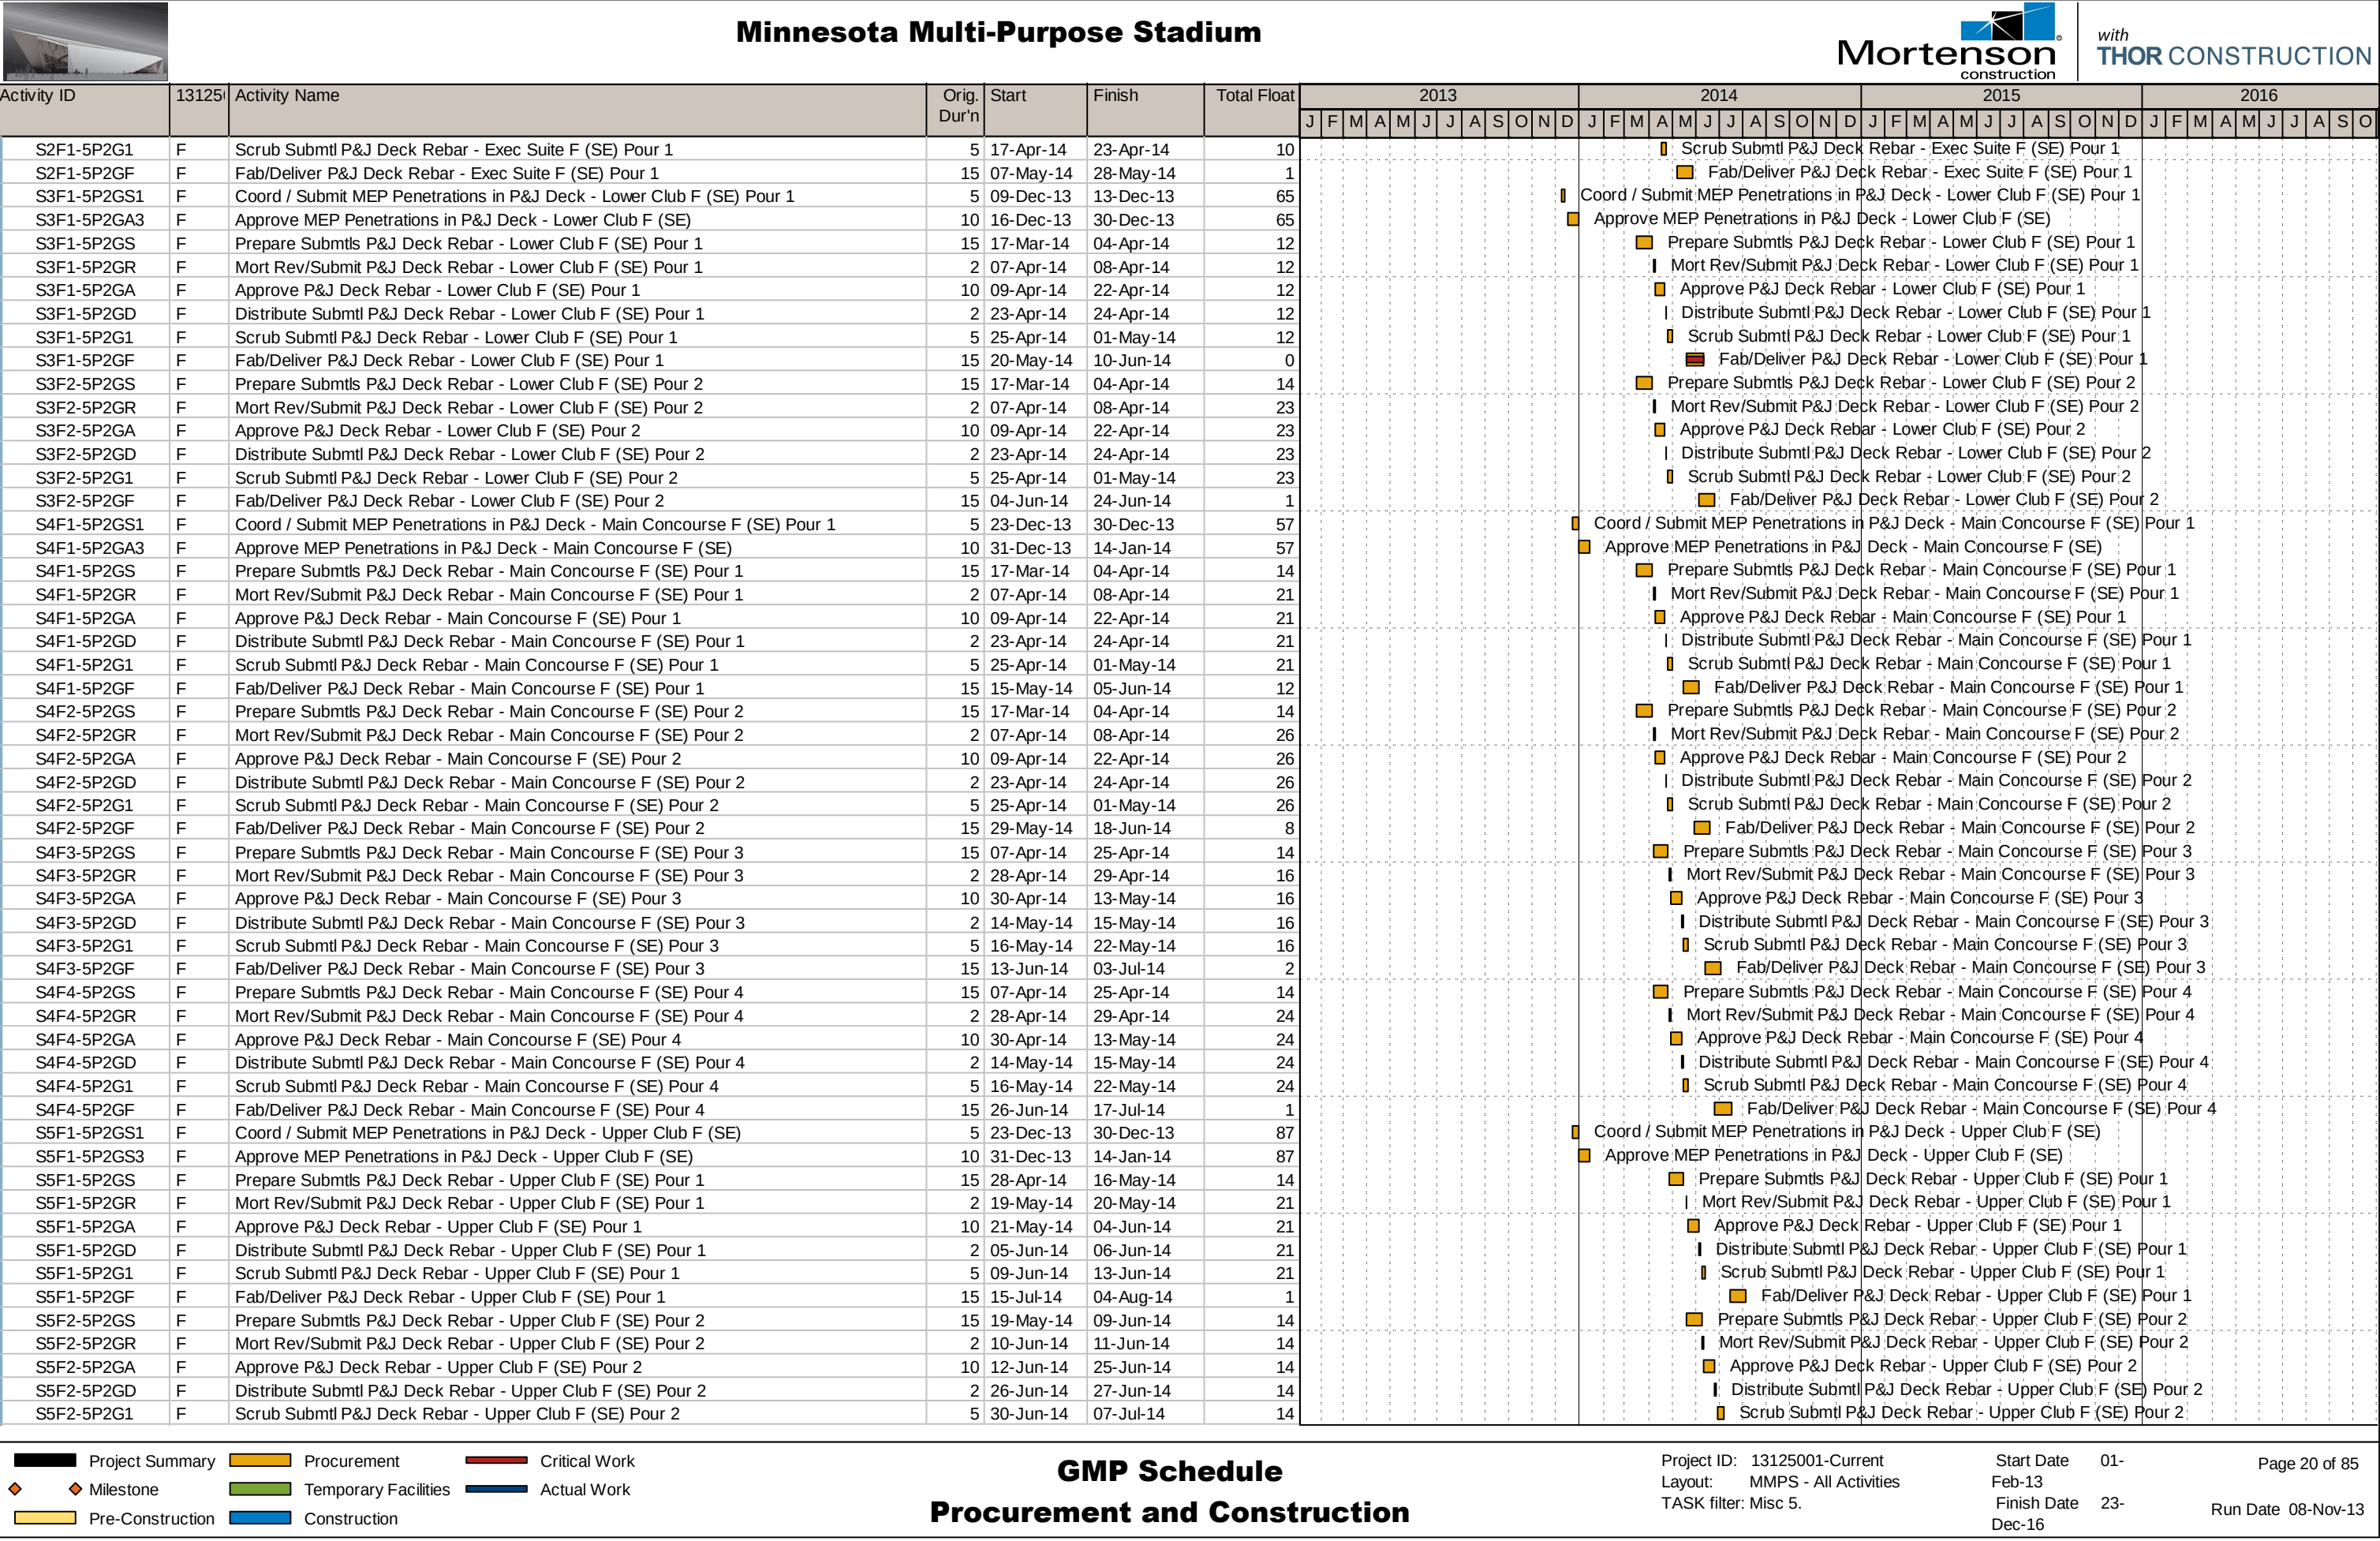



Minnesota Multi-Purpose Stadium

[illegible]

Project Summary

Procurement

Critical Work

Pre-Construction

Temporary Facilities

Actual Work

Milestone

Construction

GMP Schedule

Procurement and Construction

Project ID: 13125001-Current

Layout: MMPS - All Activities

TASK filter: Misc 5.

Start Date 01-Feb-13

Finish Date 23-Dec-16

Page 21 of 85

Run Date 08-Nov-13



Minnesota Multi-Purpose Stadium

[illegible]

Project Summary
 Procurement
 Critical Work

Milestone
 Temporary Facilities
 Actual Work

Pre-Construction
 Construction

GMP Schedule

Procurement and Construction

Project ID: 13125001-Current

Layout: MMPS - All Activities


TASK filter: Misc 5.


Start Date 01-Feb-13

Finish Date 23-Dec-16

Page 22 of 85

Run Date 08-Nov-13

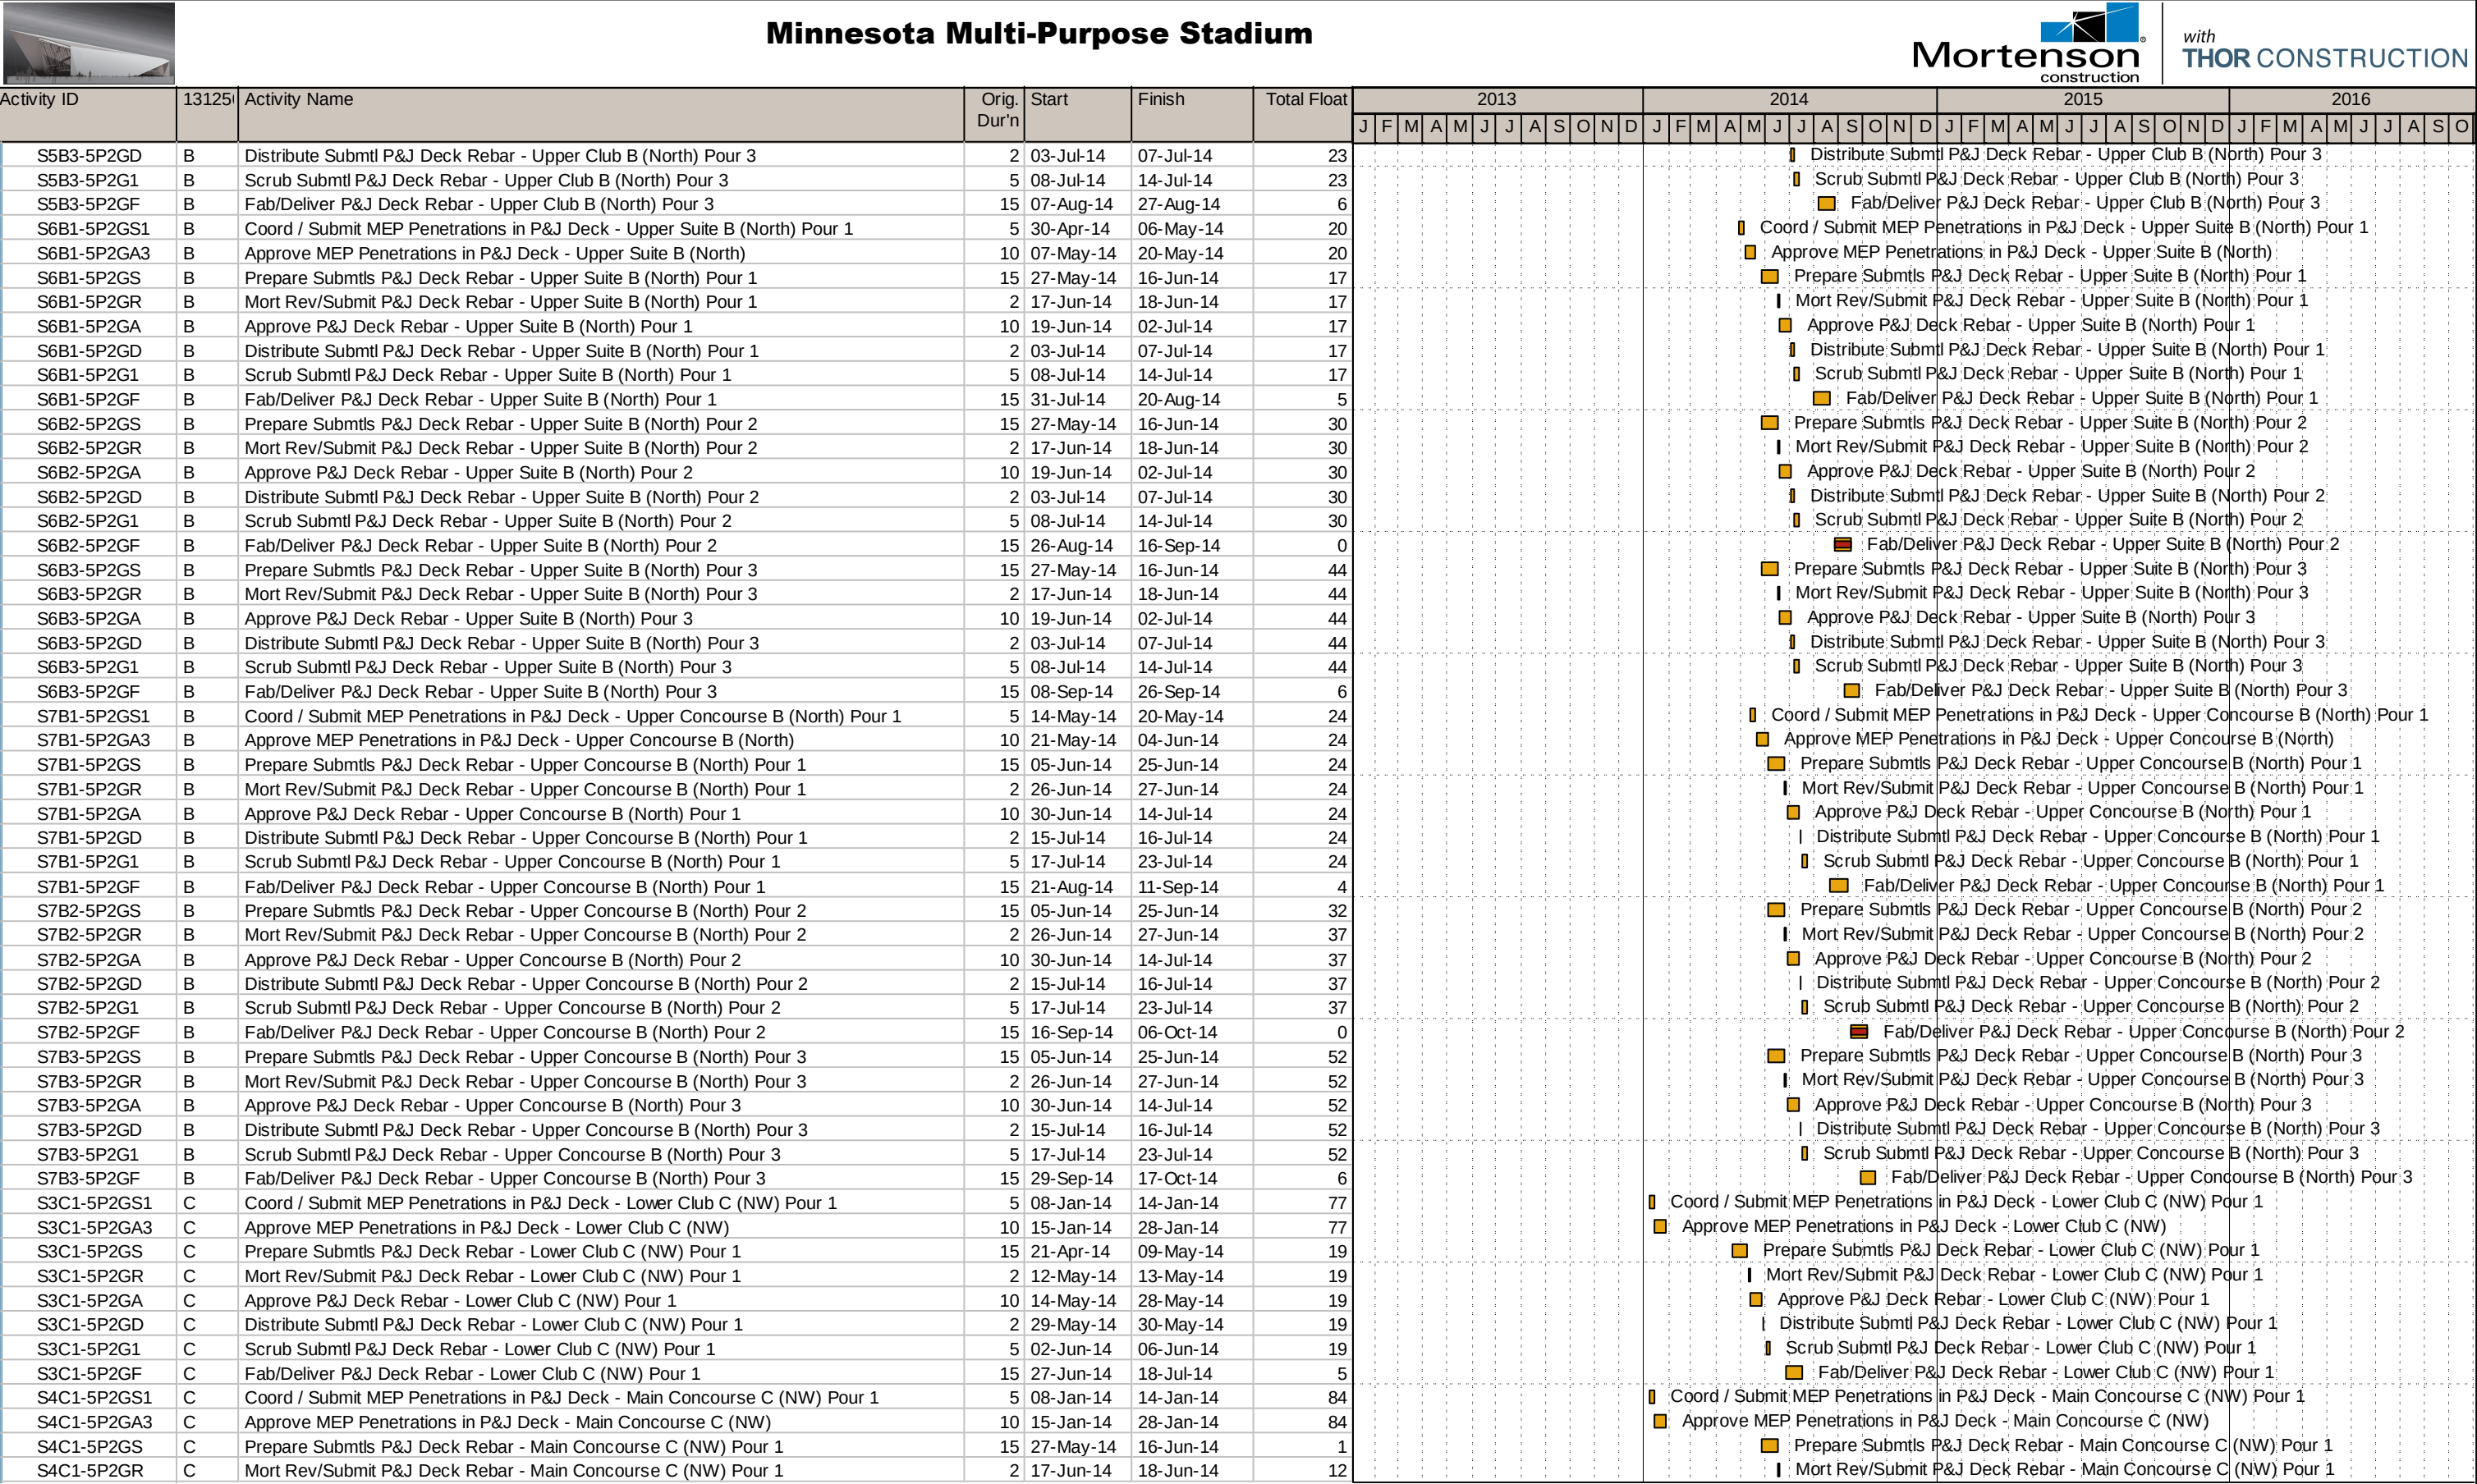

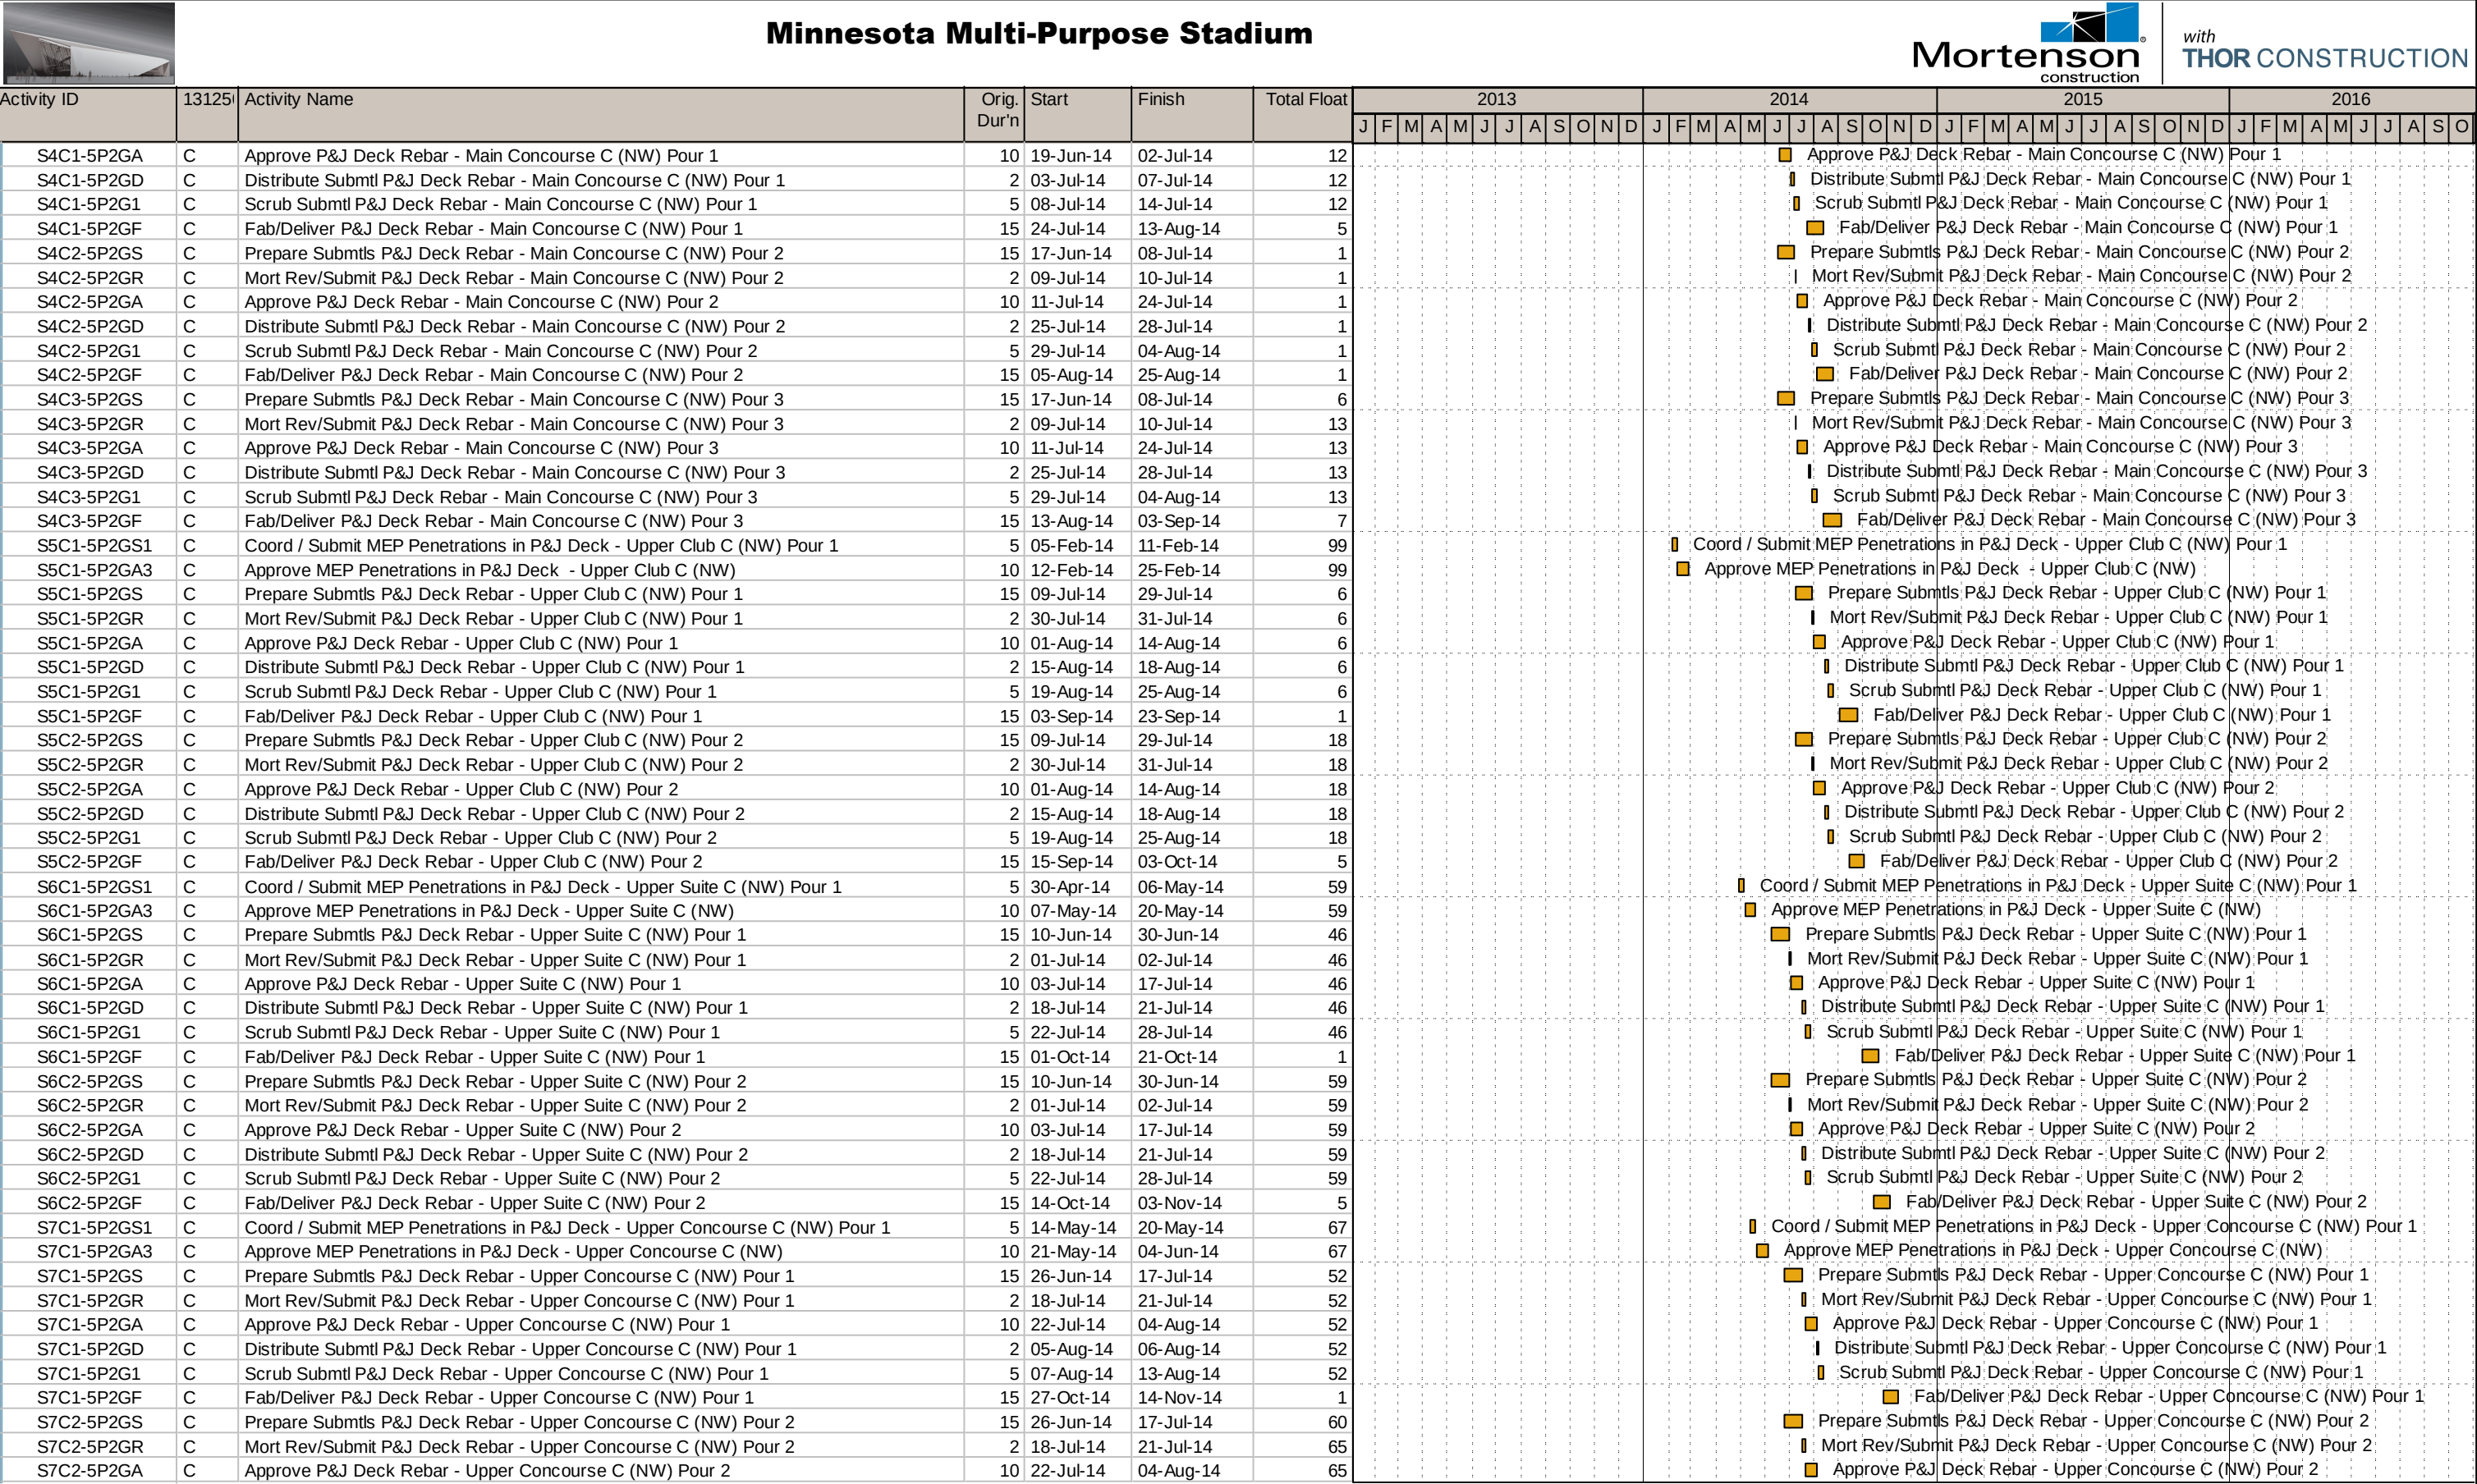



Minnesota Multi-Purpose Stadium

[illegible]

Project Summary

Procurement

Critical Work

Pre-Construction

Temporary Facilities

Actual Work

Milestone

GMP Schedule

Procurement and Construction

Project ID: 13125001-Current

Layout: MMPS - All Activities

TASK filter: Misc 5.

Start Date 01-Feb-13

Finish Date 23-Dec-16

Page 25 of 85

Run Date 08-Nov-13



Minnesota Multi-Purpose Stadium

[illegible]

Project Summary

Procurement

Critical Work

Pre-Construction

Temporary Facilities

Actual Work

Milestone

Construction

GMP Schedule

Procurement and Construction

Project ID: 13125001-Current

Layout: MMPS - All Activities

TASK filter: Misc 5.

Start Date 01-Feb-13

Finish Date 23-Dec-16

Page 26 of 85

Run Date 08-Nov-13



Minnesota Multi-Purpose Stadium

[illegible]

Project Summary

Procurement

Critical Work

Milestone

Temporary Facilities

Actual Work

Pre-Construction

Construction

GMP Schedule

Procurement and Construction

Project ID: 13125001-Current

Layout: MMPS - All Activities

TASK filter: Misc 5.

Start Date 01-Feb-13

Finish Date 23-Dec-16

Page 27 of 85

Run Date 08-Nov-13



Minnesota Multi-Purpose Stadium

[illegible]

Project Summary

 Procurement

Critical Work

Temporary Facilities

Milestone

Actual Work

Pre-Construction

Construction

GMP Schedule

Procurement and Construction

Project ID: 13125001-Current

Layout: MMPS - All Activities

TASK filter: Misc 5.

Start Date 01-Feb-13

Finish Date 23-Dec-16

Page 28 of 85

Run Date 08-Nov-13



Minnesota Multi-Purpose Stadium

[illegible]

Project Summary

Procurement

Critical Work

Pre-Construction

Temporary Facilities

Actual Work

Milestone

GMP Schedule

Procurement and Construction

Project ID: 13125001-Current

Layout: MMPS - All Activities

TASK filter: Misc 5.

Start Date 01-Feb-13

Finish Date 23-Dec-16

Page 29 of 85

Run Date 08-Nov-13



Minnesota Multi-Purpose Stadium

[illegible]

Project Summary

Procurement

Critical Work

GMP Schedule

Procurement and Construction

Project ID: 13125001-Current

Layout: MMPS - All Activities

TASK filter: Misc 5.

Start Date 01-Feb-13

Finish Date 23-Dec-16

Page 30 of 85

Run Date 08-Nov-13

Milestone

Temporary Facilities

Actual Work

Pre-Construction

Construction



Minnesota Multi-Purpose Stadium

[illegible]

Project Summary

Procurement

Critical Work

Pre-Construction

Temporary Facilities

Actual Work

Construction

GMP Schedule

Procurement and Construction

Project ID: 13125001-Current

Layout: MMPS - All Activities

TASK filter: Misc 5.

Start Date 01-Feb-13

Finish Date 23-Dec-16

Page 31 of 85

Run Date 08-Nov-13



Minnesota Multi-Purpose Stadium

[illegible]

Project Summary

Procurement

Critical Work

Milestone

Temporary Facilities

Actual Work

Pre-Construction

Construction

GMP Schedule

Procurement and Construction

Project ID: 13125001-Current

Layout: MMPS - All Activities


TASK filter: Misc 5.


Start Date 01-Feb-13

Finish Date 23-Dec-16

Run Date 08-Nov-13

Page 32 of 85

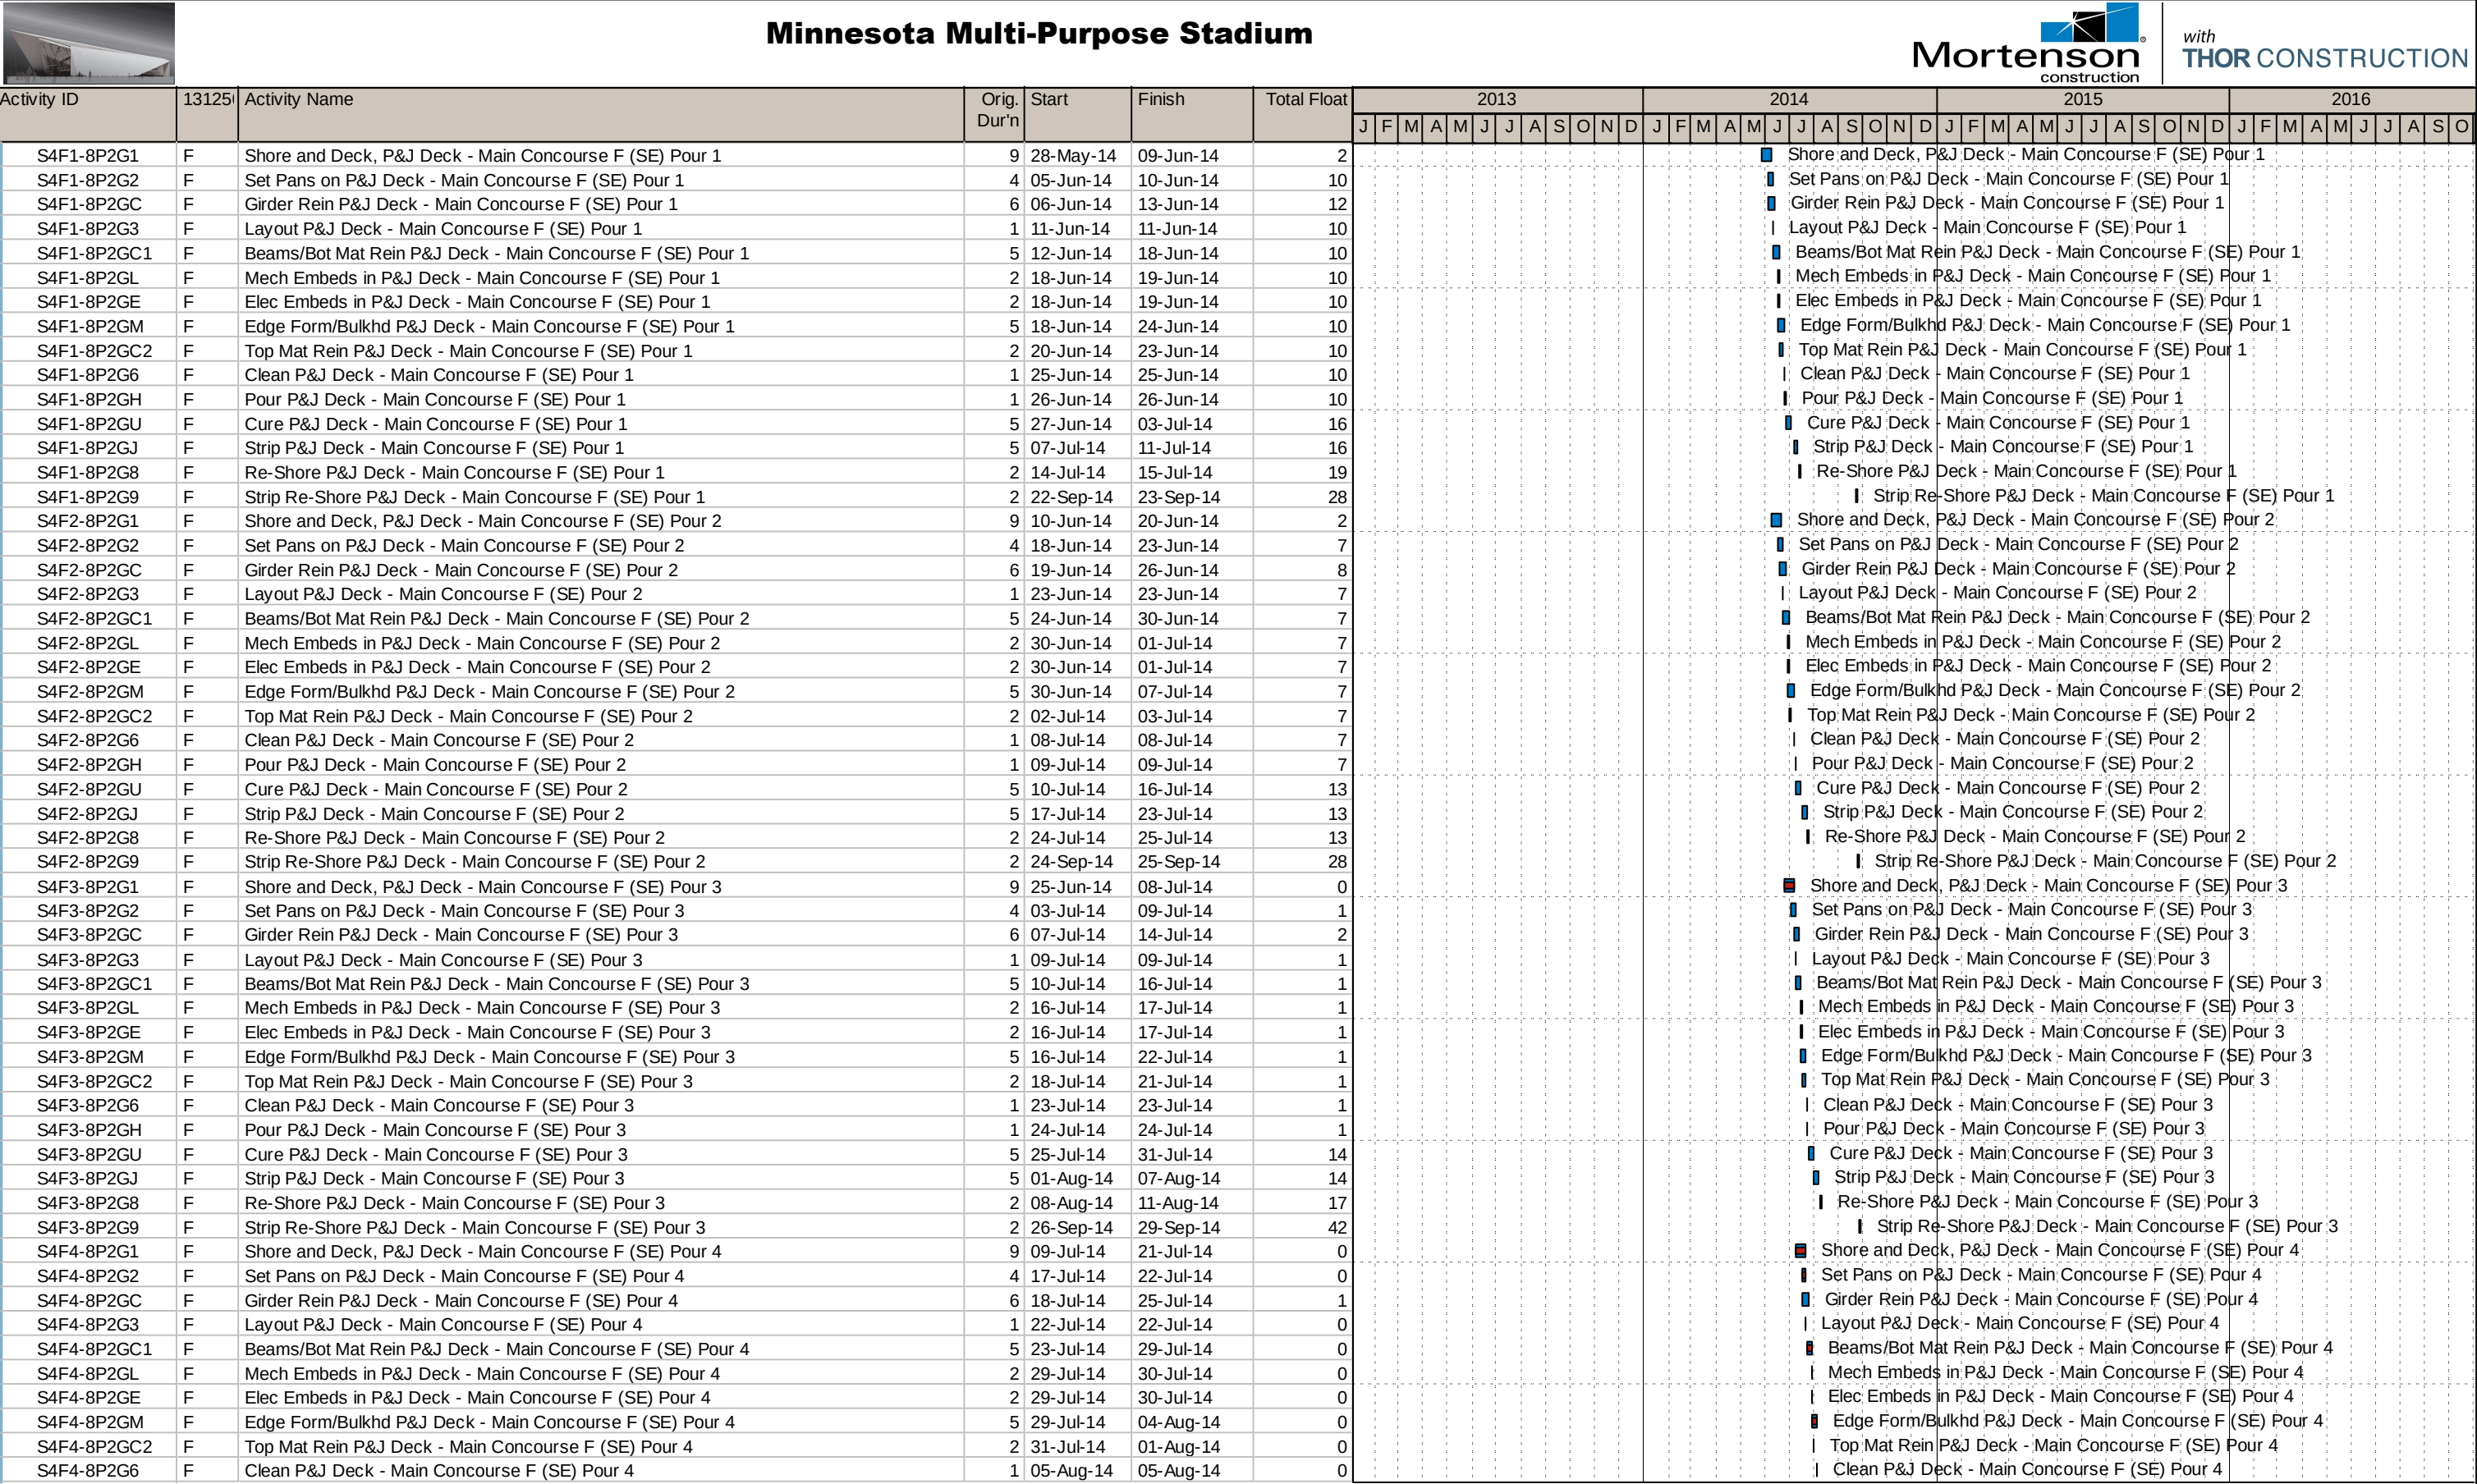

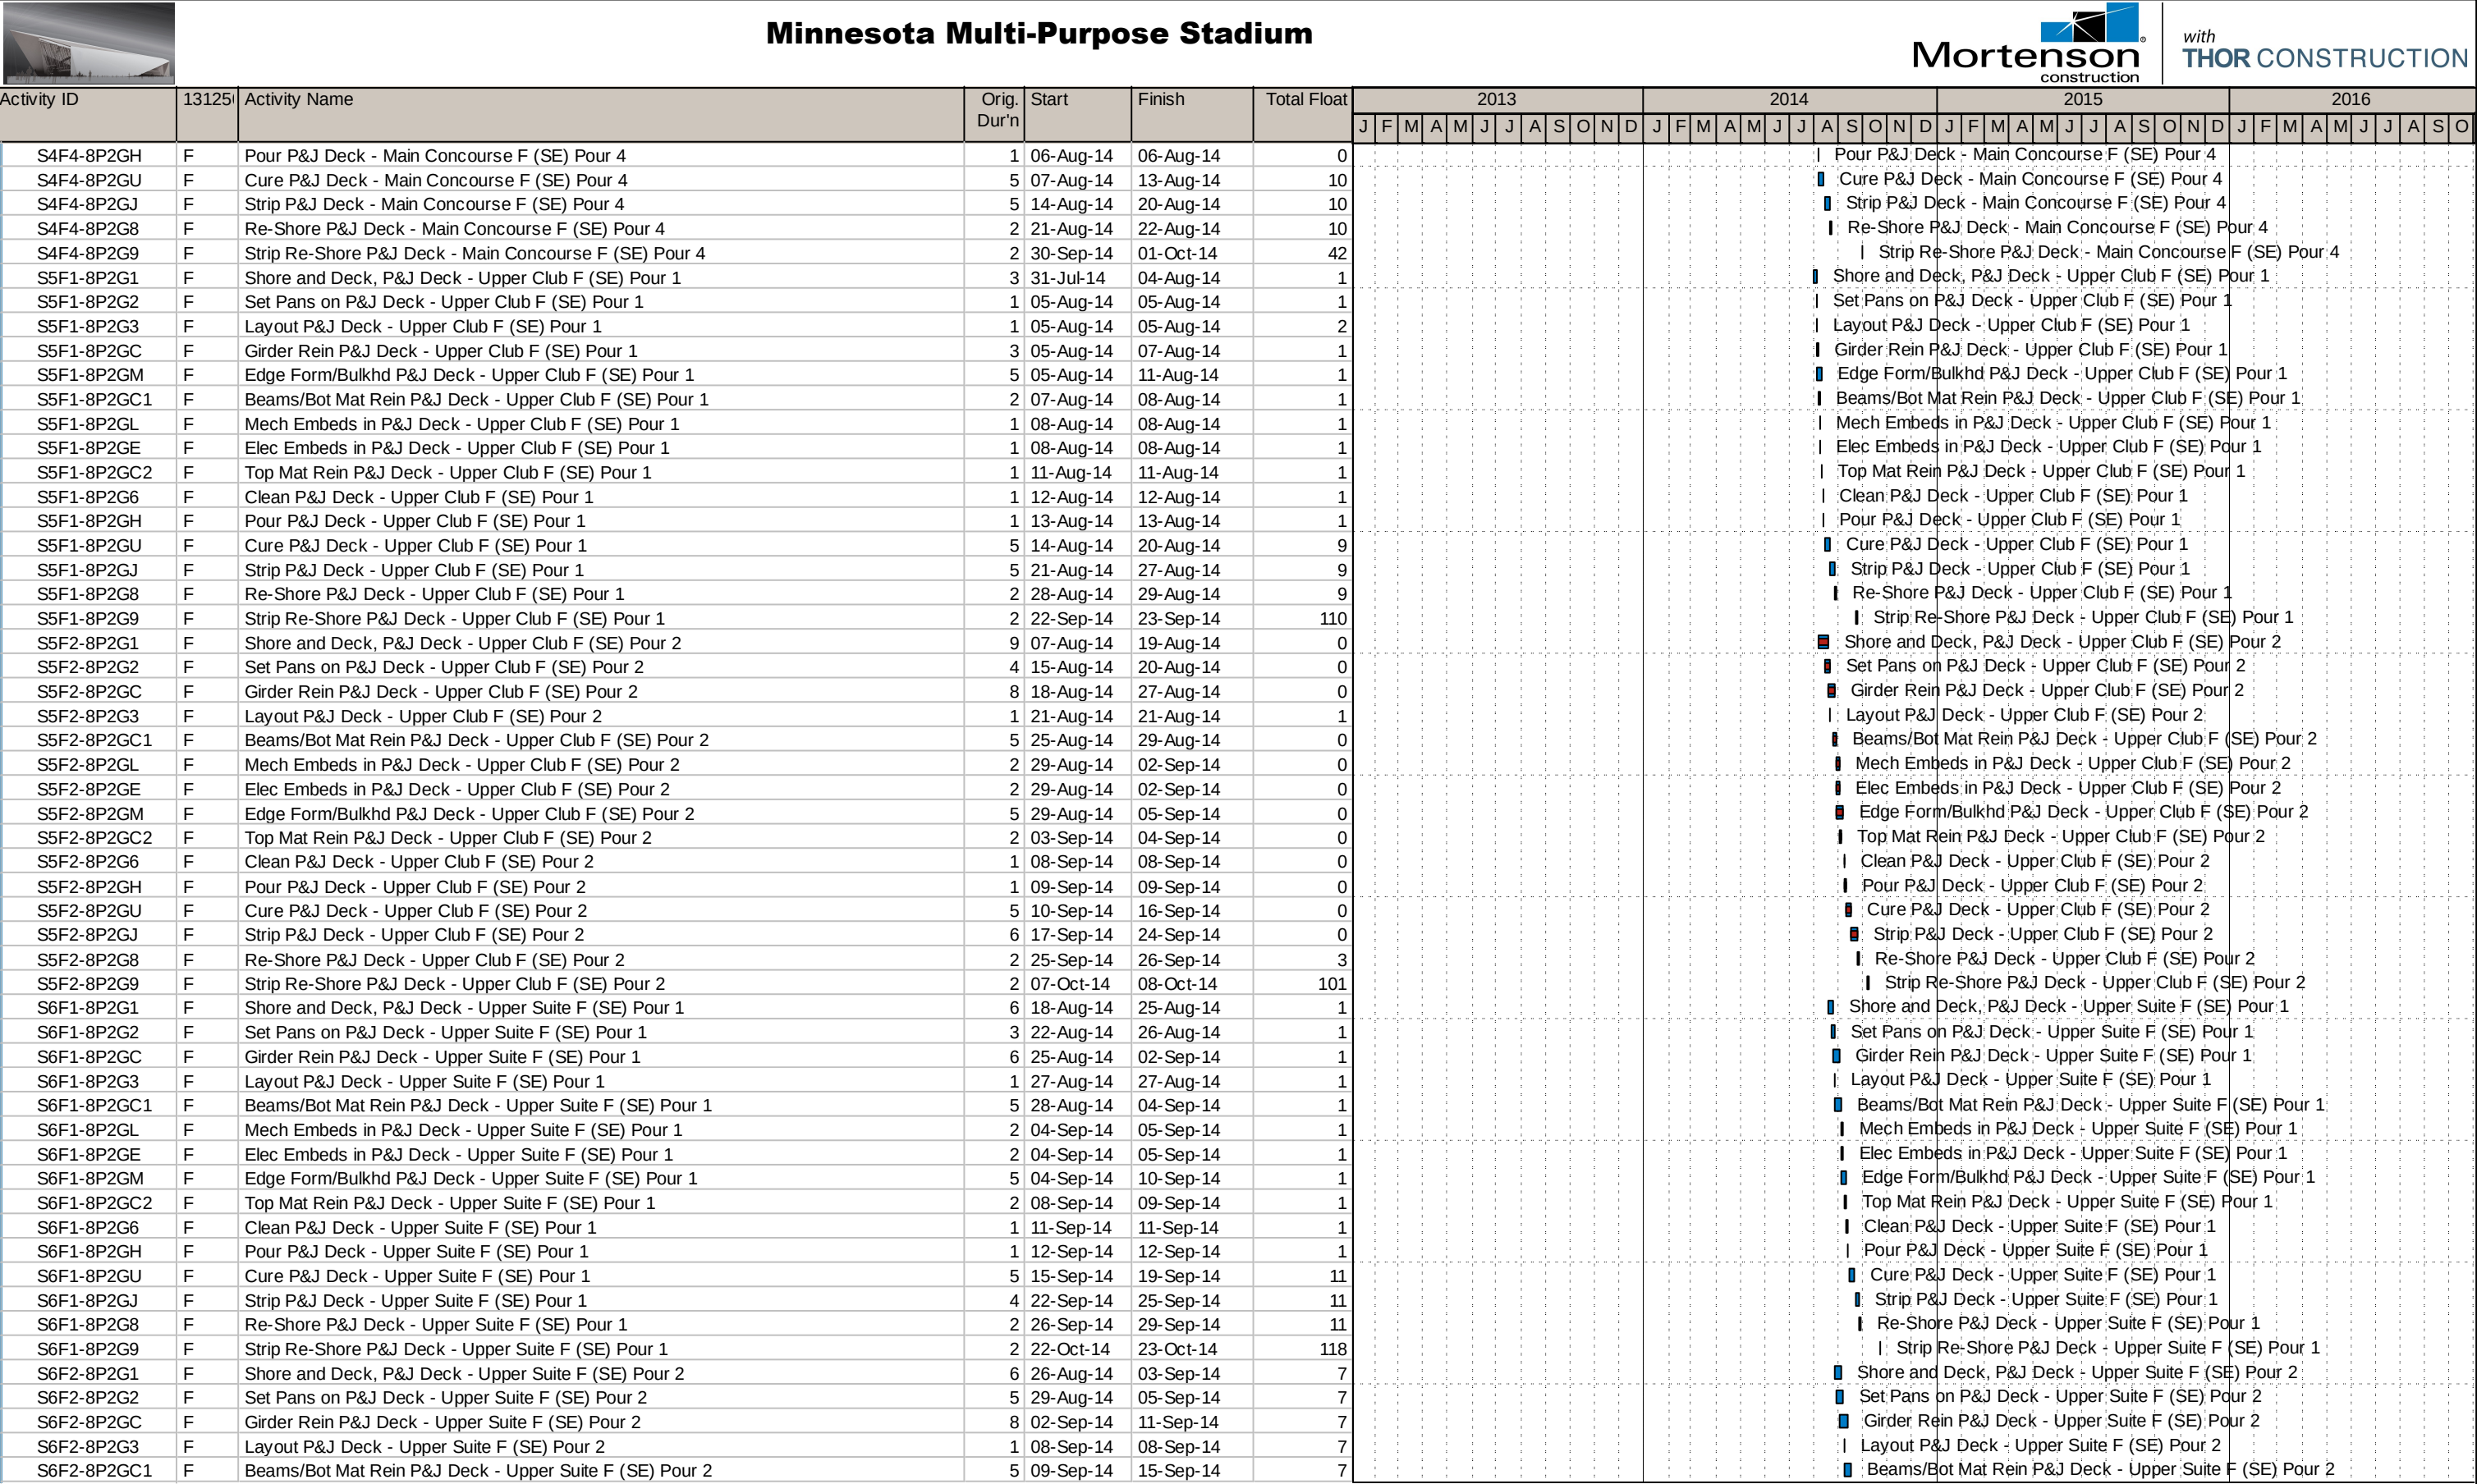



Minnesota Multi-Purpose Stadium

[illegible]

Project Summary
 Procurement
 Critical Work

Pre-Construction
 Temporary Facilities
 Actual Work

Milestone

GMP Schedule

Procurement and Construction

Project ID: 13125001-Current

Layout: MMPS - All Activities

TASK filter: Misc 5.

Start Date 01-Feb-13

Finish Date 23-Dec-16

Run Date 08-Nov-13

Page 35 of 85



Minnesota Multi-Purpose Stadium

[illegible]

Project Summary
 Procurement
 Critical Work

Milestone
 Temporary Facilities
 Actual Work

Pre-Construction
 Construction

GMP Schedule

Procurement and Construction

Project ID: 13125001-Current

Layout: MMPS - All Activities

TASK filter: Misc 5.

Start Date 01-Feb-13

Finish Date 23-Dec-16

Page 36 of 85

Run Date 08-Nov-13



Minnesota Multi-Purpose Stadium

[illegible]

Project Summary

Procurement

Critical Work

Pre-Construction

Temporary Facilities

Actual Work

Milestone

Construction

GMP Schedule

Procurement and Construction

Project ID: 13125001-Current

Layout: MMPS - All Activities

TASK filter: Misc 5.

Start Date 01-Feb-13

Finish Date 23-Dec-16

Page 37 of 85

Run Date 08-Nov-13



Minnesota Multi-Purpose Stadium

[illegible]

Project Summary

Procurement

Critical Work

Milestone

Temporary Facilities

Actual Work

Pre-Construction

Construction

GMP Schedule

Procurement and Construction

Project ID: 13125001-Current
 Layout: MMPS - All Activities
 TASK filter: Misc 5.

Start Date 01-Feb-13
 Finish Date 23-Dec-16

Page 38 of 85
 Run Date 08-Nov-13



Minnesota Multi-Purpose Stadium

[illegible]

Project Summary
 Procurement
 Critical Work

Milestone
 Temporary Facilities
 Actual Work

Pre-Construction
 Construction

GMP Schedule

Procurement and Construction

Project ID: 13125001-Current

Layout: MMPS - All Activities

TASK filter: Misc 5.

Start Date 01-Feb-13

Finish Date 23-Dec-16

Page 39 of 85

Run Date 08-Nov-13



Minnesota Multi-Purpose Stadium

[illegible]

Project Summary
 Procurement
 Critical Work

Milestone
 Temporary Facilities
 Actual Work

Pre-Construction
 Construction

GMP Schedule

Procurement and Construction

Project ID: 13125001-Current

Layout: MMPS - All Activities

TASK filter: Misc 5.

Start Date 01-Feb-13

Finish Date 23-Dec-16

Run Date 08-Nov-13

Page 40 of 85



Minnesota Multi-Purpose Stadium

[illegible]

Project Summary
 Procurement
 Critical Work

Milestone
 Temporary Facilities
 Actual Work

Pre-Construction
 Construction

GMP Schedule

Procurement and Construction

Project ID: 13125001-Current
Start Date 01-
Page 41 of 85

Layout: MMPS - All Activities
Feb-13

TASK filter: Misc 5.
Finish Date 23-
Run Date 08-Nov-13

Dec-16



Minnesota Multi-Purpose Stadium

[illegible]

Project Summary

Procurement

Critical Work

Milestone

Temporary Facilities

Actual Work

Pre-Construction

Construction

GMP Schedule

Procurement and Construction

Project ID: 13125001-Current

Layout: MMPS - All Activities

TASK filter: Misc 5.

Start Date 01-Feb-13

Finish Date 23-Dec-16

Page 42 of 85

Run Date 08-Nov-13

[illegible]



Minnesota Multi-Purpose Stadium

[illegible]

Project Summary

Procurement

Critical Work

Temporary Facilities

Actual Work

Pre-Construction

Construction

Milestone

GMP Schedule

Procurement and Construction

Project ID: 13125001-Current

Layout: MMPS - All Activities

TASK filter: Misc 5.

Start Date 01-Feb-13

Finish Date 23-Dec-16

Page 44 of 85

Run Date 08-Nov-13



Minnesota Multi-Purpose Stadium

[illegible]

Project Summary

Procurement

Critical Work

Temporary Facilities

Actual Work

Pre-Construction

Construction

GMP Schedule

Procurement and Construction

Project ID: 13125001-Current

Layout: MMPS - All Activities

TASK filter: Misc 5.

Start Date 01-Feb-13

Finish Date 23-Dec-16

Page 45 of 85

Run Date 08-Nov-13



Minnesota Multi-Purpose Stadium

[illegible]

Project Summary

Procurement

Critical Work

Pre-Construction

Temporary Facilities

Actual Work

GMP Schedule

Procurement and Construction

Project ID: 13125001-Current

Layout: MMPS - All Activities

TASK filter: Misc 5.

Start Date 01-Feb-13

Finish Date 23-Dec-16

Page 46 of 85

Run Date 08-Nov-13



Minnesota Multi-Purpose Stadium

[illegible]

Project Summary

Procurement

Critical Work

Milestone

Temporary Facilities

Actual Work

Pre-Construction

Construction

GMP Schedule

Procurement and Construction

Project ID: 13125001-Current

Layout: MMPS - All Activities

TASK filter: Misc 5.

Start Date 01-Feb-13

Finish Date 23-Dec-16

Page 47 of 85

Run Date 08-Nov-13



Minnesota Multi-Purpose Stadium

[illegible]

Project Summary

Procurement

Critical Work

Pre-Construction

Temporary Facilities

Actual Work

Milestone

Construction

GMP Schedule

Procurement and Construction

Project ID: 13125001-Current

Layout: MMPS - All Activities

TASK filter: Misc 5.

Start Date 01-Feb-13

Finish Date 23-Dec-16

Page 48 of 85

Run Date 08-Nov-13

[illegible]



Minnesota Multi-Purpose Stadium

[illegible]

Project Summary

Procurement

Critical Work

Temporary Facilities

Actual Work

Pre-Construction

Construction

GMP Schedule

Procurement and Construction

Project ID: 13125001-Current

Layout: MMPS - All Activities

TASK filter: Misc 5.

Start Date 01-Feb-13

Finish Date 23-Dec-16

Page 50 of 85

Run Date 08-Nov-13



Minnesota Multi-Purpose Stadium

[illegible]

Project Summary

Procurement

Critical Work

Pre-Construction

Construction

Milestone

Temporary Facilities

Actual Work

GMP Schedule

Procurement and Construction

Project ID: 13125001-Current

Layout: MMPS - All Activities

TASK filter: Misc 5.

Start Date 01-Feb-13

Finish Date 23-Dec-16

Page 51 of 85

Run Date 08-Nov-13

[illegible]



Minnesota Multi-Purpose Stadium

[illegible]

Project Summary

Procurement

Critical Work

Pre-Construction

Temporary Facilities

Actual Work

Construction

GMP Schedule

Procurement and Construction

Project ID: 13125001-Current

Layout: MMPS - All Activities

TASK filter: Misc 5.

Start Date 01-Feb-13

Finish Date 23-Dec-16

Page 53 of 85

Run Date 08-Nov-13



Minnesota Multi-Purpose Stadium

[illegible]

Project Summary

Procurement

Critical Work

Pre-Construction

Temporary Facilities

Actual Work

Milestone

Construction

GMP Schedule

Procurement and Construction

Project ID: 13125001-Current

Layout: MMPS - All Activities

TASK filter: Misc 5.

Start Date 01-Feb-13

Finish Date 23-Dec-16

Page 54 of 85

Run Date 08-Nov-13



Minnesota Multi-Purpose Stadium

[illegible]

Project Summary

Procurement

Critical Work

Milestone

Temporary Facilities

Actual Work

Pre-Construction

Construction

GMP Schedule

Procurement and Construction

Project ID: 13125001-Current

Layout: MMPS - All Activities

TASK filter: Misc 5.


Start Date 01-Feb-13

Finish Date 23-Dec-16

Page 55 of 85

Run Date 08-Nov-13

[illegible]

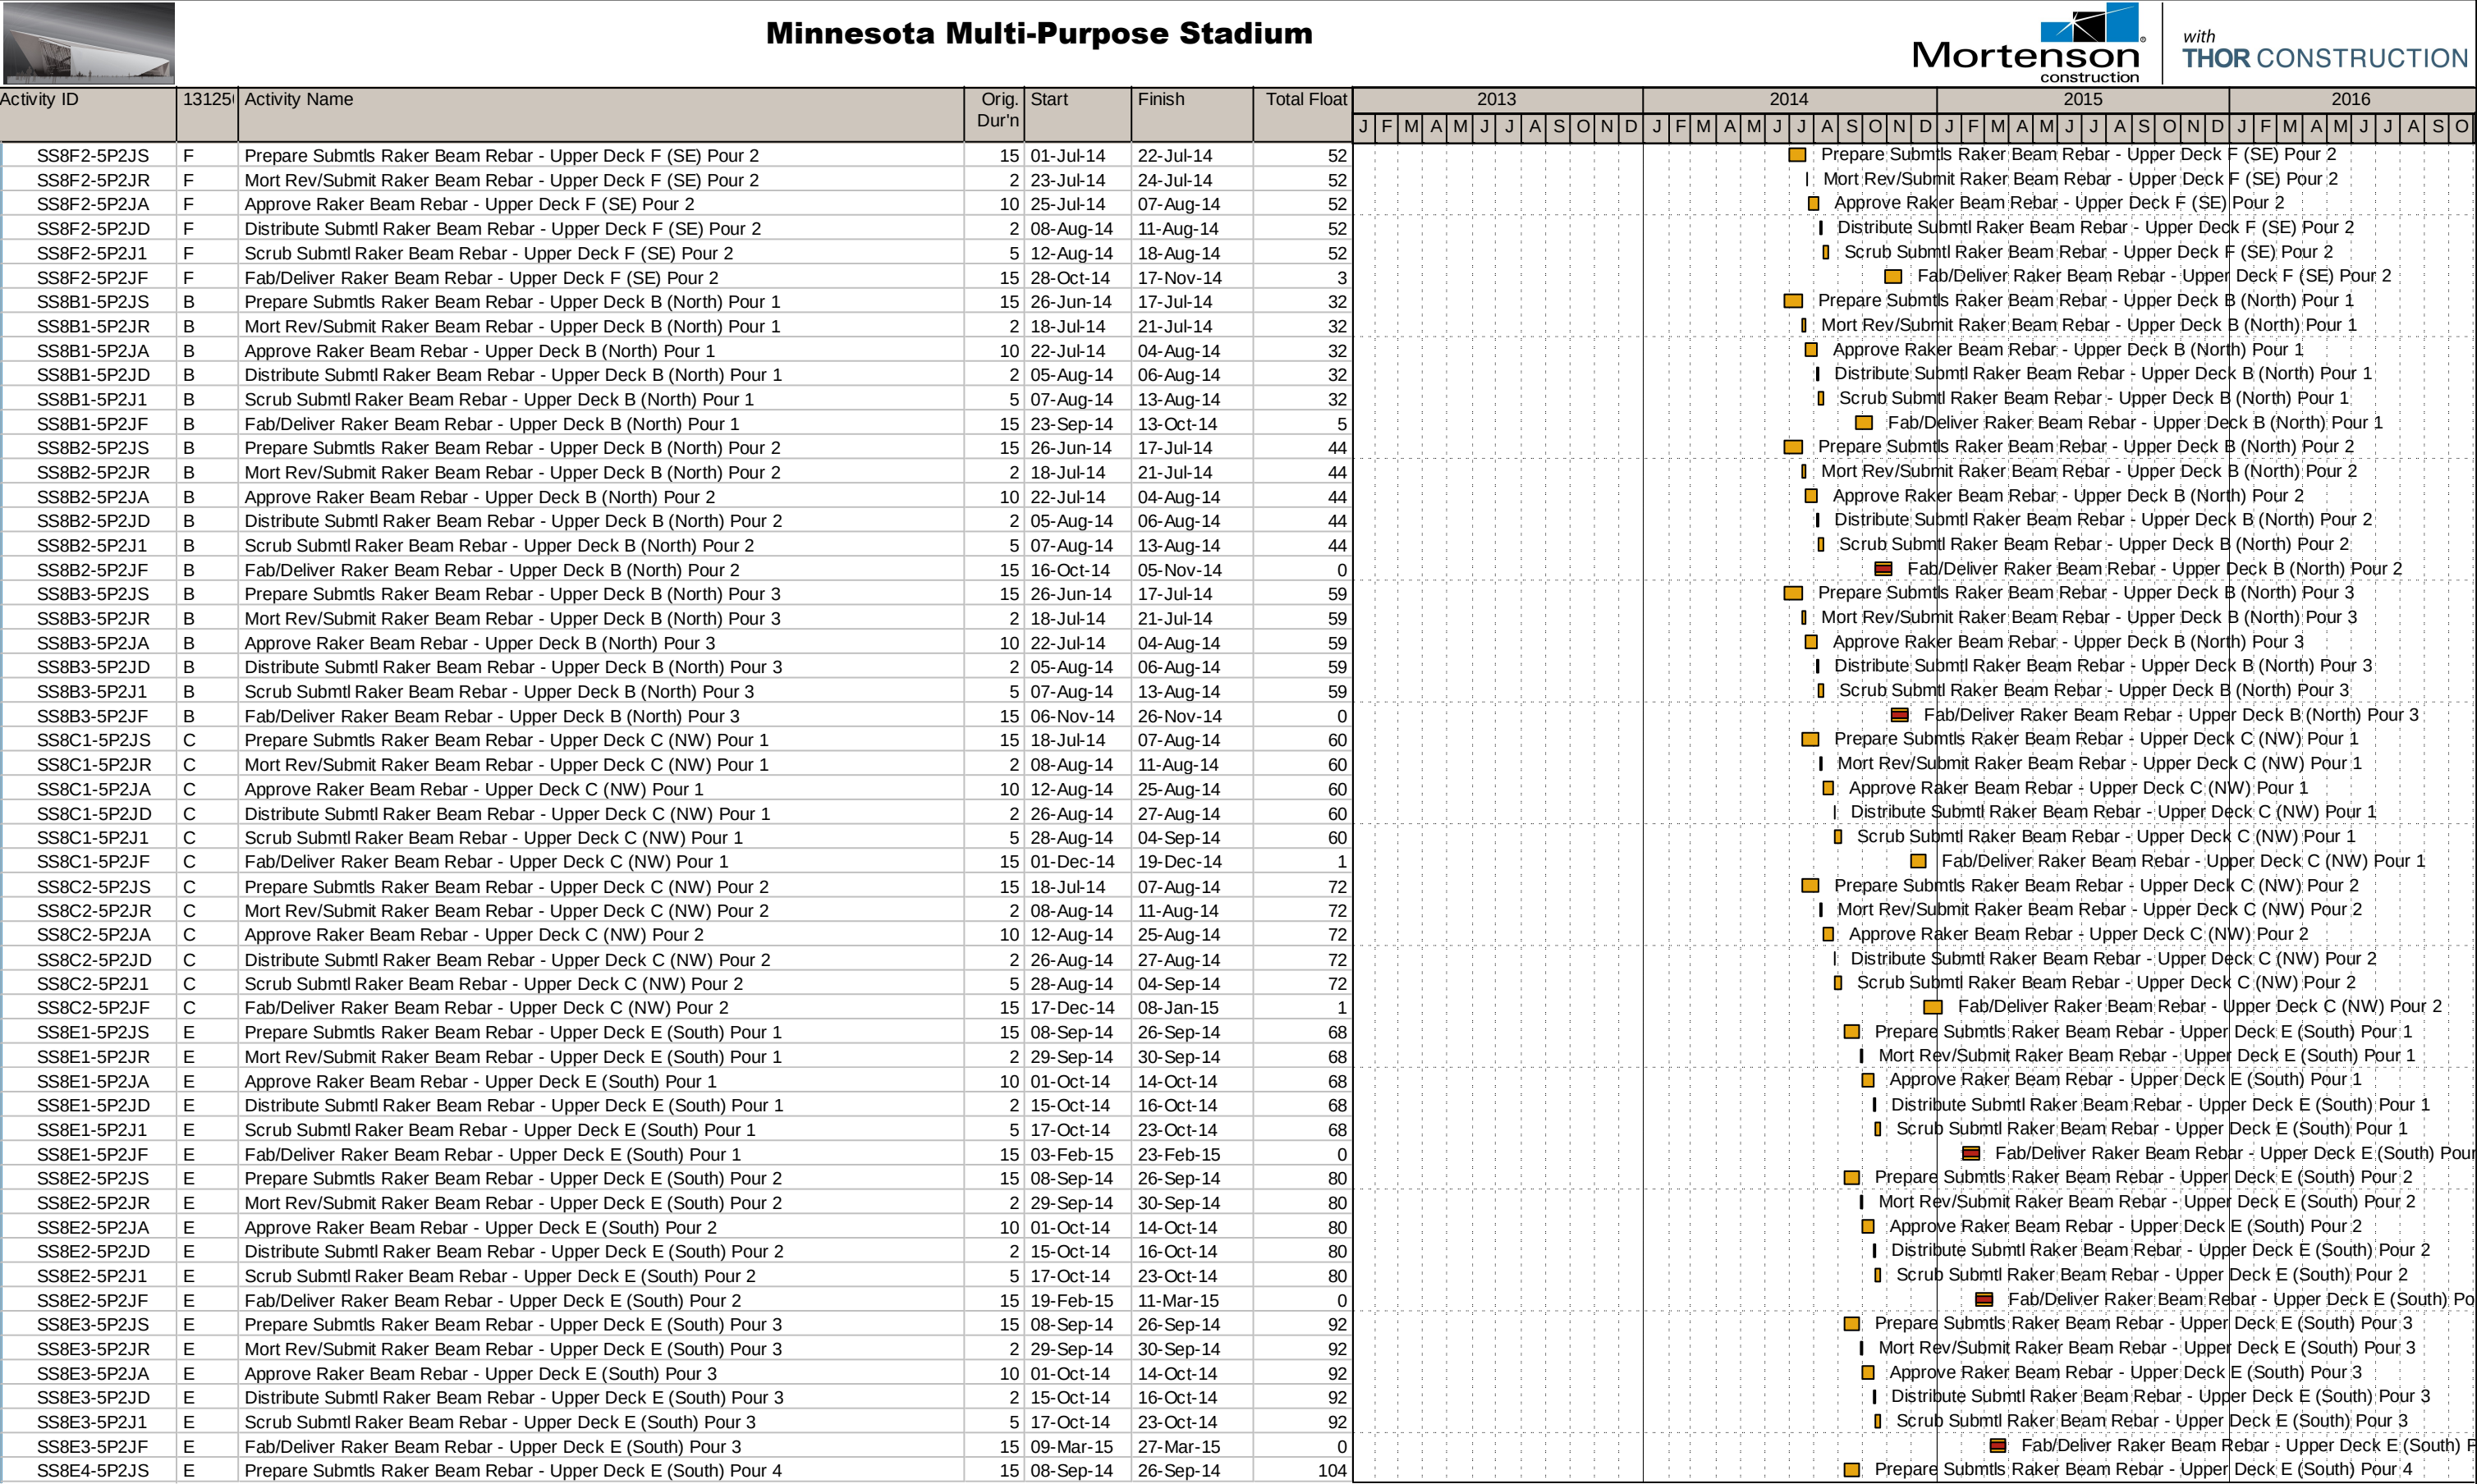



Minnesota Multi-Purpose Stadium

[illegible]

Project Summary

Procurement

Critical Work

Milestone

Temporary Facilities

Actual Work

Pre-Construction

Construction

GMP Schedule

Procurement and Construction

Project ID: 13125001-Current

Layout: MMPS - All Activities

TASK filter: Misc 5.

Start Date 01-Feb-13

Finish Date 23-Dec-16

Page 58 of 85

Run Date 08-Nov-13



Minnesota Multi-Purpose Stadium

[illegible]

Project Summary

Procurement

Critical Work

Milestone

Temporary Facilities

Actual Work

Pre-Construction

Construction

GMP Schedule

Procurement and Construction

Project ID: 13125001-Current

Layout: MMPS - All Activities


TASK filter: Misc 5.


Start Date 01-Feb-13

Finish Date 23-Dec-16


Page 59 of 85

Run Date 08-Nov-13

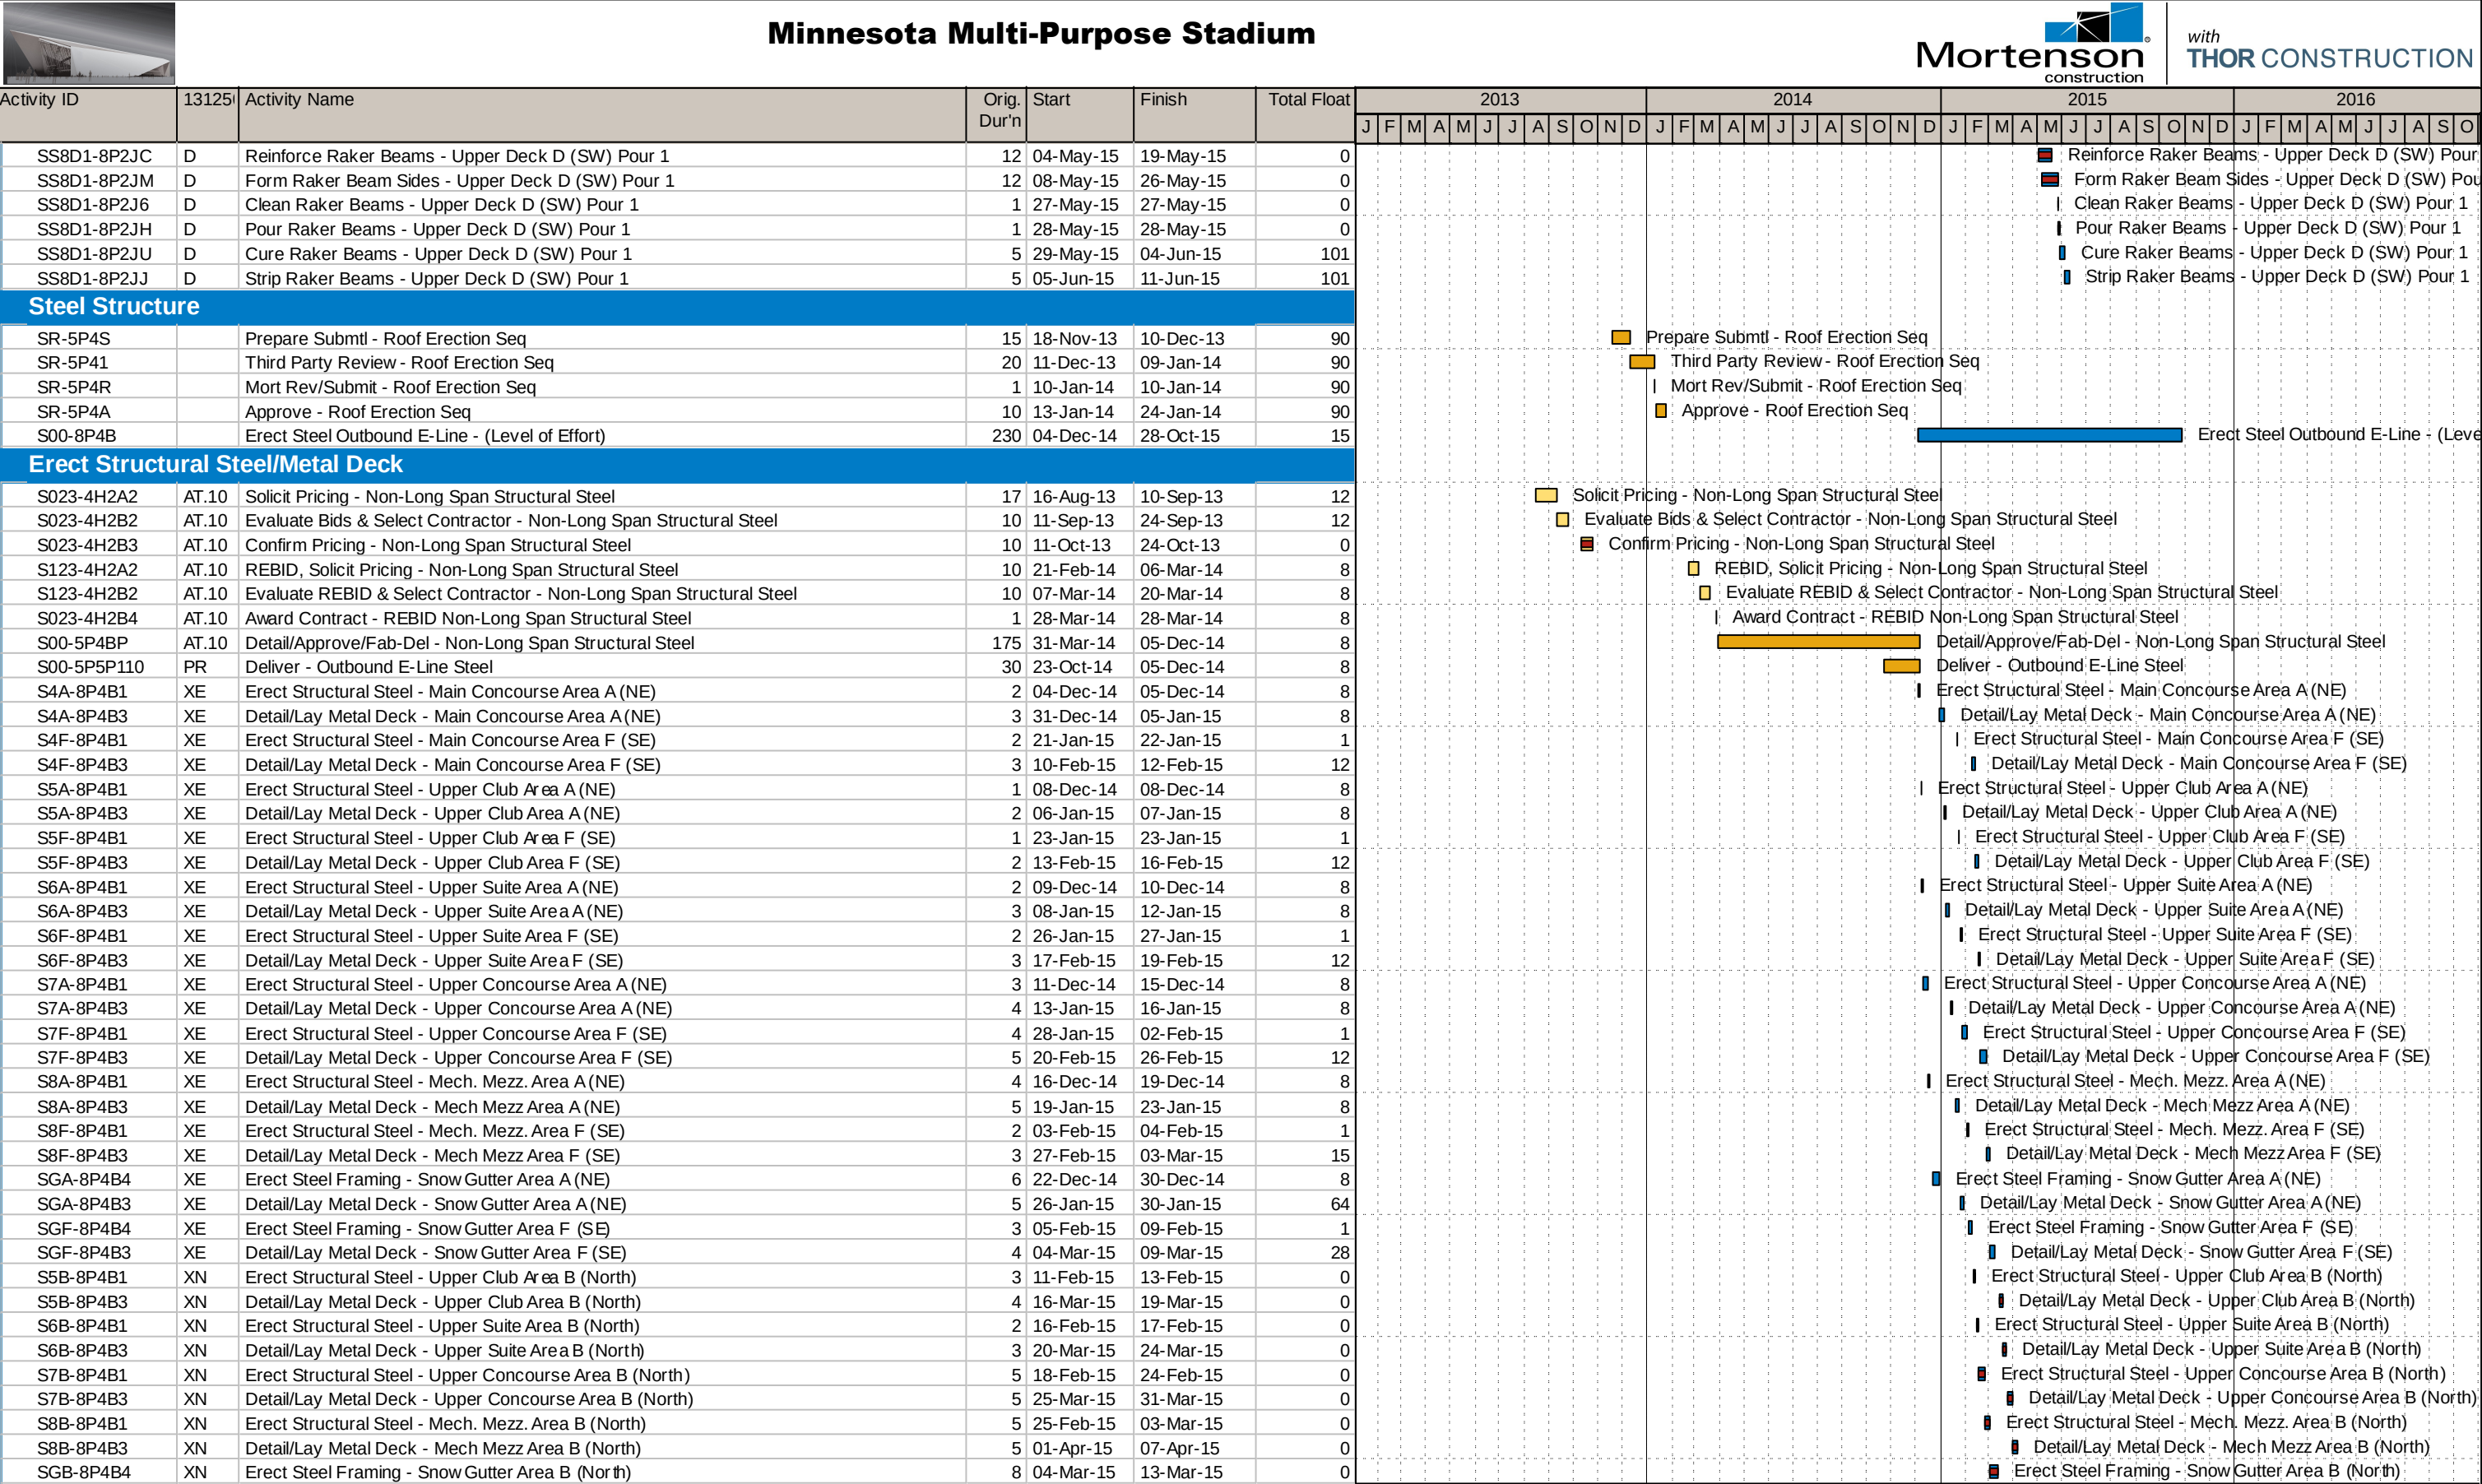

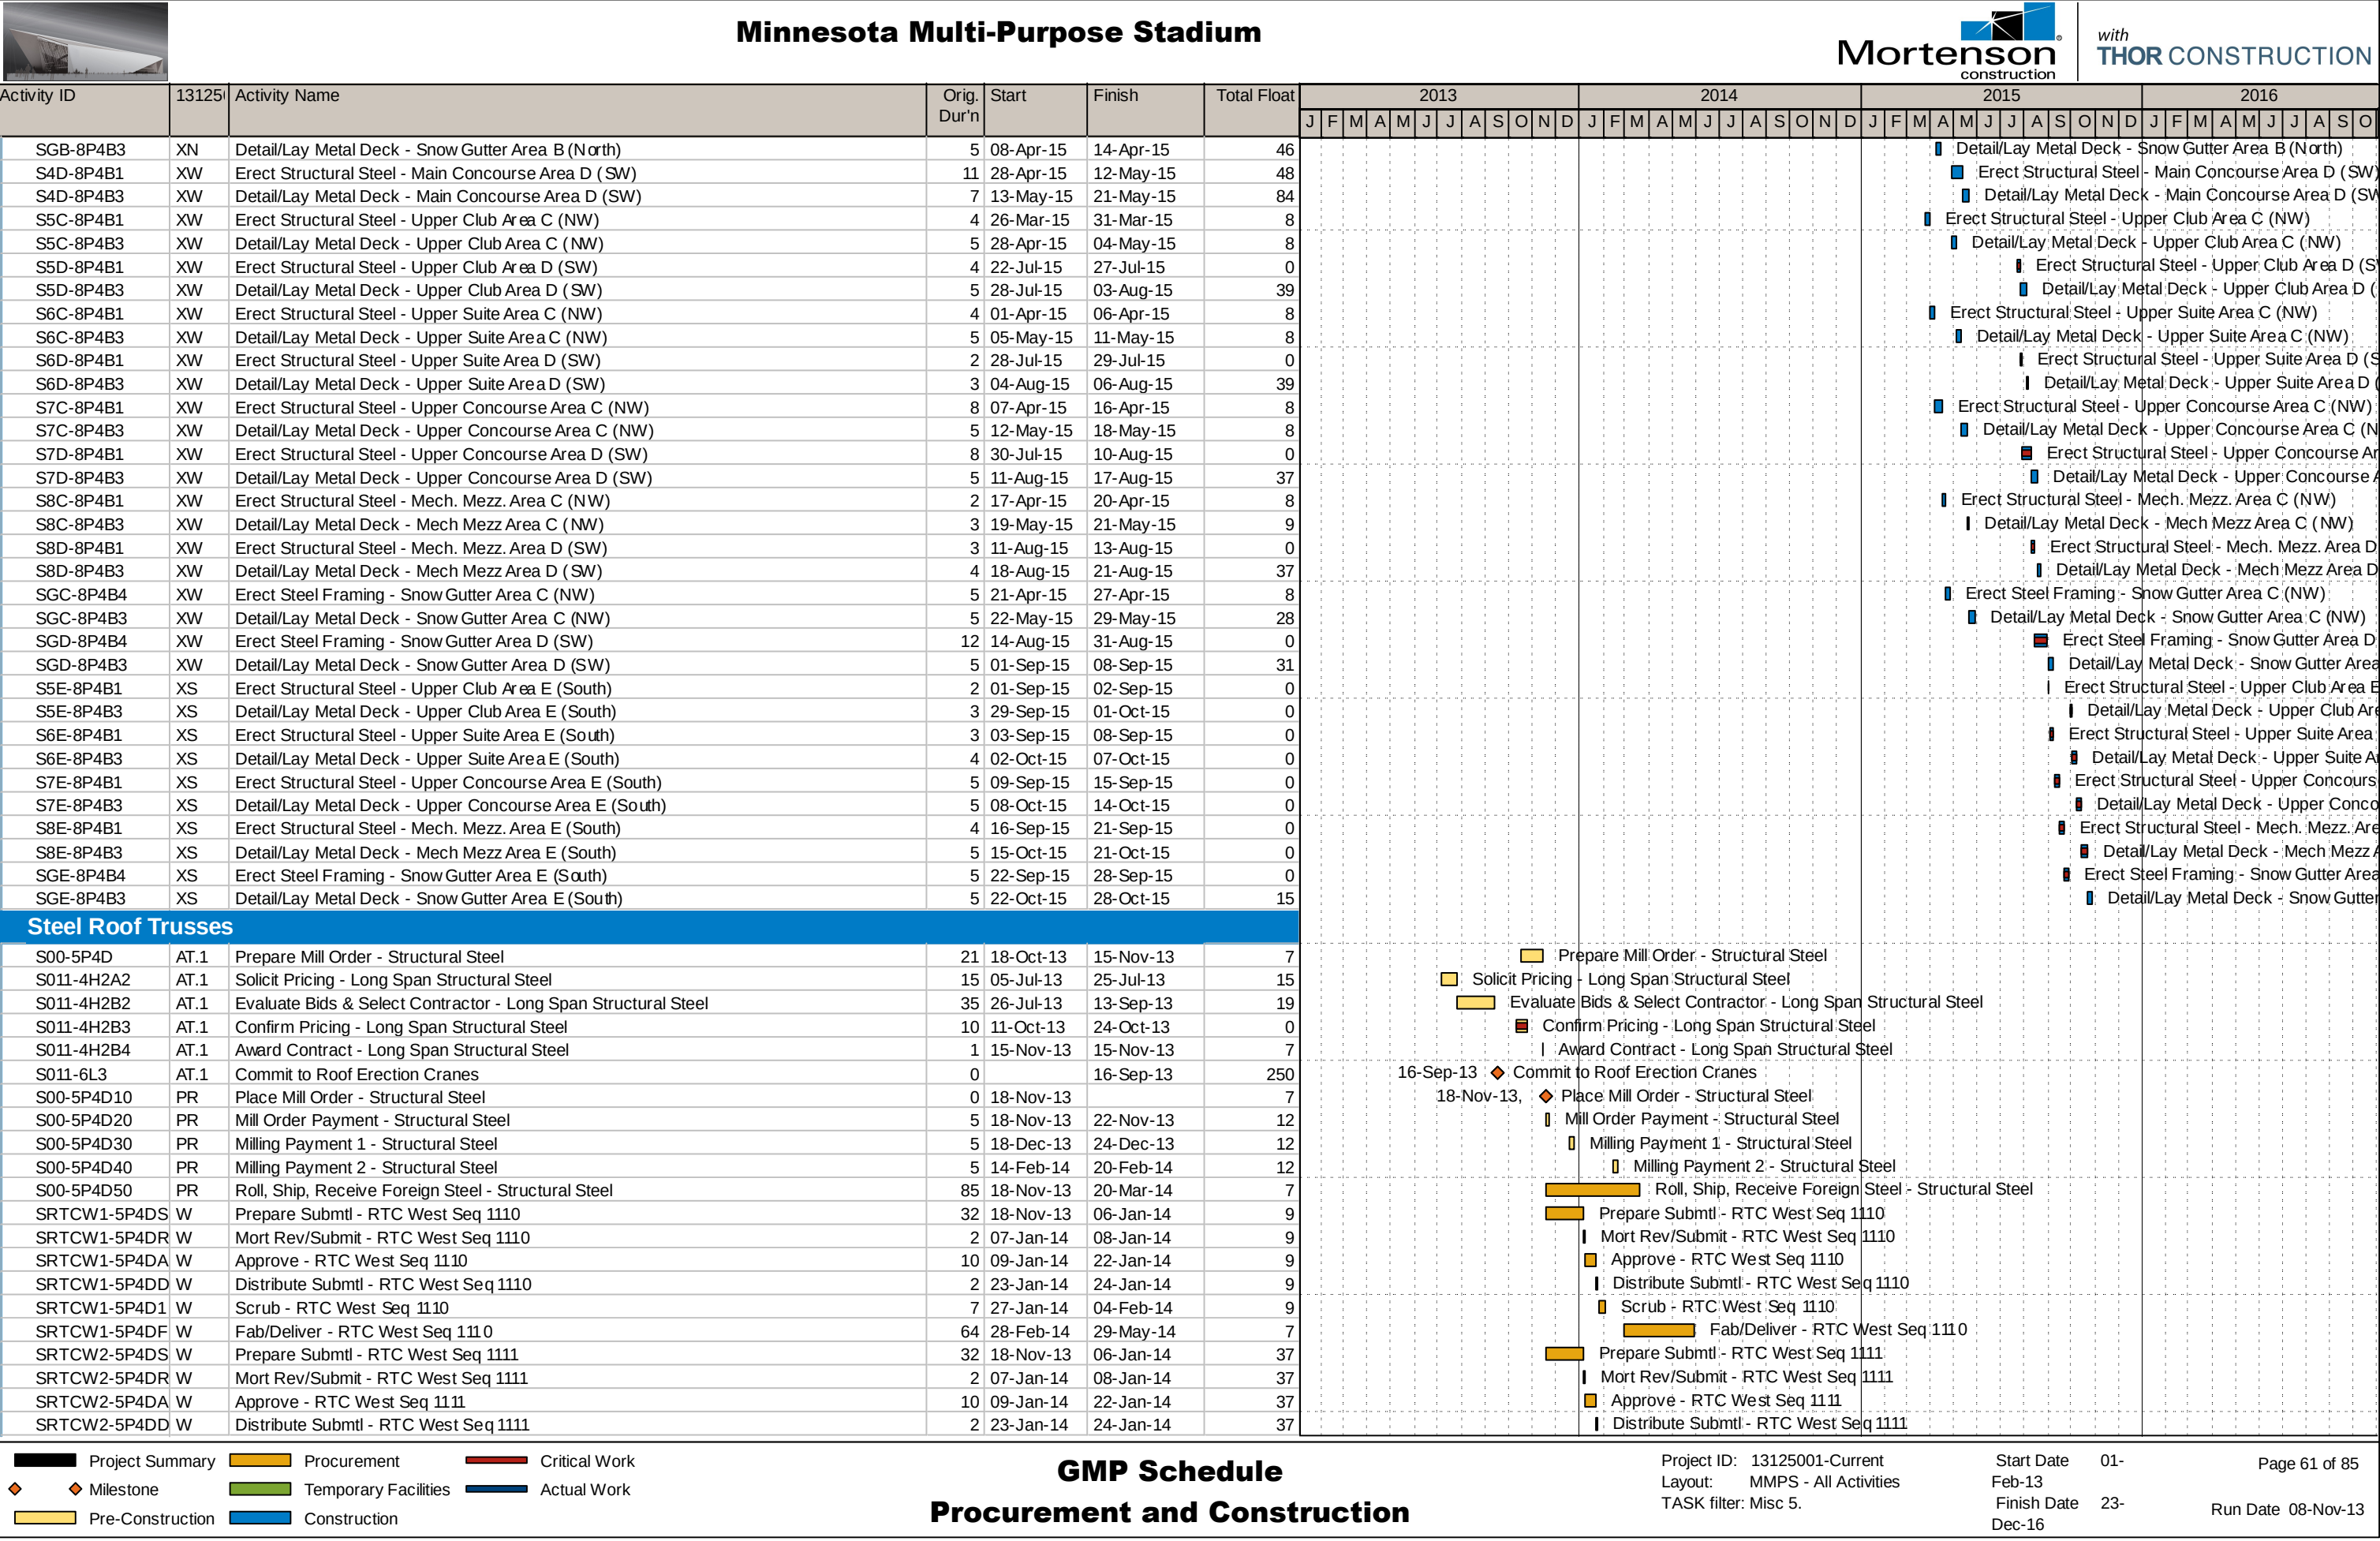

[illegible]

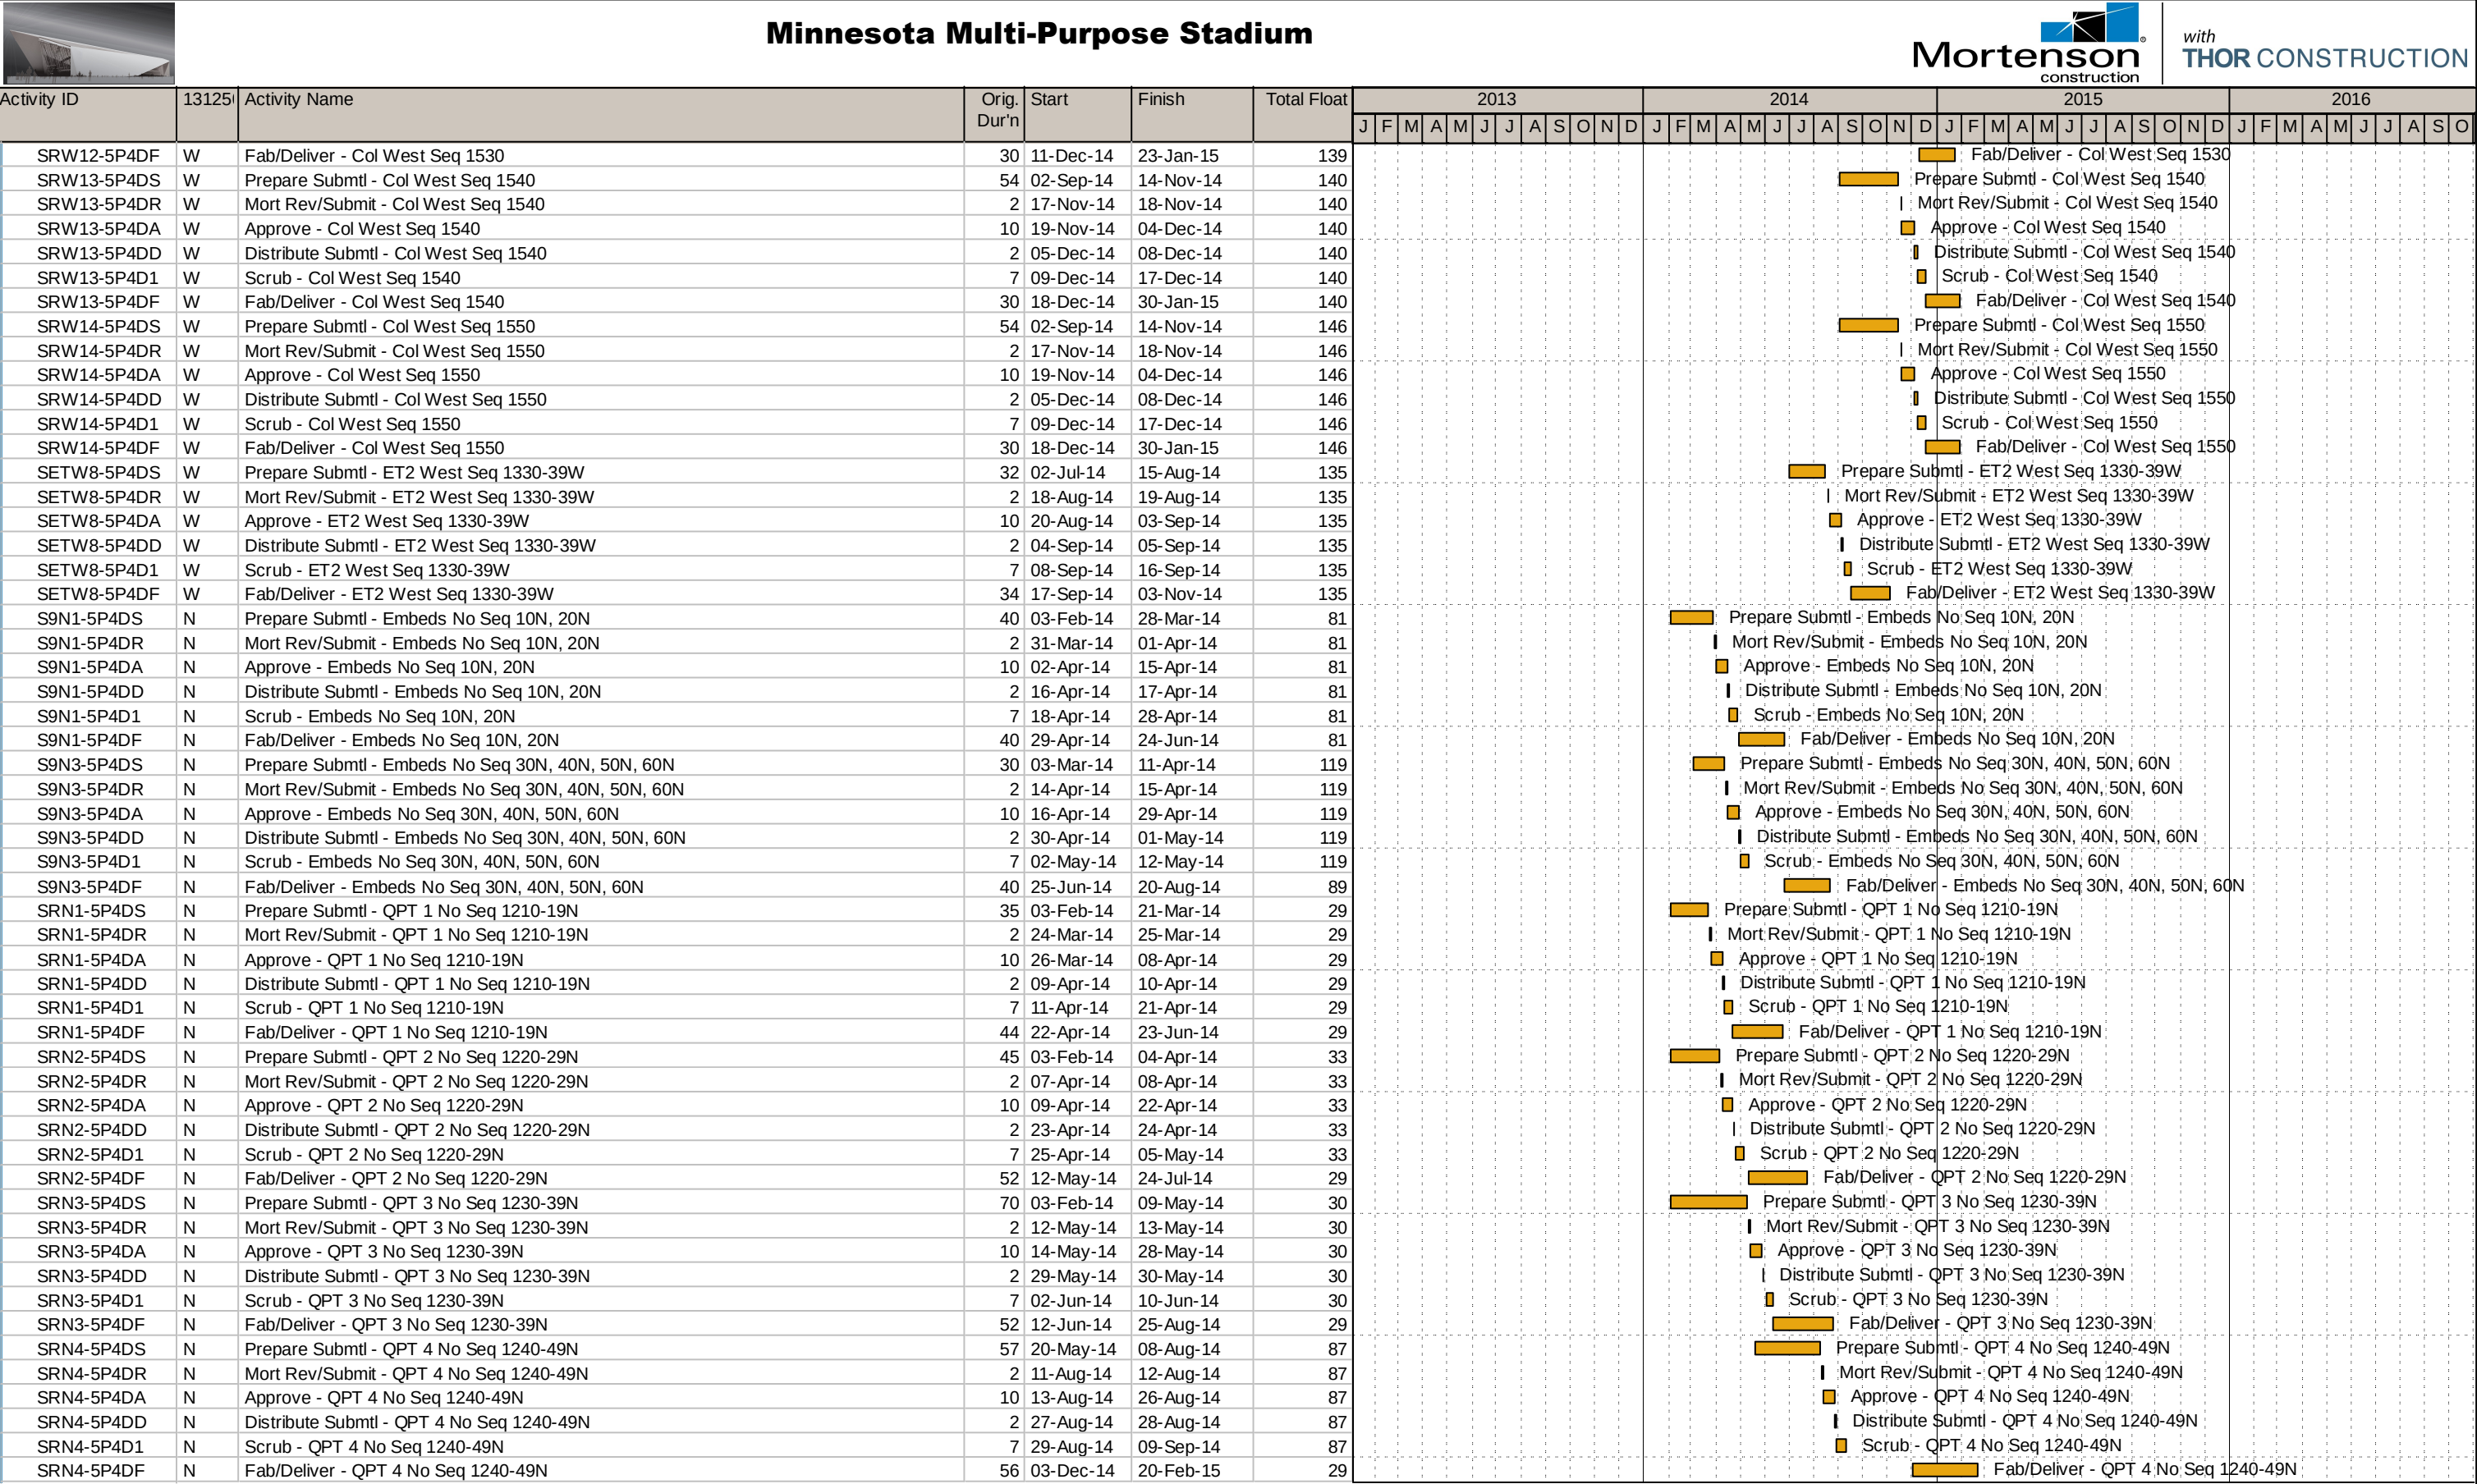



Minnesota Multi-Purpose Stadium

[illegible]

Project Summary
 Procurement
 Critical Work

Milestone
 Temporary Facilities
 Actual Work

Pre-Construction
 Construction

GMP Schedule

Procurement and Construction

Project ID: 13125001-Current
Start Date 01-
Page 64 of 85

Layout: MMPS - All Activities
Feb-13

TASK filter: Misc 5.
Finish Date 23-
Run Date 08-Nov-13

Dec-16



Minnesota Multi-Purpose Stadium

[illegible]

Project Summary

Procurement

Critical Work

Milestone

Temporary Facilities

Actual Work

Pre-Construction

Construction

GMP Schedule

Procurement and Construction

Project ID: 13125001-Current

Layout: MMPS - All Activities

TASK filter: Misc 5.

Start Date 01-Feb-13

Finish Date 23-Dec-16

Page 65 of 85

Run Date 08-Nov-13

[illegible]



Minnesota Multi-Purpose Stadium

[illegible]

 Project Summary
  Procurement
  Critical Work

 Milestone
  Temporary Facilities
  Actual Work

 Pre-Construction
  Construction

GMP Schedule

Procurement and Construction

Project ID: 13125001-Current
Layout: MMPS - All Activities
TASK filter: Misc 5.

Start Date 01-Feb-13 Page 67 of 85
Finish Date 23-Dec-16 Run Date 08-Nov-13



Minnesota Multi-Purpose Stadium

[illegible]

Project Summary

Procurement

Critical Work

Milestone

Temporary Facilities

Actual Work

Pre-Construction

Construction

GMP Schedule

Procurement and Construction

Project ID: 13125001-Current

Layout: MMPS - All Activities


TASK filter: Misc 5.

Start Date 01-Feb-13

Finish Date 23-Dec-16

Run Date 08-Nov-13

Page 68 of 85

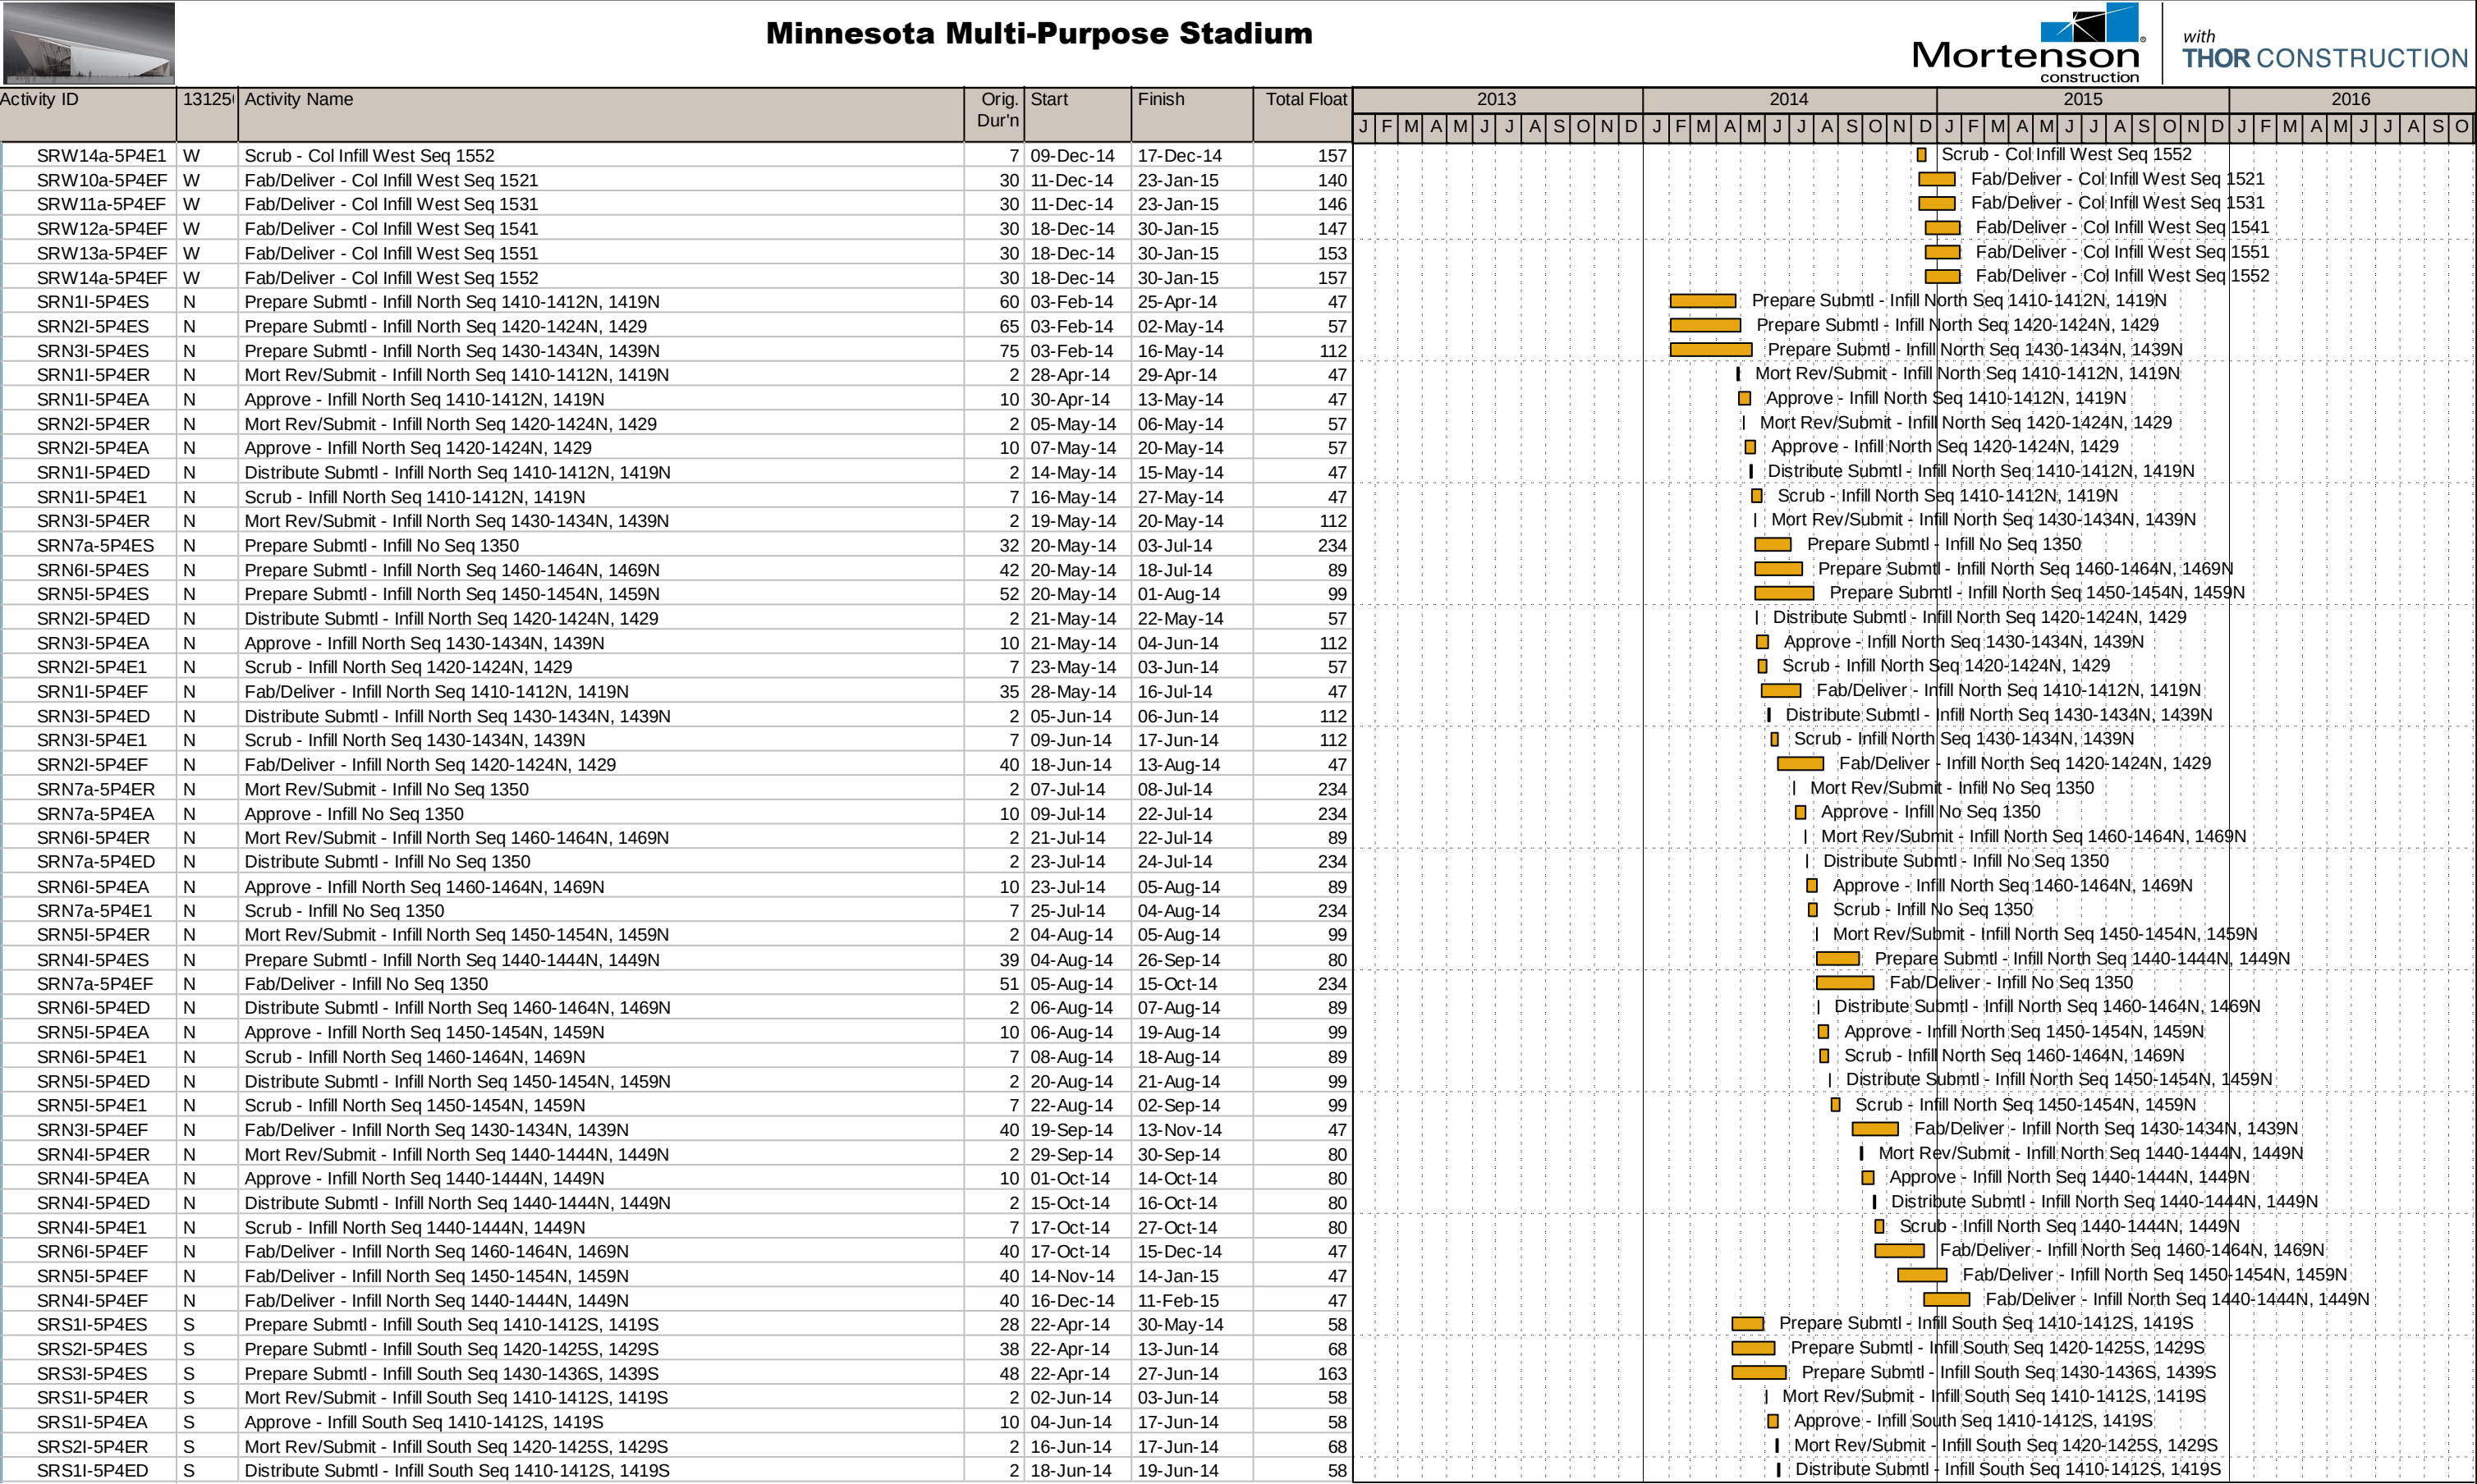



Minnesota Multi-Purpose Stadium

[illegible]

Project Summary

Procurement

Critical Work

Milestone

Temporary Facilities

Actual Work

Pre-Construction

Construction

GMP Schedule

Procurement and Construction

Project ID: 13125001-Current

Layout: MMPS - All Activities

TASK filter: Misc 5.

Start Date 01-Feb-13

Finish Date 23-Dec-16

Page 70 of 85

Run Date 08-Nov-13



Minnesota Multi-Purpose Stadium

[illegible]

Project Summary

Procurement

Critical Work

Temporary Facilities

Actual Work

GMP Schedule

Procurement and Construction

Project ID: 13125001-Current

Layout: MMPS - All Activities

TASK filter: Misc 5.


Start Date 01-Feb-13

Finish Date 23-Dec-16

Page 71 of 85

Run Date 08-Nov-13

[illegible]

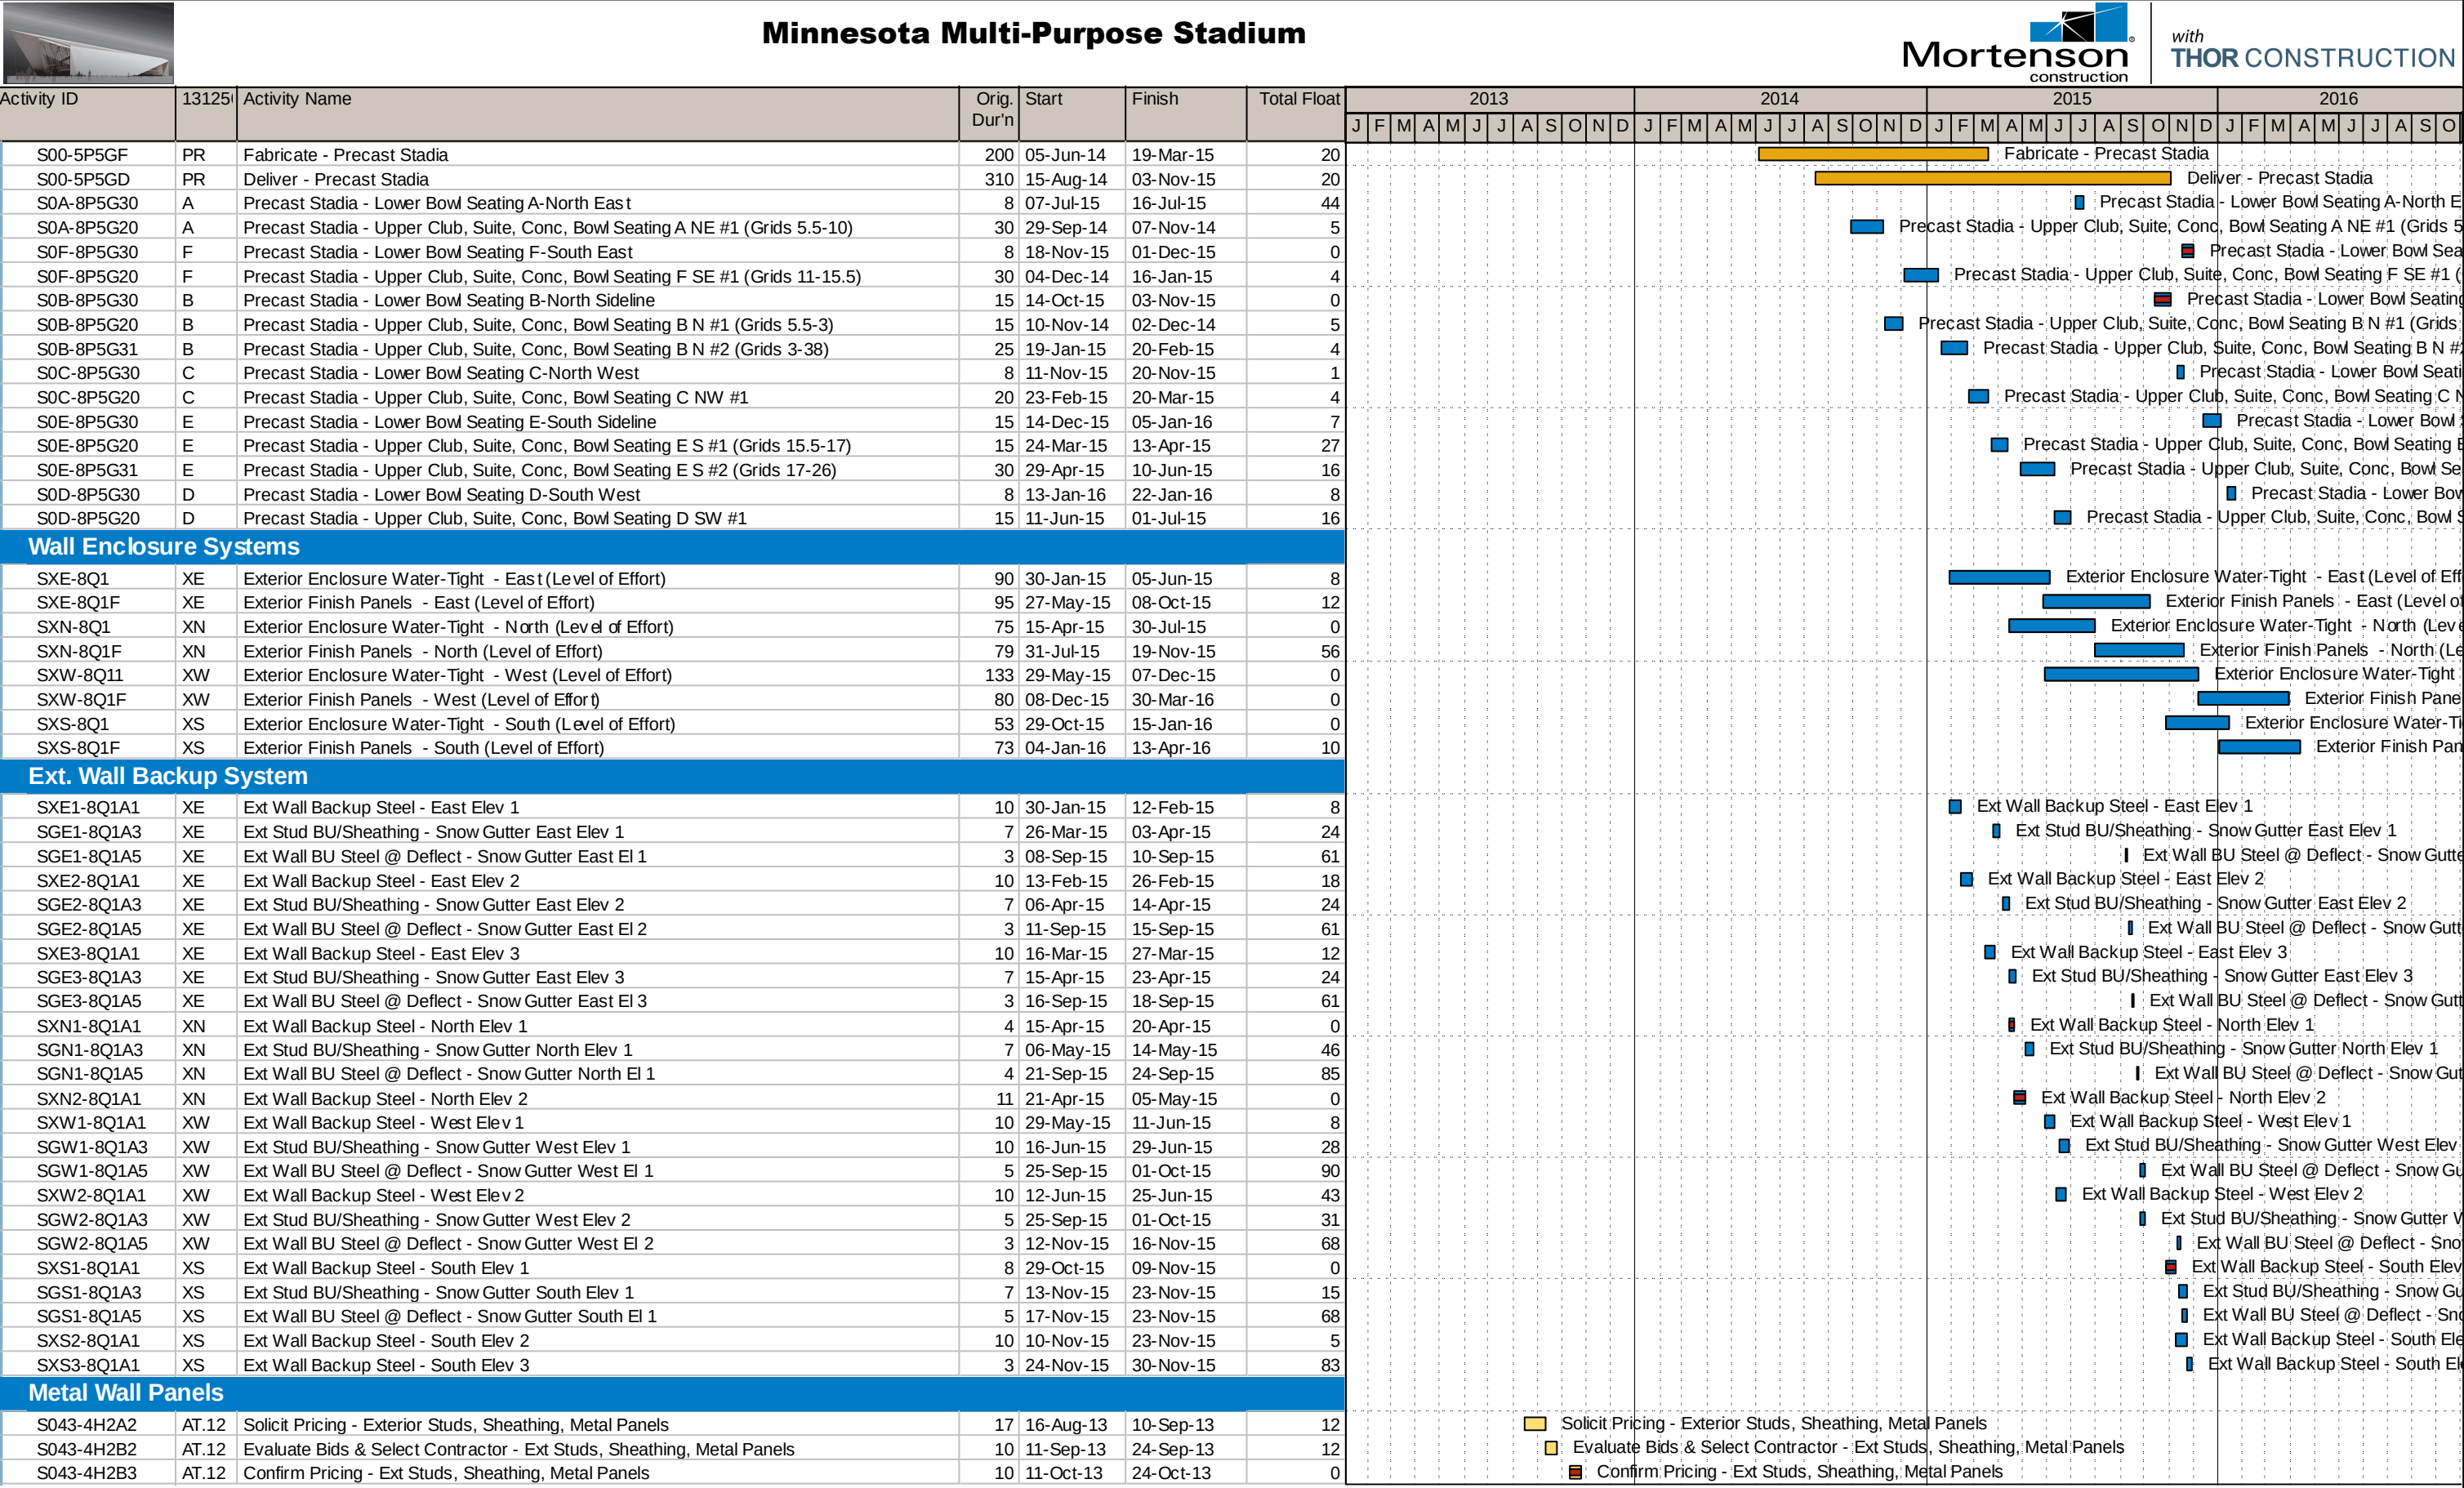



Minnesota Multi-Purpose Stadium

[illegible]

Project Summary

Procurement

Critical Work

Milestone

Temporary Facilities

Actual Work

Pre-Construction

Construction

GMP Schedule

Procurement and Construction

Project ID: 13125001-Current

Layout: MMPS - All Activities


TASK filter: Misc 5.

Start Date 01-Feb-13

Finish Date 23-Dec-16

Page 74 of 85

Run Date 08-Nov-13

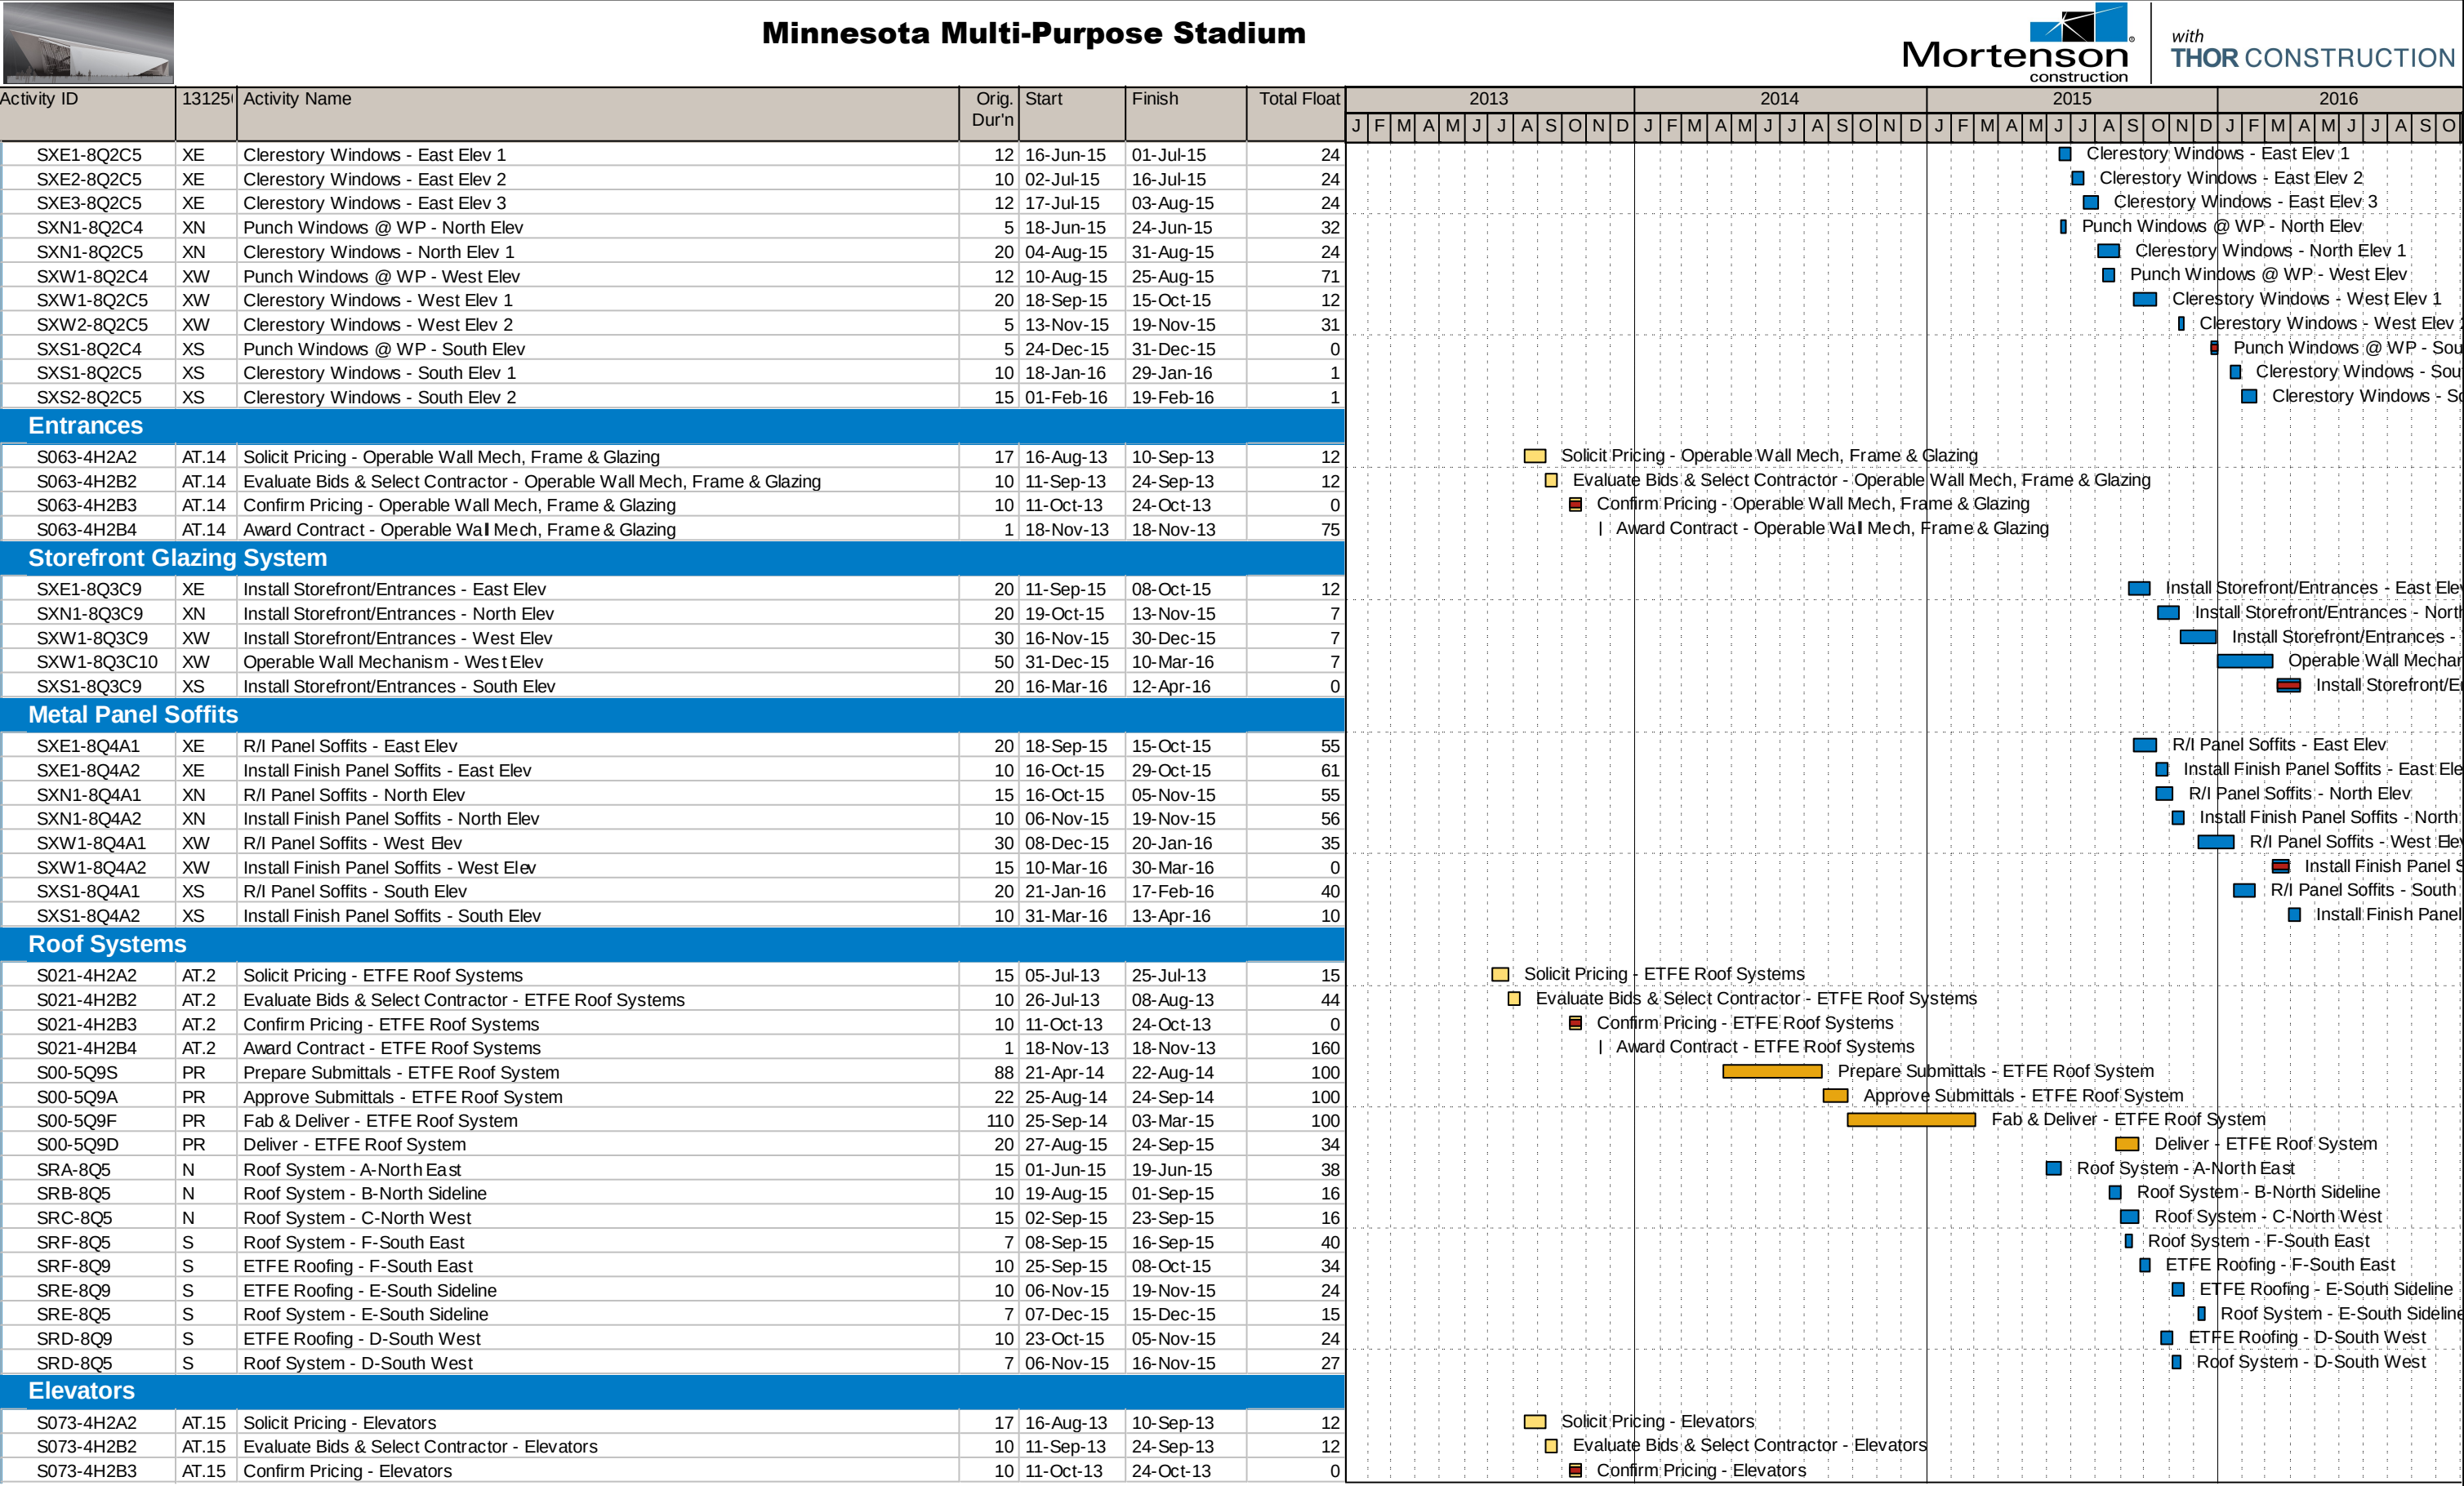



Minnesota Multi-Purpose Stadium

[illegible]

Project Summary
 Procurement
 Critical Work
 Temporary Facilities
 Actual Work

GMP Schedule

Procurement and Construction

Project ID: 13125001-Current

Layout: MMPS - All Activities

TASK filter: Misc 5.

Start Date 01-Feb-13

Finish Date 23-Dec-16

Page 76 of 85

Run Date 08-Nov-13

Milestone
 Temporary Facilities
 Actual Work
 Pre-Construction
 Construction

[illegible]

 Project Summary
  Procurement
  Critical Work

 Milestone
  Temporary Facilities
  Actual Work

 Pre-Construction
  Construction

GMP Schedule

Procurement and Construction

Project ID: 13125001-Current Start Date 01- Page 77 of 85
 Layout: MMPS - All Activities Feb-13
 TASK filter: Misc 5. Finish Date 23- Run Date 08-Nov-13
 Dec-16

[illegible]

 Project Summary
  Procurement
  Critical Work

 Milestone
  Temporary Facilities
  Actual Work

 Pre-Construction
  Construction

GMP Schedule

Procurement and Construction

Project ID: 13125001-Current Start Date 01- Page 78 of 85
 Layout: MMPS - All Activities Feb-13
 TASK filter: Misc 5. Finish Date 23- Run Date 08-Nov-13
 Dec-16



[illegible]



Minnesota Multi-Purpose Stadium

[illegible]

Project Summary

Procurement

Critical Work

Temporary Facilities

Actual Work

GMP Schedule

Procurement and Construction

Project ID: 13125001-Current

Layout: MMPS - All Activities

TASK filter: Misc 5.

Start Date 01-Feb-13

Finish Date 23-Dec-16

Page 81 of 85

Run Date 08-Nov-13



Minnesota Multi-Purpose Stadium

[illegible]

Project Summary

Procurement

Critical Work

Milestone

Temporary Facilities

Actual Work

Pre-Construction

Construction

GMP Schedule

Procurement and Construction

Project ID: 13125001-Current
 Layout: MMPS - All Activities
 TASK filter: Misc 5.

Start Date 01-Feb-13
 Finish Date 23-Dec-16

Page 82 of 85
 Run Date 08-Nov-13



Minnesota Multi-Purpose Stadium

[illegible]

Project Summary

Procurement

Critical Work

Milestone

Temporary Facilities

Actual Work

Pre-Construction

Construction

GMP Schedule

Procurement and Construction

Project ID: 13125001-Current

Layout: MMPS - All Activities

TASK filter: Misc 5.

Start Date 01-Feb-13

Finish Date 23-Dec-16

Page 83 of 85

Run Date 08-Nov-13



Minnesota Multi-Purpose Stadium



Activity ID	131251	Activity Name	Orig. Dur'n	Start	Finish	Total Float	2013												2014												2015												2016											
							J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D
S1-5T2EF		Fab/Deliver Generator - Event	200	13-Jun-14	27-Mar-15	6	Fab/Deliver Generator - Event																																															
Food Service Equipment																																																						
S00-5T7L	PR	Procure - Food Service Equipment	450	21-Jun-13	31-Mar-15	39	Procure - Food Service Equipment																																															
S00-5T7L10	PR	Submit Shop Dwgs- Sleeves, Embeds, Layout - Food Service Eq	60	01-Oct-13	26-Dec-13	64	Submit Shop Dwgs- Sleeves, Embeds, Layout - Food Service Eq																																															
S00-5T7L20	PR	Procure / Fab-Del Range Hoods - Food Service Equipment	250	27-Dec-13	19-Dec-14	64	Procure / Fab-Del Range Hoods - Food Service Equipment																																															
Sports Equipment																																																						
S005-4H2A3	AT	Solicit Pricing - Scoreboards/Ribbon Boards	15	21-Apr-14	09-May-14	43	Solicit Pricing - Scoreboards/Ribbon Boards																																															
S005-4H2B5	AT	Evaluate Bids & Award Contracts - Scoreboards/Ribbon Boards	10	12-May-14	23-May-14	43	Evaluate Bids & Award Contracts - Scoreboards/Ribbon Boards																																															
S00-5T7PS	PR	Prepare Submittals - Scoreboards/Ribbon Boards	66	27-May-14	27-Aug-14	43	Prepare Submittals - Scoreboards/Ribbon Boards																																															
S00-5T7PA	PR	Approve Submittals - Scoreboards/Ribbon Boards	22	28-Aug-14	29-Sep-14	43	Approve Submittals - Scoreboards/Ribbon Boards																																															
S00-5T7PF	PR	Fab & Deliver -Scoreboards/Ribbon Boards	255	30-Sep-14	30-Sep-15	43	Fab & Deliver -Scoreboards/Ribbon Boards																																															
S00-8UC370	SB	Scoreboards/Ribbon Boards	125	16-Nov-15	12-May-16	11	Scoreboards/Ribbon Boards																																															
Drywall and Interior Finishes																																																						
S00-5P5S50	PR	Prepare Submittals - Interior Finishes	120	20-Jun-14	10-Dec-14	1	Prepare Submittals - Interior Finishes																																															
S00-5P5R50	PR	Approve Submittals - Interior Finishes	120	18-Aug-14	06-Feb-15	1	Approve Submittals - Interior Finishes																																															
S00-5P5P50	PR	Fab & Deliver - Interior Finishes	132	20-Oct-14	27-Apr-15	1	Fab & Deliver - Interior Finishes																																															
S1ND-8U	N	Drywall and Interior Finishes - Event North Half (A,B,C) Out Board	64	15-Sep-15	15-Dec-15	24	Drywall and Interior Finishes - Event North Half (A,B,C) Out Board																																															
S1NH-8U	N	Drywall and Interior Finishes - Event North Half (A,B,C) In Board	70	09-Nov-15	18-Feb-16	9	Drywall and Interior Finishes - Event North Half (A,B,C) In Board																																															
S3N-8U	N	Drywall and Interior Finishes - Lower Club North Half (A,B,C)	86	29-Jul-15	30-Nov-15	12	Drywall and Interior Finishes - Lower Club North Half (A,B,C)																																															
S4N-8U	N	Drywall and Interior Finishes - Main Concourse North Half (A,B,C)	96	08-Sep-15	25-Jan-16	16	Drywall and Interior Finishes - Main Concourse North Half (A,B,C)																																															
S5N-8U	N	Drywall and Interior Finishes - Upper Club North Half (A,B,C)	81	11-Nov-15	08-Mar-16	12	Drywall and Interior Finishes - Upper Club North Half (A,B,C)																																															
S6N-8U	N	Drywall and Interior Finishes - Upper Suite North Half (A,B,C)	65	08-Oct-15	12-Jan-16	12	Drywall and Interior Finishes - Upper Suite North Half (A,B,C)																																															
S7N-8U	N	Drywall and Interior Finishes - Upper Concourse North Half (A,B,C)	73	13-Nov-15	29-Feb-16	16	Drywall and Interior Finishes - Upper Concourse North Half (A,B,C)																																															
S8N-8U	N	Drywall and Interior Finishes - Mech. Mezz. North Half (A,B,C)	28	06-Oct-15	12-Nov-15	120	Drywall and Interior Finishes - Mech. Mezz. North Half (A,B,C)																																															
S1SD-8U	S	Drywall and Interior Finishes - Event South Half (D,E,F) Out Board	89	07-Jan-16	10-May-16	1	Drywall and Interior Finishes - Event South Half (D,E,F) Out Board																																															
S1SH-8U	S	Drywall and Interior Finishes - Event South Half (D,E,F) In Board	103	08-Feb-16	30-Jun-16	0	Drywall and Interior Finishes - Event South Half (D,E,F) In Board																																															
S2S-8U	S	Drywall and Interior Finishes - Exec. SuiteSouth Half (D,E,F)	92	18-Jan-16	24-May-16	6	Drywall and Interior Finishes - Exec. SuiteSouth Half (D,E,F)																																															
S3S-8U	S	Drywall and Interior Finishes - Lower Club South Half (D,E,F)	60	03-Feb-16	26-Apr-16	12	Drywall and Interior Finishes - Lower Club South Half (D,E,F)																																															
S4S-8U	S	Drywall and Interior Finishes - Main Concourse South Half (D,E,F)	94	20-Jan-16	31-May-16	0	Drywall and Interior Finishes - Main Concourse South Half (D,E,F)																																															
S5S-8U	S	Drywall and Interior Finishes - Upper Club South Half (D,E,F)	73	03-Mar-16	14-Jun-16	12	Drywall and Interior Finishes - Upper Club South Half (D,E,F)																																															
S6S-8U	S	Drywall and Interior Finishes - Upper Suite South Half (D,E,F)	74	15-Mar-16	27-Jun-16	3	Drywall and Interior Finishes - Upper Suite South Half (D,E,F)																																															
S7S-8U	S	Drywall and Interior Finishes - Upper Concourse South Half (D,E,F)	70	21-Mar-16	27-Jun-16	3	Drywall and Interior Finishes - Upper Concourse South Half (D,E,F)																																															
S8S-8U	S	Drywall and Interior Finishes - Mech. Mezz. South Half (D,E,F)	28	16-Feb-16	24-Mar-16	57	Drywall and Interior Finishes - Mech. Mezz. South Half (D,E,F)																																															
Specialty Flooring																																																						
S00-8UC280	PF	Playing Field	88	16-Feb-16	17-Jun-16	19	Playing Field																																															
Multiple Seating																																																						
S0A-8P5B10	SB	Stadium Seating, Rails, Steps, etc.	163	23-Nov-15	14-Jul-16	1	Stadium Seating, Rails, Steps, etc.																																															
Site Improvements																																																						
S0A-8V	A	Site Improvements - Plaza - NE - Area A	99	30-Oct-15	22-Mar-16	71	Site Improvements - Plaza - NE - Area A																																															
S0F-8V	F	Site Improvements - Plaza - SE - Area F	99	30-Oct-15	22-Mar-16	71	Site Improvements - Plaza - SE - Area F																																															
S0B-8V	B	Site Improvements - Plaza - N - Area B	99	20-Nov-15	12-Apr-16	56	Site Improvements - Plaza - N - Area B																																															
S0C-8V	C	Site Improvements - Plaza - NW - Area C	110	07-Jan-16	09-Jun-16	0	Site Improvements - Plaza - NW - Area C																																															
S0E-8V	E	Site Improvements - Plaza - S - Area E	99	29-Jan-16	16-Jun-16	10	Site Improvements - Plaza - S - Area E																																															
S0D-8V	D	Site Improvements - Plaza - SW - Area D	110	22-Dec-15	25-May-16	25	Site Improvements - Plaza - SW - Area D																																															
S00-8V		Site Improvements - Plaza - All Areas (Level of Effort)	155	30-Oct-15	09-Jun-16	0	Site Improvements - Plaza - All Areas (Level of Effort)																																															
Project Close-Out																																																						
S00-CX	Site	Punchlist - Site Improvements	66	13-Apr-16	15-Jul-16	0	Punchlist - Site Improvements																																															
S10-CX	ALL	Punchlist - Event Level	45	12-May-16	15-Jul-16	0	Punchlist - Event Level																																															
S20-CX	ALL	Punchlist - Exec. Suite	39	14-Apr-16	08-Jun-16	26	Punchlist - Exec. Suite																																															
S30-CX	ALL	Punchlist - Lower Club	33	27-Apr-16	13-Jun-16	23	Punchlist - Lower Club																																															
S40-CX	ALL	Punchlist - Main Concourse	32	01-Jun-16	15-Jul-16	0	Punchlist - Main Concourse																																															
S50-CX	ALL	Punchlist - Club	33	13-May-16	29-Jun-16	11	Punchlist - Club																																															

Project Summary
 Procurement
 Critical Work

Milestone
 Temporary Facilities
 Actual Work

Pre-Construction
 Construction

GMP Schedule

Procurement and Construction

Project ID: 13125001-Current

Layout: MMPS - All Activities

TASK filter: Misc 5.

Start Date 01-Feb-13

Finish Date 23-Dec-16

Page 84 of 85

Run Date 08-Nov-13



Minnesota Multi-Purpose Stadium



with
THOR CONSTRUCTION

[illegible]

 Project Summary
  Procurement
  Critical Work

 Milestone
  Temporary Facilities
  Actual Work

 Pre-Construction
  Construction

GMP Schedule

Procurement and Construction

Project ID: 13125001-Current
Layout: MMPS - All Activities
TASK filter: Misc 5.

Start Date	01-Feb-13	Page 85 of 85
Finish Date	23-Dec-16	Run Date 08-Nov-13
